

DEPARTMENT OF TRANSPORTATION

DIVISION OF ENGINEERING SERVICES

Office of Structural Materials

Quality Assurance and Source Inspection



Bay Area Branch
690 Walnut Ave.St. 150
Vallejo, CA 94592-1133
(707) 649-5453
(707) 649-5493

Contract #: 04-0120F4Cty: SF/ALA Rte: 80 PM: 13.2/13.9File #: 69.28**WELDING INSPECTION REPORT****Resident Engineer:**Pursell, Gary**Address:** 333 Burma Road**City:** Oakland, CA 94607**Report No:** WIR-005427**Date Inspected:** 08-Feb-2009**Project Name:** SAS Superstructure**OSM Arrival Time:** 700**Prime Contractor:** American Bridge/Fluor Enterprises, a JV**OSM Departure Time:** 1900**Contractor:** Zhenhua Port Machinery Company, Ltd (ZPMC), Changxing Island **Location:** Shanghai, China**CWI Name:** Luan Zhao Gang**CWI Present:** Yes No**Inspected CWI report:** Yes No N/A**Rod Oven in Use:** Yes No N/A**Electrode to specification:** Yes No N/A**Weld Procedures Followed:** Yes No N/A**Qualified Welders:** Yes No N/A**Verified Joint Fit-up:** Yes No N/A**Approved Drawings:** Yes No N/A**Approved WPS:** Yes No N/A**Delayed / Cancelled:** Yes No N/A**Bridge No:** 34-0006**Component:** OBG segment**Summary of Items Observed:**

On this day CALTRANS OSM Quality Assurance Inspector (QA) Steve Hall was present during the times noted above for observations relative to the fabrication of the SAS Superstructure being performed by Zhenhua Port Machinery Company (ZPMC) at Changxing Island in Shanghai, China. QA observed and/or found the following:

OBG outside assembly (OBG segment 3AE)

This QA observed ZPMC qualified welding personnel identified as Mr. Jian Cheng Mao (058551) perform FCAW welding on weld joints identified as SEG016A-PP020-257 and 247. ZPMC QC identified as Mr. Wang Wei Ming was present to monitor the welding process. The welding parameters as measured using QC's calibrated instruments appeared to be in general compliance with WPS-B-T-2232-Tc-U5-F.

This QA observed ZPMC qualified welding personnel identified as Mr. Li Yong Shui (067656) perform SMAW welding on weld joints identified as SEG016A-PP020-222, 232, 243 and 253. ZPMC QC identified as Mr. Wang Wei Ming was present to monitor the welding process. The welding parameters as measured using QC's calibrated instruments appeared to be in general compliance with WPS-B-T-2214-Tc-U5b.

This QA observed ZPMC personnel installing tab plates identified on the detail drawings as part number X3P. These tab plates were being bolted into position @ PP022 prior to being welded in place.

OBG outside assembly (OBG segment 3AW)

This QA observed ZPMC personnel preparing this segment to be moved into the blast and paint bay.


WELDING INSPECTION REPORT

(Continued Page 2 of 3)

OBG outside assembly (OBG segment 4AE and 3BE)

No significant work was being performed on these segments while QA was present.

Unless otherwise noted, all work observed on this date appeared to be in general compliance with the applicable contract documents.

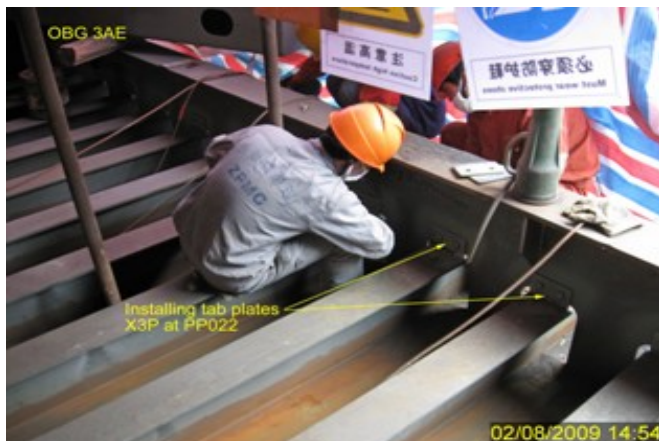

Summary of Conversations:

Only general conversation was held between QA and QC concerning this project.

Comments

This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact Eric Tsang, 15000422372, who represents the Office of Structural Materials for

WELDING INSPECTION REPORT

(Continued Page 3 of 3)

your project.

Inspected By:	Hall,Steven	Quality Assurance Inspector
----------------------	-------------	-----------------------------

Reviewed By:	Carreon,Albert	QA Reviewer
---------------------	----------------	-------------
