

DEPARTMENT OF TRANSPORTATION

DIVISION OF ENGINEERING SERVICES

Office of Structural Materials

Quality Assurance and Source Inspection



Bay Area Branch
690 Walnut Ave. St. 150
Vallejo, CA 94592-1133
(707) 649-5453
(707) 649-5493

Contract #: 04-0120F4Cty: SF/ALA Rte: 80 PM: 13.2/13.9File #: 69.28**WELDING INSPECTION REPORT****Resident Engineer:** Pursell, Gary**Address:** 333 Burma Road**City:** Oakland, CA 94607**Report No:** WIR-016361**Date Inspected:** 14-Aug-2010**Project Name:** SAS Superstructure**OSM Arrival Time:** 700**Prime Contractor:** American Bridge/Fluor Enterprises, a JV**OSM Departure Time:** 1900**Contractor:** Zhenhua Port Machinery Company, Ltd (ZPMC), Changxing Island **Location:** Shanghai, China**CWI Name:** Mr. Qiu Wen**CWI Present:** Yes No**Inspected CWI report:** Yes No N/A**Rod Oven in Use:** Yes No N/A**Electrode to specification:** Yes No N/A**Weld Procedures Followed:** Yes No N/A**Qualified Welders:** Yes No N/A**Verified Joint Fit-up:** Yes No N/A**Approved Drawings:** Yes No N/A**Approved WPS:** Yes No N/A**Delayed / Cancelled:** Yes No N/A**Bridge No:** 34-0006**Component:** Tower**Summary of Items Observed:**

On this day CALTRANS OSM Quality Assurance (QA) Inspector Shailesh Gaikwad was present during the times noted above for observations relative to the fabrication of the SAS Superstructure being performed by Zhenhua Port Machinery Company (ZPMC) at Changxing Island in Shanghai, China. QA observed and/or found the following:

This QA Inspector observed the following work in progress:

BAY 10, SMAW Process:

This QA Inspector observed ZPMC qualified welding personnel identified as 057266, 050289, Perform Shielded Metal Arc Welding (SMAW) on South Tower lift 5 Grillage plate. Joint identified as SSD1-TL5-1B-F-10. ZPMC QC Identified as Li Peng Fei. The welding parameters as measured using QC's calibrated instrument appeared to be in general compliance with WPS-B-T-3213-Tc-U4c.

This QA Inspector observed ZPMC qualified welding personnel identified as 040273, 040582, Perform Shielded Metal Arc Welding (SMAW) on South Tower lift 5 Grillage plate. Joint identified as SSD1-TL5-1B-F-5A. ZPMC QC Identified as Li Peng Fei. The welding parameters as measured using QC's calibrated instrument appeared to be in general compliance with WPS-B-T-3213-Tc-U5b.

This QA Inspector observed ZPMC qualified welding personnel identified as 066236, 066261, 066471, 066422, Perform Shielded Metal Arc Welding (SMAW) on North Tower lift 5 Grillage plate. Joint identified as NSD1-TL5-3E-F-16A, 10B. ZPMC QC Identified as Li Peng Fei. The welding parameters as measured using QC's calibrated instrument appeared to be in general compliance with WPS-B-T-3213-Tc-U5b.

WELDING INSPECTION REPORT

(Continued Page 2 of 3)

This QA Inspector observed ZPMC qualified welding personnel identified as 068091, 037932, 067611, Perform Shielded Metal Arc Welding (SMAW) on North Tower lift 5 Grillage plate. Joint identified as NSD1-TL5-3B-F-80. ZPMC QC Identified as Li Peng Fei. The welding parameters as measured using QC's calibrated instrument appeared to be in general compliance with WPS-B-T-3213-Tc-U5b.

This QA Inspector observed ZPMC qualified welding personnel identified as 066038, 066326, 066002, 066179, Perform Shielded Metal Arc Welding (SMAW) on North Tower lift 5 Grillage plate. Joint identified as NSD1-TL5-3F-F-20A, 17B. ZPMC QC Identified as Li Peng Fei. The welding parameters as measured using QC's calibrated instrument appeared to be in general compliance with WPS-B-T-3213-Tc-U5b.

This QA Inspector observed ZPMC qualified welding personnel identified as 050038, Perform Shielded Metal Arc Welding (SMAW) on South Tower lift 4 Skin A Pad eye, Joint identified as SSD1-FASA4-1A/E-37, 38, 39, 40, 29, 30, 31, 32. ZPMC QC Identified as Yuan Hai Gang. The welding parameters as measured using QC's calibrated instrument appeared to be in general compliance with WPS-B-P-2112, and WPS-B-P-2113. For more information see below attached picture number 1.

BAY 11: SMAW Process.

This QA Inspector observed ZPMC qualified welding personnel identified as 046709, 046769, 040610, 040611, 040655 Perform Shielded Metal Arc Welding (SMAW) on East Tower lift 5 Grillage plate, Joint identified as ESD1-TL5-2B-F-10, 41, 42. ZPMC QC Identified as Xu Jie. The welding parameters as measured using QC's calibrated instrument appeared to be in general compliance with WPS-B-T-3313-Tc-P5.

This QA Inspector observed ZPMC qualified welding personnel identified as 044541 Perform Shielded Metal Arc Welding (SMAW) on East Tower lift 5 Grillage plate, Joint identified as ESD1-TL5-2B-F-5B. ZPMC QC Identified as Xu Jie. The welding parameters as measured using QC's calibrated instrument appeared to be in general compliance with WPS-B-T-3213-Tc-U5b.

This QA Inspector observed ZPMC qualified welding personnel identified as 066758, 037997, 066163 Perform Shielded Metal Arc Welding (SMAW) on West Tower lift 5 Grillage plate, Joint identified as WSD1-TL5-4B-F-35, 36. ZPMC QC Identified as Xu Jie. The welding parameters as measured using QC's calibrated instrument appeared to be in general compliance with WPS-B-T-3313-Tc-P5.

This QA Inspector observed ZPMC qualified welding personnel identified as 067993, 066674, Perform Shielded Metal Arc Welding (SMAW) on West Tower lift 5 Grillage plate, Joint identified as WSD1-TL5-4B-F-16B, 16A. ZPMC QC Identified as Xu Jie. The welding parameters as measured using QC's calibrated instrument appeared to be in general compliance with WPS-B-T-3213-Tc-U5b.

SMAW process Repair welding:

This QA Inspector observed ZPMC qualified welding personnel identified as 058026, Perform Shielded Metal Arc Welding (SMAW) on Interior splice plate. Joint identified as ESD1-SPSA5-7-2A/B. ZPMC QC Identified as Liu Dao Feng with temporary welding repair report. The welding parameters as measured using QC's calibrated instrument appeared to be in general compliance with WPS-485-SMAW-2G (2F) Repair. For more information see below attached picture number 2.


WELDING INSPECTION REPORT

(Continued Page 3 of 3)

BAY 11 Magnetic Particle Testing:

This QA Inspector observed ZPMC Magnetic Particle Testing Inspector performed MT on Tower Strut. Item identified as WD1-STSA4-5-123M-1. For more information see below attached picture number 3.

Unless otherwise noted, all work observed on this date appeared to be in general compliance with the applicable contract documents.

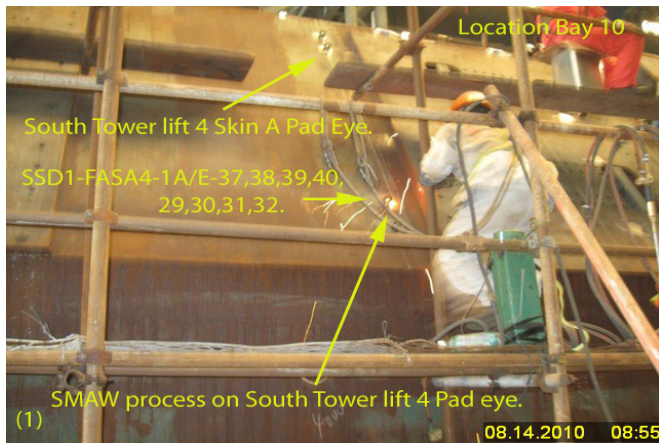

Summary of Conversations:

Only general conversation was held between QA and QC concerning this project.

Comments

This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact Michael Ng Phone: 15921845703, who represents the Office of Structural Materials for your project.

Inspected By: Gaikwad,Shailesh

Quality Assurance Inspector

Reviewed By: Clifford,William

QA Reviewer
