

**DEPARTMENT OF TRANSPORTATION**

DIVISION OF ENGINEERING SERVICES

Office of Structural Materials

Quality Assurance and Source Inspection



Bay Area Branch  
690 Walnut Ave.St. 150  
Vallejo, CA 94592-1133  
(707) 649-5453  
(707) 649-5493

Contract #: 04-0120F4Cty: SF/ALA Rte: 80 PM: 13.2/13.9File #: 69.28**WELDING INSPECTION REPORT****Resident Engineer:**Siegenthaler, Peter**Address:** 333 Burma Road**City:** Oakland, CA 94607**Report No:** WIR-025650**Date Inspected:** 26-Jul-2011**Project Name:** SAS Superstructure**OSM Arrival Time:** 1900**Prime Contractor:** American Bridge/Fluor Enterprises, a JV**OSM Departure Time:** 700**Contractor:** Zhenhua Port Machinery Company, Ltd (ZPMC), Changxing Island **Location:** Shanghai, China

<b>CWI Name:</b>	N/A	<b>CWI Present:</b>	Yes	No			
<b>Inspected CWI report:</b>	Yes	No	N/A	<b>Rod Oven in Use:</b>	Yes	No	N/A
<b>Electrode to specification:</b>	Yes	No	N/A	<b>Weld Procedures Followed:</b>	Yes	No	N/A
<b>Qualified Welders:</b>	Yes	No	N/A	<b>Verified Joint Fit-up:</b>	Yes	No	N/A
<b>Approved Drawings:</b>	Yes	No	N/A	<b>Approved WPS:</b>	Yes	No	N/A
				<b>Delayed / Cancelled:</b>	Yes	No	N/A
<b>Bridge No:</b>	34-0006	<b>Component:</b>	OBG				

**Summary of Items Observed:**

On this date CALTRANS OSM Quality Assurance (QA) Inspector, Mr. Paul Dawson, arrived on site at the Zhenhua Port Machinery Company (ZPMC) facility at Changxing Island, in Shanghai China, for the purpose of monitoring welding and fabrication of the San Francisco / Oakland Bay Bridge (SFOBB) components. This QA Inspector observed the following:



Caltrans and ABF have agreed to conduct visual and magnetic particle inspections (MT) of segment 13 West welds as part of a special inspection program, reference NWIT #09815. This QA Inspector observed ABF Inspectors had completed and accepted MT inspections of welds: SEG3013V-128, 129, 130, 131, 132, 133, 134, 135, 137, 138, 139, 140, 141, 142, 144, 145, 146, 147, 148, 149, 150, 151, 152, 153, 154, 155, 156, 157, 158, 159, 160, 161, 163 and 164. ABF initially rejected and later accepted weld SEG3013V-157 after ZPMC workers performed grinding and welding of this weld. This QA Inspector performed random visual and magnetic particle inspection of welds: SEG3013V-128, 129, 130, 131, 132, 133, 134, 135, 137, 138, 148, 149, 150, 151, 152, 153, 154, 155, 157, 158, 159, 160, 161, 163, 164 and these welds appear to comply with AWS D1.5 MT and visual requirements. For additional information on these inspections see this QA Inspector's TL6028 Magnetic Particle Test Report and the photographs below for additional information

---

# WELDING INSPECTION REPORT

( Continued Page 2 of 2 )

---

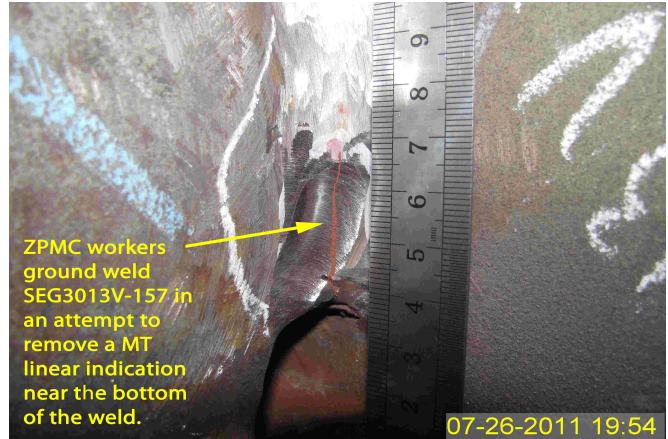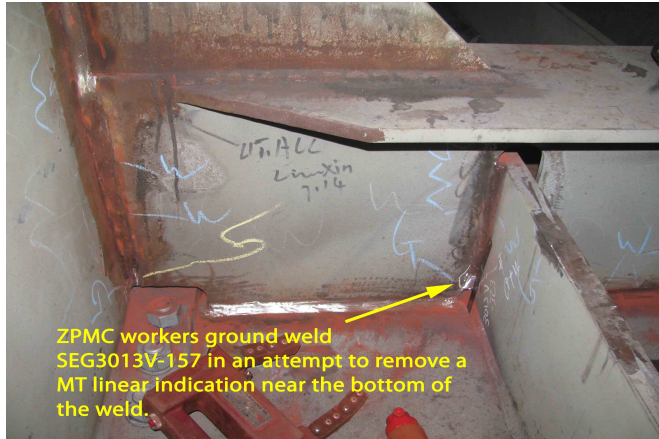

## Summary of Conversations:

See Above.

## Comments

This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact Eric Tsang phone: 150-0042-2372 , who represents the Office of Structural Materials for your project.

---

**Inspected By:** Dawson,Paul

Quality Assurance Inspector

---

**Reviewed By:** Riley,Ken

QA Reviewer
