

DEPARTMENT OF TRANSPORTATION

DIVISION OF ENGINEERING SERVICES

Office of Structural Materials

Quality Assurance and Source Inspection



Bay Area Branch
690 Walnut Ave.St. 150
Vallejo, CA 94592-1133
(707) 649-5453
(707) 649-5493

Contract #: 04-0120F4Cty: SF/ALA Rte: 80 PM: 13.2/13.9File #: 1.28**WELDING INSPECTION REPORT****Resident Engineer:**Siegenthaler, Peter**Address:** 333 Burma Road**City:** Oakland, CA 94607**Report No:** WIR-026126**Date Inspected:** 19-Aug-2011**Project Name:** SAS Superstructure**OSM Arrival Time:** 700**Prime Contractor:** American Bridge/Fluor Enterprises, a JV**OSM Departure Time:** 1530**Contractor:** American Bridge/Fluor Enterprises, a JV**Location:** Job Site**CWI Name:** William Sherwood**CWI Present:** Yes No**Inspected CWI report:** Yes No N/A**Rod Oven in Use:** Yes No N/A**Electrode to specification:** Yes No N/A**Weld Procedures Followed:** Yes No N/A**Qualified Welders:** Yes No N/A**Verified Joint Fit-up:** Yes No N/A**Approved Drawings:** Yes No N/A**Approved WPS:** Yes No N/A**Delayed / Cancelled:** Yes No N/A**Bridge No:** 34-0006**Component:** OBG Components**Summary of Items Observed:**

Quality Assurance Inspector (QA) William Clifford was at the American Bridge/Fluor (ABF) job site at Yerba Buena Island in California between the times noted above in order to monitor Quality Control functions and the in process work being performed by ABF personnel. The following items were observed:

This QA randomly observed ABF/JV qualified welder Wai Kt Li #2953 performing Shielded Metal Arc Welding (SMAW) with 1/8" diameter E7018H4R electrode and implementing Caltrans approved Welding Procedure Specification (WPS) ABF-WPS-D15-1000-R. . The joint being welded was in the 3G vertical position at the side plate C1/C2 on the inside of the OBG 11E/12E.

C2 – Y=1550, D=14, W=20, L=70

C1 – Y=1920, D=15, W=22, L=160

C1 – Y=3503, D=11, W=25, L=80

C1 – Y=4830, D=11, W=26, L=180

C1 – Y=5150, D=10, W=15, L=90

During welding, ABF Quality Control (QC) William Sherwood was noted monitoring the welding parameters. Welding parameters were recorded as (A=128).



Approximately 7:45 this QA randomly observed ABF/JV qualified welder Jorge Lopez #6149 performing fit up of Complete Joint Penetration (CJP) for Shielded Metal Arc Welding (SMAW) with 5/32" diameter E7018H4R electrode and implementing Caltrans approved Welding Procedure Specification (WPS) ABF-WPS-D15-1050A-CU. The joint being welded was a 14mm plate insert at the "A" deck to close the lifting

WELDING INSPECTION REPORT

(Continued Page 2 of 2)

lug deck penetration holes. This work was located at E4-PP101-L#3 and was performed in the flat position from the top side of the "A" deck.

Unless otherwise noted, all work observed on this date appeared to generally comply with applicable contract documents.

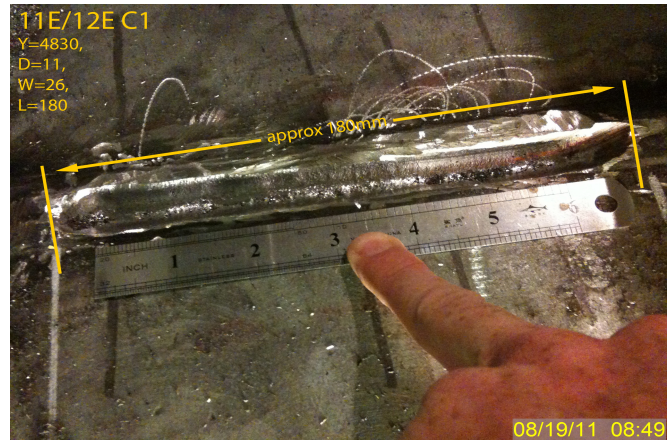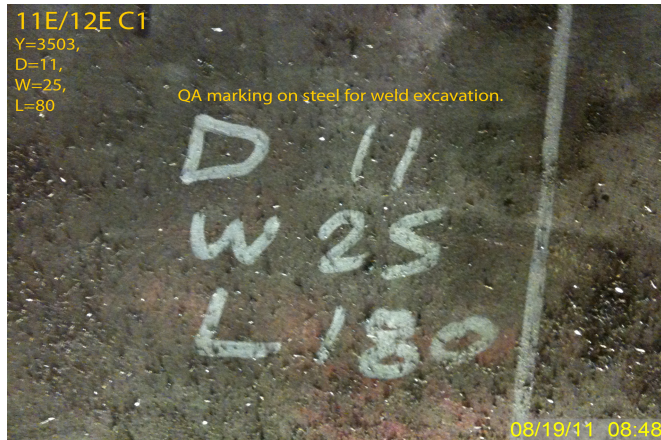

Summary of Conversations:

No relevant conversations.

Comments

This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact SMR Nina Choy (510) 385-5910, who represents the Office of Structural Materials for your project.

Inspected By: Clifford, William

Quality Assurance Inspector

Reviewed By: Levell, Bill

QA Reviewer
