

DEPARTMENT OF TRANSPORTATION**DIVISION OF ENGINEERING SERVICES**

Office of Structural Materials

Quality Assurance and Source Inspection



Bay Area Branch

690 Walnut Ave.St. 150

Vallejo, CA 94592-1133

(707) 649-5453

(707) 649-5493

Contract #: 04-0120F4Cty: SF/ALA Rte: 80 PM: 13.2/13.9File #: 1.28**WELDING INSPECTION REPORT****Resident Engineer:** Casey, William**Address:** 333 Burma Road**City:** Oakland, CA 94607**Report No:** WIR-027222**Date Inspected:** 17-Feb-2012**Project Name:** SAS Superstructure**OSM Arrival Time:** 700**Prime Contractor:** American Bridge/Fluor Enterprises, a JV**OSM Departure Time:** 1730**Contractor:** American Bridge/Fluor Enterprises, a JV**Location:** Job Site**CWI Name:** Salvador Merino**CWI Present:** Yes No**Inspected CWI report:** Yes No N/A**Rod Oven in Use:** Yes No N/A**Electrode to specification:** Yes No N/A**Weld Procedures Followed:** Yes No N/A**Qualified Welders:** Yes No N/A**Verified Joint Fit-up:** Yes No N/A**Approved Drawings:** Yes No N/A**Approved WPS:** Yes No N/A**Delayed / Cancelled:** Yes No N/A**Bridge No:** 34-0006**Component:** OBG**Summary of Items Observed:**

Quality Assurance Inspector (QA) Rene Hernandez was at the American Bridge/Fluor (ABF) job site at Yerba Buena Island in California between the times noted above in order to monitor Quality Control functions and the in process work being performed by ABF personnel. The following items were randomly being observed:

West Line

This QA observed, at random intervals, ABF/JV qualified welder Mike Jimenez #4671 performing Shielded Metal Arc Welding (SMAW) with 1/8" diameter E7018H4R electrode and implementing Caltrans approved Welding Procedure Specification (WPS) ABF-WPS-D15-1050A-CU. This was a Complete Joint Penetration (CJP) weld on a 14mm plate insert at the "A" deck to close the lifting lug deck penetration holes. This work was located at 13W PP119.5 W3 1 was performed in the flat position from the topside of the "A" deck plate. During welding, ABF Quality Control (QC) Salvador Merino was noted monitoring the welding parameters. Welding parameters were recorded. Also verified that CU backup strip was secured from top and under deck.

This QA observed, at random intervals, ABF/JV qualified welder Richard Garcia #5892 performing Flux Cored Arc Welding (FCAW) with 1.6mm diameter E71T-1M electrode and implementing Caltrans approved Welding Procedure Specification (WPS) ABF-WPS-D15-1012-3. This was a Complete Joint Penetration (CJP) weld connecting vertical stiffener plates to stiffener plate. This work was located at West line connection joint 13W to 14W LS 5.



This QA inspector observed ABF QC personnel performing UT weld inspection in accordance with section 6 of AWS D1.5. All work was being performed by certified personnel performing UT testing to level II requirements.

WELDING INSPECTION REPORT

(Continued Page 2 of 2)

Weld inspection was observed at 13W/14W weld # E2.

This QA inspector observed ABF QC personnel performing MT weld inspection in accordance with section 6 of AWS D1.5. All work was being performed by certified personnel performing MT testing to level II requirements. Weld inspection was observed at 13W/14W weld # A4.

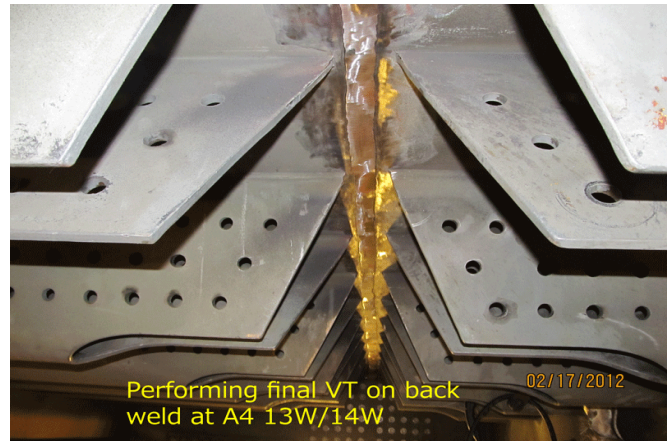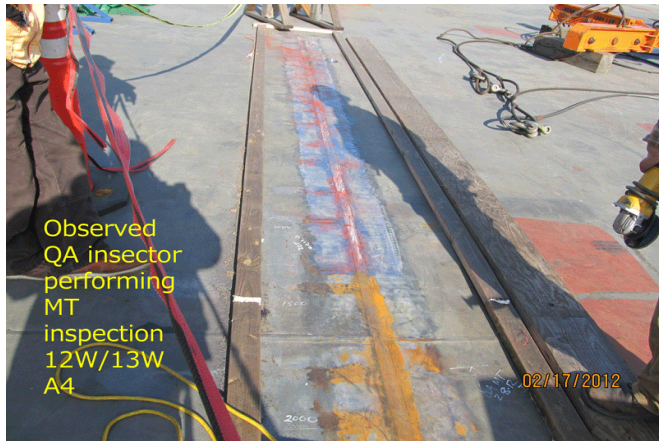

Summary of Conversations:

Pertinent conversations are in the body of this report

Comments

This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact Nina Choy, 510-385-5910, who represents the Office of Structural Materials for your project.

Inspected By: Hernandez,Rene

Quality Assurance Inspector

Reviewed By: Levell,Bill

QA Reviewer
