


Russian River Bridge Weekly Update
July 14, 2006

- Confab finished casting double T girders.
- Foundation Constructors, Inc finished driving a pile at abutment 1.
- Fontana Steel continued forming and placing steel rebar at abutment 11 and bent caps at bents 2-4.
- CC Myers formed for bent caps.
- Rege Construction excavated for water channel at abutment 1 to river bank.



7/12/06 Bent cap at bent 7 was completed.

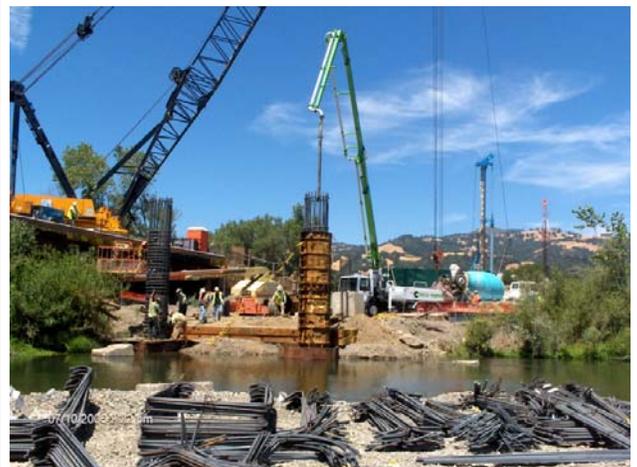

7/10/06 Poured concrete for columns at bent 5.
