

Memorandum

To: CHAIR AND COMMISSIONERS

CTC Meeting: April 7-8, 2010

Reference No.: 3.4
Information Item

From: NORMA ORTEGA
Chief Financial Officer

Prepared by: Karla Sutliff
Division Chief
Project Management

Subject: **FY 2009-10 SECOND QUARTER PROJECT DELIVERY REPORT**

Attached is the California Department of Transportation's Fiscal Year 2009-10 Second Quarter Project Delivery Report. This report has been discussed with the Commission's Executive Committee.

Attachment



Second Quarter FY 2009-10 Project Delivery Report

**Quarterly Report to the
California Transportation
Commission**



Contents

Executive Summary	pg 1
FY 2008-09 Contract for Delivery	pg 2
Program Delivery Summary	pg 10
Past Years' Contracts for Delivery Award Status	pg 13
Environmental Document Milestones	pg 14
Right of Way Program	pg 15
Construction Program	pg 16
Appendix:	pg 17
(A) Glossary	pg 18
(B) Past Years' Contracts For Delivery Award Status	
Projects Not Yet Awarded	pg 19
(C) Environmental Documents	pg 21
(D) Right of Way Status of Major Projects	pg 24
(E) Construction Contract Administration	pg 26

The Project Delivery Report is prepared quarterly in November, February, May, and August pursuant to California Transportation Commission (CTC) Resolution G-92-12. The Department of Transportation (Department) staff prepares this report. The purpose of this report is to monitor and track the progress of project delivery during the year and to compare against past years.

All costs shown are in \$1,000's unless noted otherwise. Abbreviations and acronyms are listed in the appendix.

Executive Summary

Second Quarter FY 2009-10

Project delivery by all programs though the second quarter is on track.

FY 2009-10 Contract for Delivery

For FY 2009-10, the dollar value of projects in the Contract for Delivery is \$3.062 billion. Through the second quarter, the Department delivered a total of 143 (47 percent of annual plan) highway construction contracts valued at \$1.089 billion (36 percent of annual plan).

Program Delivery Summary

Through the second quarter of FY 2009-10, the Department has delivered a total of 240 projects valued at \$1.359 billion from all funding programs.

Through the second quarter, the Department delivered a total of 14 (56 percent of annual plan) programmed State Transportation Improvement Program (STIP) highway construction contracts valued at \$93 million (26 percent of annual plan).

Through the second quarter, the Department delivered a total of 78 (45 percent of annual plan) programmed State Highway Operations and Protection Program (SHOPP) highway construction contracts valued at \$747 million (43 percent of annual plan).

Prior Years' Contracts for Delivery Award Status

Through the second quarter of FY 2009-10, the Department has awarded 312 projects out of 334 (93 percent) from the FY 2008-09 Contract for Delivery and 292 projects out of 294 (99 percent) from the FY 2007-08 Contract for Delivery.

Environmental Document Milestones

In FY 2009-10, the planned total number of environmental document milestones is 182. Through the second quarter, the Department delivered 99 (67 percent of annual plan) final environmental documents and 10 (29 percent of annual plan) draft environmental documents.

Right of Way Program

In FY 2009-10, the Department received a right-of-way allocation of \$237.7 million dollars. Through the second quarter, the Department expended \$80.3 million (34 percent of annual plan).

Construction Program

There are 540 on-going construction contracts valued at \$9.556 billion.

FY 2009-10 Contract for Delivery

Each year, the Department Director signs a contract with each of the Department's 12 district directors committing RTL Milestones for delivery by quarter.

The Contract for Delivery is the Department's fiscal year plan and includes programmed projects and projects funded from other sources including seismic, toll bridge, and partnership projects. The contract is not subject to change, so it does not include program amendments, emergency, or minor program projects.

The total estimated value at the "Ready To List" delivery milestone for all 306 projects in the FY 2009-10 Contract for Delivery is \$3.062 billion.

Reported delivery for the year is on track.

All 40 projects planned in the first quarter were delivered. 65 out of 68 projects planned for delivery in the second quarter were delivered. The Department also successfully accelerated the delivery of an additional 38 projects from future quarters.

Of the three projects that were not delivered as planned the status is as follows:

- one has subsequently been delivered,
- one was previously delivered in the first quarter and is now being revised to include the full programmed scope
- one project needs additional time to secure the necessary right of way.

Through the second quarter of FY 2009-10, the Department delivered a total of 143 projects (47 percent of annual plan) highway construction contracts valued at \$1,088.7 million (36 percent of annual plan).


STATUS AS OF DECEMBER 31, 2009




STATEWIDE Contract for Delivery FY 2009-10

Ready to List (RTL) Milestone Delivery

Description	1st Quarter	2nd Quarter	3rd Quarter	4th Quarter	TOTAL
NUMBER OF DELIVERIES					
Planned	40	68	122	76	306
Actual	40	65	35	3	143
CONSTRUCTION CAPITAL VALUE (\$ MILLIONS)					
Estimate in Contract	\$470.5	\$497.5	\$1,336.7	\$756.9	\$3,061.7
Estimated at RTL	\$421.5	\$418.6	\$246.8	\$1.7	\$1,088.7

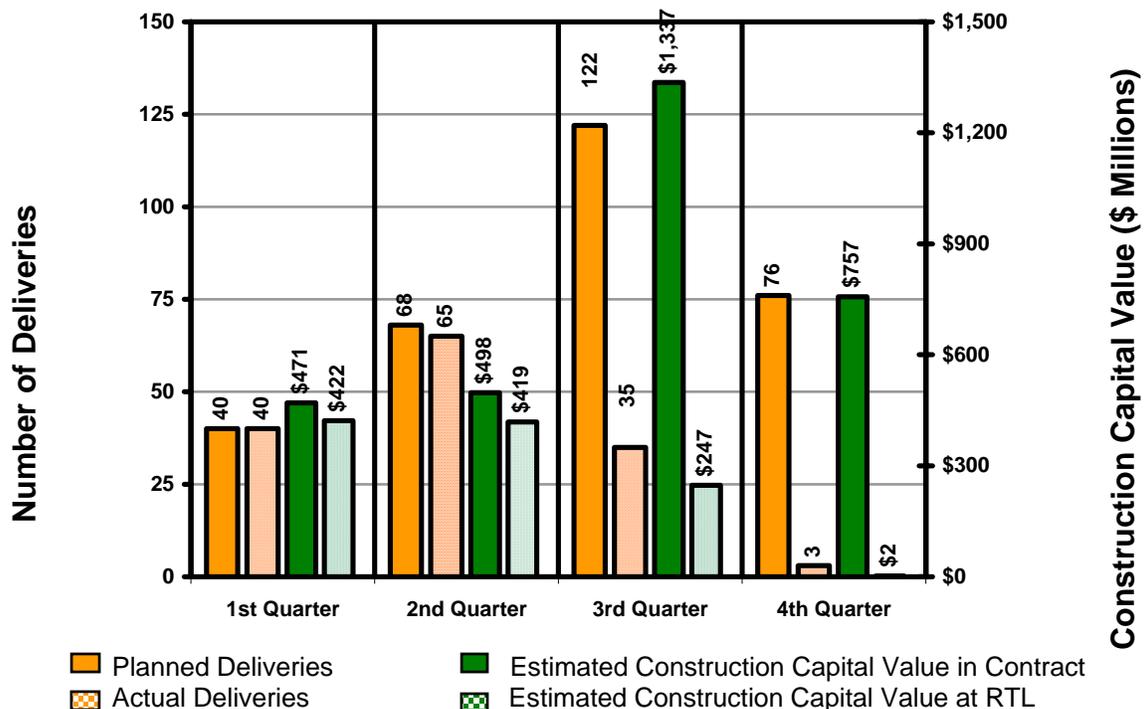

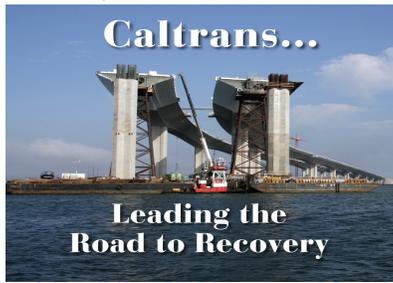

The California Department of Transportation Revised Contract for Delivery FY 2009/2010

2nd QUARTER DELIVERY REPORT 68 Planned Deliveries

DISTRICT	PROJECT	PROGRAM	COUNTY	ROUTE	EST. CONSTRUCTION CAPITAL VALUE IN CONTRACT (\$1000)	BUDGETED PE SUPPORT (\$1000)	ACTUAL PE SUPPORT (\$1000)	PROJECT DESCRIPTION	PROJECT APPROVAL & ENVIRONMENTAL DOCUMENT	RIGHT OF WAY CERTIFICATION	PLANS, SPECIFICATIONS AND ESTIMATES	READY TO LIST	AWARD
01	46400	SHOPP	HUM	101	\$10,679	\$1,176	\$878	RECONSTRUCT GUARD RAILING	★			★	10/01/10
01	46430	SHOPP	MEN	101	\$5,249	\$2,163	\$720	RECONSTRUCT GUARD RAILING			★	★	10/15/10
01	47600	SHOPP	MEN	253	\$850	\$535	\$529	REPAIR STORM DAMAGE	★			★	03/01/10
01	47640	SHOPP	MEN	162	\$1,920	\$726	\$590	REPAIR STORM DAMAGE	★			★	03/01/10
01	47730	SHOPP	MEN	20	\$586	\$507	\$519	REPAIR STORM DAMAGE	★		AADD	★	03/01/10
02	1E480	SHOPP	SHA	299	\$609	\$370	\$287	INSTALL SIGNALS	★				02/23/10
02	1E830	HM-p	LAS	395	\$5,000	\$90	\$90	THIN BLANKET OVERLAY NEAR DOYLE FROM ROUTE 70/395 SEPARATION	★	★	AADD		02/18/10
02	1E850	HM-p	LAS	44	\$6,000	\$90	\$90	THIN BLANKET OVERLAY FROM CRATER LAKE ROAD TO ROUTE 36	★	★	AADD		04/15/10
02	37100	B-CMIA	SHA	5	\$20,802	\$4,356	\$1,660	CONSTRUCT TRUCK CLIMBING LANES, NB & SB		★	★	★	03/24/10
02	37310	SHOPP	PLU	70	\$43,734	\$5,444	\$5,485	REPLACE BRIDGE NO. 9-15				★	03/22/10
03	2C844	SHOPP	SAC		\$8,045	\$1,700	\$1,916	FIRE AND LIFE SAFETY UPGRADE					07/15/10
03	35553	STIP	ED	50	\$817	\$35	\$132	MITIGATION PLANTING		★		★	07/15/10
03	3E390	B-RTE99	SAC	99	\$6,000	\$1,400	\$1,084	CONSTRUCT AUXILLARY LANES		★	★		07/15/10
03	3M140	HM-p	NEV	20	\$8,000	\$960	\$960	MICROSURFACING FROM JCT ROUTE 49 N TO JCT I-80		★	AADD		04/01/10
03	3M150	HM-p	YUB	65	\$2,800	\$336	\$336	GRIND PCC PAVEMENT FROM WHEATLAND TO SOUTH OF JCT SR 70		★	AADD		07/01/10
03	3M240	HM-p	BUT	32	\$1,600	\$192	\$192	MICROSURFACING FROM FOREST RANCH WAY TO HUMBOLDT ROAD		★	AADD	★	07/01/10
03	3M350	HM-b	SAC	50	\$3,600	\$432	\$432	TREAT BRIDGE DECKS & REPLACE JOINT SEALS		★	AADD		04/01/10
03	3M360	HM-b	YOL	5	\$1,900	\$220	\$220	TREAT BRIDGE DECKS & REPLACE JOINT SEALS		★	AADD	★	★
03	3M370	HM-b	GLE	5	\$1,200	\$144	\$144	TREAT BRIDGE DECKS & REPLACE JOINT SEALS		★	AADD	★	03/01/10
03	3M550	HM-p	ED	50	\$6,200	\$744	\$744	WEARING COURSE OVERLAY FROM ICE HOUSE RD TO STRAWBERRY RD		★	AADD	★	07/01/10
03	4A530	SHOPP	GLE	5	\$2,397	\$393	\$113	REPLACE METAL BEAM GUARD RAILS		★	★	★	07/15/10
04	04080	TOLL	SF	80	\$1,560	\$1,020	\$1,159	REPLACE 15KV CABLE AT LOWER DECK OF SFOBB		★			04/21/10

SECOND QUARTER OCTOBER 1 -DECEMBER 31

Status as of 12/31/09



- AADD - Authority to Advertise District Delegation
- HM - p - Highway Maintenance - pavement
- HM - b - Highway Maintenance - bridge
- HM - d - Highway Maintenance - drainage
- MTC - Metropolitan Transportation Commission
- STIP - State Transportation Improvement Program
- TCIF - Trade Corridors Improvement Program
- TCRP - Traffic Congestion Relief Program
- VAR - Various
- B-CMIA - Bond - Corridor Mobility Improvement Account
- SHOPP - State Highway Operation & Protection Program
- B-SHOPP - Bond - State Highway Operations Protection Program Augmentation
- B-RTE99 - P1B SR99 Improvement
- L - Reimb - Local Reimbursed
- M - Reimb - Measure Reimbursed
- PE - Preliminary Engineering
- Ph2 Ret - Phase 2 Retrofit
- RA - Recovery Act
- RETRO-SW - Retrofit Soundwall
- RM2 - Regional Measure 2
- TOLL - Other Toll
- TOLL-R - Toll Retrofit

- Completed
- Completed Ahead of Schedule
- Behind Schedule
- To be Completed/Awarded
- Awarded
- Awarded Ahead of Schedule
- Award Behind Schedule



The California Department of Transportation Revised Contract for Delivery FY 2009/2010

2nd QUARTER DELIVERY REPORT 68 Planned Deliveries

DISTRICT	PROJECT	PROGRAM	COUNTY	ROUTE	EST. CONSTRUCTION CAPITAL VALUE IN CONTRACT (\$1000)	BUDGETED PE SUPPORT (\$1000)	ACTUAL PE SUPPORT (\$1000)	PROJECT DESCRIPTION	PROJECT APPROVAL & ENVIRONMENTAL DOCUMENT	RIGHT OF WAY CERTIFICATION	PLANS, SPECIFICATIONS AND ESTIMATES	READY TO LIST	AWARD
04	0E980	HM-b	SON	1	\$814	\$178	\$178	TREAT BRIDGE DECKS & REPLACE JOINT SEALS	★		AADD		03/30/10
04	16374	RA/SHOPP/MTC	SF	101	\$110,000	\$11,400	\$7,761	DOYLE DRIVE - CONTRACT 4, SB BATTERY TUNNEL					12/16/09
04	1E480	HM-b	SCL	87	\$3,205	\$561	\$561	TREAT BRIDGE DECKS & REPLACE JOINT SEALS	★		AADD		04/06/10
04	1E720	HM-p	SM	92	\$3,700	\$324	\$324	RUBBERIZED HOT MIX ASPHALT OVERLAY	★	★	AADD	★	03/29/10
04	1E740	HM-p	SM	82	\$3,600	\$311	\$311	BONDED WEARING COURSE OVERLAY		★	AADD		04/15/10
04	24992	STIP/SHOPP	SM	82	\$10,908	\$2,343	\$2,364	MODIFY EXISTING TRAFFIC SIGNAL		★			05/03/10
04	25376	TCRP/LOCAL	ALA	680	\$1,915	\$2,003	\$988	ENVIRONMENTAL MITIGATION		★			04/08/10
04	2A541	SHOPP	NAP	29	\$760	\$301	\$476	NAPA COUNTY VISTA POINT ADA IMPROVEMENTS		★			03/29/10
04	3A820	SHOPP	MRN	1	\$495	\$734	\$829	RE-GRADING & RE-CONSTRUCT PAVEMENT AT ACCESSIBLE PARKING SPACES			AADD		03/26/10
05	0C882	SHOPP	MON	68	\$3,638	\$1,101	\$845	INSTALL CHANGEABLE MESSAGE SIGNS & CCTV CAMERAS		★			03/24/10
05	0G030	GARVEE	SLO	101	\$39,238	\$4,600	\$3,580	HIGHWAY REHABILITATION	★	★		★	
05	0Q420	SHOPP	SB	166	\$573	\$368	\$150	TRAFFIC SIGNALS AND MODIFY CURB RAMPS		★	★	★	04/13/10
05	34950	STIP	MON	101	\$18,291	\$8,276	\$6,783	RECONSTRUCT INTERCHANGE		★		★	03/22/10
05	44590	STIP	SLO	101	\$45,000	\$6,412	\$5,691	WIDEN & REPLACE BRIDGES, CONSTRUCT AUX LANES & BICYCLE PATH		★			05/01/10
05	44781	STIP	SB	101	\$2,300	\$245	\$257	LANDSCAPE MITIGATION		★		★	04/19/10
06	0A490	STIP	FRE	41	\$1,166	\$301	\$263	CORRIDOR ENHANCEMENT				★	06/01/10
06	0A990	SHOPP	KER	5	\$8,133	\$2,701	\$1,853	SAFETY ROADSIDE REST AREA RESTORATION		★			06/03/10
06	0F730	SHOPP	KER	178	\$1,929	\$446	\$266	INSTALL METAL BEAM GUARDRAILS				★	★
07	24890	SHOPP	LA	5	\$9,454	\$1,230	\$788	RETROFIT CONNECTOR			★	★	07/16/10
07	25610	SHOPP	LA	110	\$3,377	\$948		UPGRADE END TREATMENT & CRASH CUSHION		08/12/08	08/17/09	12/16/09	08/10/10
07	25690	SHOPP	LA	2	\$4,590	\$780	\$973	CCTV CAMERA CONTROL SYSTEM UPGRADE		★	★	★	08/19/10
07	3Y370	HM-b	LA	10	\$1,020	\$169	\$169	BRIDGE DECK REHABILITATION			AADD	★	03/19/10


SECOND QUARTER OCTOBER 1 -DECEMBER 31

Status as of 12/31/09



- AADD - Authority to Advertise District Delegation
- HM - p - Highway Maintenance - pavement
- HM - b - Highway Maintenance - bridge
- HM - d - Highway Maintenance - drainage
- MTC - Metropolitan Transportation Commission
- STIP - State Transportation Improvement Program
- TCIF - Trade Corridors Improvement Program
- TCRP - Traffic Congestion Relief Program
- VAR - Various
- B-CMIA - Bond - Corridor Mobility Improvement Account
- SHOPP - State Highway Operation & Protection Program
- B-SHOPP - Bond - State Highway Operations Protection Program Augmentation
- B-RTE99 - P1B SR99 Improvement
- L - Reimb - Local Reimbursed
- M - Reimb - Measure Reimbursed
- PE - Preliminary Engineering
- Ph2 Ret - Phase 2 Retrofit
- RA - Recovery Act
- RETRO-SW - Retrofit Soundwall
- RM2 - Regional Measure 2
- TOLL - Other Toll
- TOLL-R - Toll Retrofit

- Completed
- Completed Ahead of Schedule
- Behind Schedule
- To be Completed/Awarded
- Awarded
- Awarded Ahead of Schedule
- Award Behind Schedule

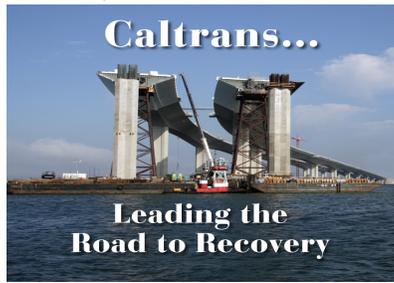

The California Department of Transportation Revised Contract for Delivery FY 2009/2010

2nd QUARTER DELIVERY REPORT 68 Planned Deliveries

DISTRICT	PROJECT	PROGRAM	COUNTY	ROUTE	EST. CONSTRUCTION CAPITAL VALUE IN CONTRACT (\$1000)	BUDGETED PE SUPPORT (\$1000)	ACTUAL PE SUPPORT (\$1000)	PROJECT DESCRIPTION	PROJECT APPROVAL & ENVIRONMENTAL DOCUMENT	RIGHT OF WAY CERTIFICATION	PLANS, SPECIFICATIONS AND ESTIMATES	READY TO LIST	AWARD
07	3Y770	HM-p	LA	605	\$1,200	\$380	\$380	COUNTYLINE TO ALONDRA BLVD UC, PROFILE GRINDING.			AADD	★	03/19/10
07	3Y820	HM-p	LA	118	\$3,300	\$1,056	\$1,056	FROM DE SOTO AVENUE UC TO 0.1 MILE WEST OF BRADLEY AVENUE UC			AADD	★	03/19/10
07	3Y900	HM-p	LA	103	\$1,200	\$380	\$380	COLD PLANE & OVERLAY			AADD	★	03/19/10
07	3Y910	HM-p	LA	110	\$6,000	\$1,898	\$1,898	PCC PROFILE GRINDING		★	AADD		03/19/10
07	3Y930	HM-p	LA	405	\$2,160	\$957	\$957	HIGH ADT/RAC OVERLAY, SO VAN NESS AVE UC TO 166TH STREET UC.		★	AADD	★	02/16/10
08	0K880	SHOPP	SBD	62	\$788	\$335	\$418	INSTALL CONCRETE BARRIER TYPE 60		★	AADD		04/05/10
08	0L240	SHOPP	RIV	79	\$317	\$248	\$142	RESTRIPE EXISTING CENTERLINE AND ADD GROUND IN RUMBLE STRIPES.		★	AADD	★	04/12/10
08	0L320	SHOPP	SBD	395	\$374	\$251	\$305	INSTALL "NO PASSING" STRIPING AND RUMBLE STRIPS ON CENTERLINE		★	AADD	★	05/05/10
08	0N170	SHOPP	SBD	15	\$1,500	\$390	\$110	REPLACE RECESSED PAVEMENT MARKERS		★		★	04/12/10
09	32710	STIP	MNO	395	\$2,399	\$797	\$1,102	WILDLIFE UNDERCROSSING FOR DEER AND OTHER LARGE ANIMALS		★	★	★	04/01/10
09	34180	HM-b	KER	58	\$880	\$71	\$71	METHACRYLATE SEAL DECK TREATMENT			★	★	02/17/10
09	34190	HM-b	KER	58	\$859	\$71	\$71	METHACRYLATE SEAL DECK TREATMENT			★	★	02/17/10
10	0A872	B-CMIA	STA	219	\$26,000	\$4,000		WIDEN TO 4 LANES AND INTERSECTION IMPROVEMENTS		11/26/09		11/26/09	10/14/10
10	0S500	HM-p	ALP	4	\$1,500	\$123	\$123	RUBBERIZED HOT MIX AC OVERLAY	★		AADD	★	03/01/10
10	0S510	HM-p	MER	140	\$2,700	\$123	\$123	RUBBERIZED HOT MIX AC OVERLAY			AADD	★	03/01/10
10	0S520	HM-p	CAL	4	\$500	\$123	\$123	CHIP SEAL (PME) NEAR COTTAGE SPRINGS	★		AADD	★	03/04/10
10	0S540	HM-p	ALP	89	\$1,800	\$123	\$123	RUBBERIZED AC OVERLAY ON SR 89 FROM THE MONO COUNTY LINE	★		AADD		03/01/10
10	0S550	HM-p	STA	4	\$1,500	\$123	\$123	STANISLAUS CO, FROM SAN JOAQUIN CO LINE TO CALAVERAS CO LINE		★	AADD		03/01/10
10	0T440	SHOPP	STA	5	\$647	\$192	\$146	TREAT BRIDGE DECKS & REPLACE JOINT SEALS	★				03/09/10
10	0T960	HM-p	SJ	4	\$1,000	\$123	\$123	RUBBERIZED HOT MIX AC OVERLAY	★	★	AADD	★	03/04/10
10	37930	SHOPP	CAL	12	\$6,748	\$2,672	\$2,754	STRUCTURAL SECTION REPAIR		★		★	02/11/10
11	2M080	HM-p	SD	8	\$6,000	\$500	\$500	GRIND PCC LANES AND OVERLAY SHOULDERS (E/B Only)		★	AADD	12/28/09	05/04/10

SECOND QUARTER OCTOBER 1 -DECEMBER 31


Status as of 12/31/09



- AADD** - Authority to Advertise District Delegation
- HM - p** - Highway Maintenance - pavement
- HM - b** - Highway Maintenance - bridge
- HM - d** - Highway Maintenance - drainage
- MTC** - Metropolitan Transportation Commission
- STIP** - State Transportation Improvement Program
- TCIF** - Trade Corridors Improvement Program
- TCRP** - Traffic Congestion Relief Program
- VAR** - Various
- B-CMIA** - Bond - Corridor Mobility Improvement Account
- SHOPP** - State Highway Operation & Protection Program
- B-SHOPP** - Bond - State Highway Operations Protection Program Augmentation
- B-RTE99** - P1B SR99 Improvement
- L - Reimb** - Local Reimbursed
- M - Reimb** - Measure Reimbursed
- PE** - Preliminary Engineering
- Ph2 Ret** - Phase 2 Retrofit
- RA** - Recovery Act
- RETRO-SW** - Retrofit Soundwall
- RM2** - Regional Measure 2
- TOLL** - Other Toll
- TOLL-R** - Toll Retrofit

- Completed
- ★ Completed Ahead of Schedule
- Behind Schedule
- To be Completed/Awarded

- Awarded
- ★ Awarded Ahead of Schedule
- Award Behind Schedule

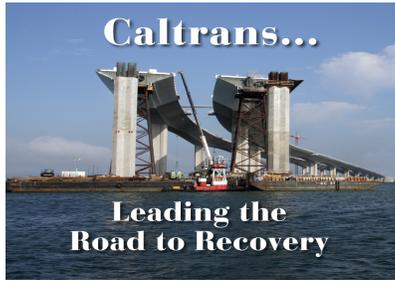

The California Department of Transportation Revised Contract for Delivery FY 2009/2010

2nd QUARTER DELIVERY REPORT 68 Planned Deliveries

DISTRICT	PROJECT	PROGRAM	COUNTY	ROUTE	EST. CONSTRUCTION CAPITAL VALUE IN CONTRACT (\$1000)	BUDGETED PE SUPPORT (\$1000)	ACTUAL PE SUPPORT (\$1000)	PROJECT DESCRIPTION	PROJECT APPROVAL & ENVIRONMENTAL DOCUMENT	RIGHT OF WAY CERTIFICATION	PLANS, SPECIFICATIONS AND ESTIMATES	READY TO LIST	AWARD
12	04322	SHOPP	ORA	74	\$1,039	\$381	\$243	PLANT ESTABLISHMENT/ ENVIRONMENTAL MITIGATION		★		★	04/01/10
12	0E570	STIP	ORA	5	\$13,447	\$2,723	\$3,314	CONSTRUCT AUX LANE & WIDEN SB OFF-RAMP, RAMP INTERSECTION & CAMINO	★	★			07/01/10
TOTAL					\$497,512	\$86,805	\$68,275						


SECOND QUARTER OCTOBER 1 -DECEMBER 31

Status as of 12/31/09



- AADD - Authority to Advertise District Delegation
- HM - p - Highway Maintenance - pavement
- HM - b - Highway Maintenance - bridge
- HM - d - Highway Maintenance - drainage
- MTC - Metropolitan Transportation Commission
- STIP - State Transportation Improvement Program
- TCIF - Trade Corridors Improvement Program
- TCRP - Traffic Congestion Relief Program
- VAR - Various
- B-CMIA - Bond - Corridor Mobility Improvement Account
- SHOPP - State Highway Operation & Protection Program
- B-SHOPP - Bond - State Highway Operations Protection Program Augmentation
- B-RTE99 - P1B SR99 Improvement
- L - Reimb - Local Reimbursed
- M - Reimb - Measure Reimbursed
- PE - Preliminary Engineering
- Ph2 Ret - Phase 2 Retrofit
- RA - Recovery Act
- RETRO-SW - Retrofit Soundwall
- RM2 - Regional Measure 2
- TOLL - Other Toll
- TOLL-R - Toll Retrofit

- Completed
- Completed Ahead of Schedule
- Behind Schedule
- To be Completed/Awarded
- Awarded
- Awarded Ahead of Schedule
- Award Behind Schedule

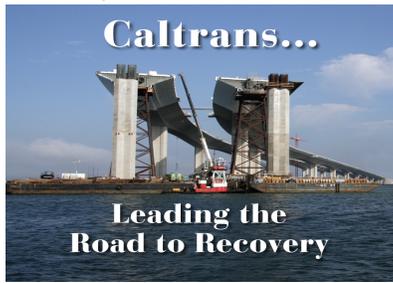

The California Department of Transportation Revised Contract for Delivery FY 2009/2010

1st QUARTER DELIVERY REPORT 40 Planned Deliveries

DISTRICT	PROJECT	PROGRAM	COUNTY	ROUTE	EST. CONSTRUCTION CAPITAL VALUE IN CONTRACT (\$1000)	BUDGETED PE SUPPORT (\$1000)	ACTUAL PE SUPPORT (\$1000)	PROJECT DESCRIPTION	PROJECT APPROVAL & ENVIRONMENTAL DOCUMENT	RIGHT OF WAY CERTIFICATION	PLANS, SPECIFICATIONS AND ESTIMATES	READY TO LIST	AWARD
01	36431	SHOPP	MEN	VAR	\$1,100	\$1,283	\$3,848	CULVERT REHABILITATION			AADD	★	★
01	47240	SHOPP	HUM	96	\$1,590	\$616	\$786	REPAIR ROADWAY AND INSTALL GALLERY DRAINAGE WALLS			AADD	★	★
01	47280	SHOPP	MEN	1	\$501	\$440	\$571	REPAIR STORM DAMAGE				★	★
01	47820	SHOPP	HUM	169	\$1,112	\$503	\$414	REPAIR STORM DAMAGE			AADD	★	★
02	0E390	SHOPP	SHA	44	\$1,447	\$442	\$267	SHOULDER WIDENING		★	AADD		★
02	1E110	SHOPP	SHA	5	\$1,645	\$434	\$381	INCREASE CURVE RADII		★		★	★
03	3M250	HM-p	SUT	99	\$2,400	\$228	\$228	GRIND PCC PAVEMENT, BUTTE HOUSE RD UC TO NORTH OF EAGER RD OC			AADD	★	07/01/10
03	4C220	SHOPP	NEV	80	\$1,601	\$853	\$873	REHAB & UPGRADE TRUCK INSP FACILITY				★	01/15/10
04	0060C	TOLL	CC	680	\$3,558	\$802	\$715	REPLACEMENT PLANTING	★	★		★	★
04	0A781	SHOPP	SCL	101	\$3,150	\$795	\$903	UPGRADE TRAFFIC BARRIER AND GUARD RAIL TERMINALS				★	12/01/09
04	16373	SHOPP/MTC	SF	101	\$130,000	\$13,700	\$6,424	DOYLE DRIVE - CONTRACT 3, SB HIGH VIADUCT					★
04	1637G	MTC	SF	101	\$1,100	\$500	\$47	CONTRACT 1.2 ENVIRONMENTAL MITIGATION - BUILDING STABILIZATION					★
04	1637H	MTC	SF	101	\$3,000	\$400	\$161	CONTRACT 1.3 ENVIRONMENTAL MITIGATION - TREE PROGRAM					★
04	1637J	MTC	SF	101	\$500	\$300	\$39	DOYLE DRIVE - CONTRACT 1.4, GEOTECHNICAL DEMONSTRATION CDSM.				★	★
04	1E300	SHOPP	SF	101	\$3,537	\$777	\$861	TREAT BRIDGE DECKS & REPLACE JOINT SEALS		★	AADD		04/13/10
04	1E410	SHOPP	SM	1	\$1,416	\$279	\$432	TREAT BRIDGE DECKS & REPLACE JOINT SEALS		★	AADD	★	04/13/10
04	1E420	HM-b	SM	280	\$864	\$162	\$162	TREAT BRIDGE DECKS & REPLACE JOINT SEALS		★	AADD		★
04	1E470	SHOPP	NAP	29	\$1,600	\$376	\$699	TREAT BRIDGE DECKS & REPLACE JOINT SEALS		★	AADD	★	04/13/10
04	26372	RM2	CC	80	\$38,300	\$6,100	\$6,104	EXTEND EASTBOUND I-80 HOV LANE				★	★
04	2S370	SHOPP	NAP	128	\$1,550	\$705	\$844	STORM DAMAGE REPAIR			AADD		★
04	2S941	SHOPP	SON	128	\$1,216	\$302	\$333	HIGHWAY PLANTING RESTORATION		★		★	04/21/10
05	0L70U	SHOPP	SCR	17	\$10,130	\$5,619	\$3,729	UPGRADE GUARDRAIL, CRASH CUSHIONS, END TREATMENTS & RETAINING WALLS				★	★

FIRST QUARTER JULY 1 - SEPTEMBER 30

Status as of 12/31/09



- AADD - Authority to Advertise District Delegation
- HM - p - Highway Maintenance - pavement
- HM - b - Highway Maintenance - bridge
- HM - d - Highway Maintenance - drainage
- MTC - Metropolitan Transportation Commission
- STIP - State Transportation Improvement Program
- TCIF - Trade Corridors Improvement Program
- TCRP - Traffic Congestion Relief Program
- VAR - Various
- B-CMIA - Bond - Corridor Mobility Improvement Account
- SHOPP - State Highway Operation & Protection Program
- B-SHOPP - Bond - State Highway Operations Protection Program Augmentation
- B-RTE99 - P1B SR99 Improvement
- L - Reimb - Local Reimbursed
- M - Reimb - Measure Reimbursed
- PE - Preliminary Engineering
- Ph2 Ret - Phase 2 Retrofit
- RA - Recovery Act
- RETRO-SW - Retrofit Soundwall
- RM2 - Regional Measure 2
- TOLL - Other Toll
- TOLL-R - Toll Retrofit

- Completed
- ★ Completed Ahead of Schedule
- Behind Schedule
- To be Completed/Awarded
- Awarded
- ★ Awarded Ahead of Schedule
- Award Behind Schedule



The California Department of Transportation Revised Contract for Delivery FY 2009/2010

1st QUARTER DELIVERY REPORT 40 Planned Deliveries

DISTRICT	PROJECT	PROGRAM	COUNTY	ROUTE	EST. CONSTRUCTION CAPITAL VALUE IN CONTRACT (\$1000)	BUDGETED PE SUPPORT (\$1000)	ACTUAL PE SUPPORT (\$1000)	PROJECT DESCRIPTION	PROJECT APPROVAL & ENVIRONMENTAL DOCUMENT	RIGHT OF WAY CERTIFICATION	PLANS, SPECIFICATIONS AND ESTIMATES	READY TO LIST	AWARD
05	0N831	SHOPP	MON	101	\$193	\$203	\$103	MITIGATION PLANTING PROJECT	★		★	★	
05	0P870	SHOPP	SCR	9	\$602	\$888	\$796	CONSTRUCT RETAINING WALL					★
05	0Q660	SHOPP	SB	135	\$4,635	\$403	\$191	CONSTRUCT MEDIAN BARRIER			★	★	
05	0Q690	SHOPP	SB	1	\$3,855	\$519	\$248	CONSTRUCT MEDIAN BARRIER			★	★	
06	0E970	SHOPP	FRE	41	\$9,680	\$1,420	\$1,207	INSTALL RAMP METERS AT 4 LOCATIONS ALONG NB RTE 41	★				10/15/10
06	44770	SHOPP	FRE	41	\$9,363	\$2,822	\$2,590	CONSTRUCT NB AUXILIARY LANE	★		★		01/15/11
07	4S730	SHOPP	VEN	34	\$270	\$247	\$292	MODIFY EXISTING SIGNAL		★	★	★	
08	0A550	SHOPP	RIV	91	\$13,720	\$1,456	\$1,037	REHABILITATE PAVEMENT (CAP-M)			★		02/15/10
08	0E570	SHOPP	SBD	66	\$2,217	\$499	\$693	UPGRADE GUARDRAIL END TREATMENTS					★
08	49750	B_CMIA	SBD	10	\$26,523	\$3,540	\$2,243	WIDEN EXIT RAMP AND CONSTRUCT AUXILIARY LANES					04/12/10
10	0L630	SHOPP	SJ	99	\$7,105	\$1,540	\$1,547	UPGRADE MEDIAN BARRIER					★
11	08010	RA	SD	76	\$95,917	\$32,154	\$21,933	CONSTRUCT 4-LANE HIGHWAY	★		★		
11	24320	SHOPP	SD	8	\$3,028	\$585	\$1,660	ROADSIDE REST AREA RESTORATION/ADA COMPLIANCE			★		12/17/09
11	2T040	B-CMIA	SD	805	\$75,380	\$14,300	\$11,940	CONSTRUCT HOV AND DAR			★		02/16/10
12	0C540	SHOPP	ORA	405	\$4,312	\$859	\$975	REMOVE RAISED CURB ISLANDS & MBGRS, GRADE, PAVE, INSTALL CONCRETE			★	★	
12	0F340	SHOPP	ORA	55	\$1,410	\$218	\$463	METHACRYLATE SEAL DECK TREATMENT, JOINT SEALS	★		★	★	
12	0H550	SHOPP	ORA	5	\$614	\$928	\$1,038	PAVEMENT DELINEATION & SIGNING			★		02/01/10
12	0J480	SHOPP	ORA	605	\$406	\$404	\$374	ADA IMPROVEMENT			★		
TOTAL					\$470,547	\$98,601	\$78,151						

FIRST QUARTER JULY 1 - SEPTEMBER 30 Status as of 12/31/09



- AADD - Authority to Advertise District Delegation
- HM - p - Highway Maintenance - pavement
- HM - b - Highway Maintenance - bridge
- HM - d - Highway Maintenance - drainage
- MTC - Metropolitan Transportation Commission
- STIP - State Transportation Improvement Program
- TCIF - Trade Corridors Improvement Program
- TCRP - Traffic Congestion Relief Program
- VAR - Various
- B-CMIA - Bond - Corridor Mobility Improvement Account
- SHOPP - State Highway Operation & Protection Program
- B-SHOPP - Bond - State Highway Operations Protection Program Augmentation
- B-RTE99 - P1B SR99 Improvement
- L - Reimb - Local Reimbursed
- M - Reimb - Measure Reimbursed
- PE - Preliminary Engineering
- Ph2 Ret - Phase 2 Retrofit
- RA - Recovery Act
- RETRO-SW - Retrofit Soundwall
- RM2 - Regional Measure 2
- TOLL - Other Toll
- TOLL-R - Toll Retrofit

- Completed
- ★ Completed Ahead of Schedule
- Behind Schedule
- To be Completed/Awarded
- Awarded
- ★ Awarded Ahead of Schedule
- Award Behind Schedule

Program Delivery Summary

This section describes by funding programs the number and dollar value of all projects delivered.

Intercity Rail Program

For FY 2009-10, three Intercity Rail projects valued at \$21.4 million are programmed for delivery.

Number of Intercity Rail Projects

	Q1	Q2	Q3	Q4	Annual
Plan	0	0	0	3	3
Actual	0	0	0	0	0

Value of Intercity Rail Projects

	Q1	Q2	Q3	Q4	Annual
Plan	\$ 0.0	\$ 0.0	\$ 0.0	\$ 21.4	\$ 21.4
Actual	\$ 0.0	\$ 0.0	\$ 0.0	\$ 0.0	\$ 0.0

AB 1740 Retrofit Soundwall Program

To date, 62 retrofit soundwall locations valued at \$208 million, out of a total 63 planned projects valued at \$226 million, have been delivered.

	Delivered		Construction Completed	
Locations	62	98%	61	97%
Value	\$ 208	92%	\$ 210	93%

The last project with a current estimated contract value of \$6 million in the program is planned for delivery in the fourth quarter of FY 2009-10.

Delivery Summary of All Programs

Through the end of the second quarter in FY 2009-10, the Department delivered a total of 240 projects valued at \$1.359 billion from all programs.

Projects are shown below by the planned program and dollar value.

Projects by Funding Programs	Number		Value	
	Annual Plan	FYTD	Annual Plan	FYTD
STIP (w TCRP,TFA)	25	14	\$ 351	\$ 93
SHOPP	174	78	\$ 1,005	\$ 445
BOND	12	6	\$ 511	\$ 122
Partnership*	31	20	\$ 997	\$ 524
Retrofit Soundwall	1	0	\$ 6	\$ 0
Maintenance (CFD)	87	40	\$ 209	\$ 101
Subtotal	330	158	\$ 3,079	\$ 1,285
Emergency		10		\$ 11
Minor		26		\$ 14
Maintenance		46		\$ 49
Total		240		\$ 1,359

* Partnership funds include all local funds and federal fund subventions given to local agencies.

Detailed Delivery Summary of All Projects by Programs

Programs	Annual Number of Projects			Annual Dollar Value of Projects		
	Plan	Actual	Percent	Plan	Actual	Percent
STIP Program						
STIP (w TCRP, TFA)	25	14	56	\$ 351	\$ 93	26
Amended** STIP	0	0	100	\$ 0	\$ 0	0
TOTAL STIP	25	14	56	\$ 351	\$ 93	26
SHOPP Program						
SHOPP (w Augmentation)	172	75	44	\$ 1,004	\$ 442	44
Amended** SHOPP	2	2	100	\$ 1	\$ 1	100
Advanced** SHOPP		1			\$ 2	
TOTAL SHOPP	174	78	45	\$ 1,005	\$ 445	44
Other ** Programs in Contract (excluding Intercity Rail Bond Program)						
BOND	12	6	50	\$ 511	\$ 122	24
Retrofit Soundwall	1	0	0	\$ 6	\$ 0	0
Partnership	31	20	65	\$ 997	\$ 524	53
Maintenance	87	40	46	\$ 209	\$ 101	48
TOTAL "Other"	131	66	50	\$ 1,723	\$ 747	43
Additional ** Programs						
Emergency		10			\$ 11	
Minor		26			\$ 14	
Maintenance		46			\$ 49	
TOTAL "Additional"		82			\$ 74	
TOTAL All Programs						
STIP	25	14	56	\$ 351	\$ 93	26
SHOPP	174	78	45	\$ 1,005	\$ 445	44
Other	131	66	50	\$ 1,723	\$ 747	43
Subtotal	330	158	48	\$ 3,079	\$ 1,285	42
Additional		82			\$ 74	
TOTAL		240			\$ 1,359	

**** Notes:**

Additional – Recent projects not in contract. Includes funding reservations.

Amended – Added or deleted to program by amendment.

Advanced – Delivered early from future program year. (Not included in planned numbers)

Other – planned non-STIP/SHOPP projects committed in contract.

Delivery Percentages – Advances in contracts are included in planned figures, other advances are not included in planned figures, but are added to delivered figures.

Due to multiple funding sources on some projects, the sum of contract projects by funding source will exceed the number of planned contract projects.

Historical Program Delivery Comparison

2nd Quarter "Annual Plan" Comparison

Number of STIP Projects

	09-10	08-09	07-08	06-07	05-06
Annual Plan	25	34	54	57	51
FYTD	14	16	30	28	19
Percent	56	47	56	49	37

Value of STIP Projects

	09-10	08-09	07-08	06-07	05-06
Annual Plan	\$ 351	\$466	\$1,002	\$ 450	\$ 490
FYTD	\$ 93	\$ 140	\$ 471	\$ 285	\$ 146
Percent	26	30	47	63	30

Number of SHOPP Projects

	09-10	08-09	07-08	06-07	05-06
Annual Plan	174	215	200	253	302
FYTD	78	107	112	117	107
Percent	45	50	56	46	35

Value of SHOPP Projects

	09-10	08-09	07-08	06-07	05-06
Annual Plan	\$1,005	\$1,441	\$1,766	\$1,331	\$1,376
FYTD	\$ 445	\$ 312	\$ 514	\$ 598	\$ 382
Percent	44	22	29	45	28

Total Number of All Projects

	09-10	08-09	07-08	06-07	05-06
FYTD	240	288	272	351	339

Total Value of All Projects

	09-10	08-09	07-08	06-07	05-06
FYTD	\$1,359	\$1,342	\$1,468	\$1,263	\$815

Prior Years' Contract For Delivery Award Status

This section describes the contract award status projects in past years for the annual Contract for Delivery.

Contract Award Status

Progress continues to be made to get past years' contracts for delivery projects awarded.

Contract Award Status	Plan	Awarded	Percent
FY 2008-09 Contract for Delivery	334	312	93%
FY 2007-08 Contract for Delivery	294	292	99%
FY 2006-07 Contract for Delivery	286	286	100%
FY 2005-06 Contract for Delivery	174	174	100%

Historical Delivery Comparison

Through the second quarter of FY 2009-10, for last year's contract for delivery (FY 2008-09), the Department has awarded 312 projects out of 334 projects or 93 percent of the planned projects. As a comparison, as reported a year ago for the same time period, the Department had awarded 273 projects out of 294 planned projects or 93 percent.

Contracts Not Yet Awarded

Of the 24 projects not yet awarded, 9 projects have been allocated and are currently out to bid. Five projects were delayed until bond sales made funds available for new allocations.


The two projects remaining from the FY 2007-08 contract have not been allocated because they were delivered in advance of their programmed funding. The remaining eight projects should be put out to bid shortly.

Contracts Not Yet Awarded	Number
Project currently bid	9
On hold pending Bond allocation	5
Delivered with future year funds	2
To be put out to bid soon	8
Total	24

See appendix for a list of projects not yet awarded

Projects Not Yet Awarded

(percent)

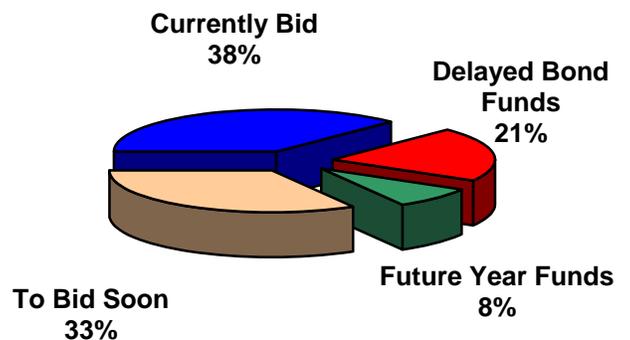

Environmental Document Milestones


Environmental Delivery Commitment

As part of this report, the Department reports on delivery for the upcoming year of the two environmental milestones that require CTC action for consideration of future funding. The two milestones include Draft Environmental Documents (DED) and Final Environmental Documents (FED). To provide a comprehensive view of environmental documents under development, the Department also includes Categorical Exclusions that do not require CTC review or action. For FY 2009-10, the Department planned 182 environmental milestones.

For FY 2009-10 through the second quarter, the Department delivered 109 (60 percent of annual plan) environmental milestones.

Through the end of the second quarter, one planned environmental document (FED) has slipped outside FY 2009-10 (milestones shown in appendix).

Number of DED Milestones

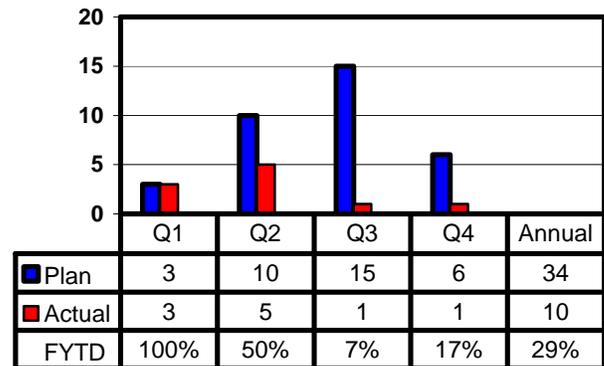

Historical Delivery Comparisons

As a benchmark for comparison, below are historical environmental milestone delivery trend charts for the current year and past four years.


Past 2nd Qtr PAED Milestones

	09-10	08-09	07-08	06-07	05-06
Plan	148	151	168	113	121
FYTD	99	98	95	71	64
Percent	67	65	57	63	53

Past 2nd Qtr DED Milestones

	09-10	08-09	07-08	06-07	05-06
Plan	34	41	47	44	54
FYTD	10	17	18	10	14
Percent	29	41	38	23	26

Number of FED Milestones

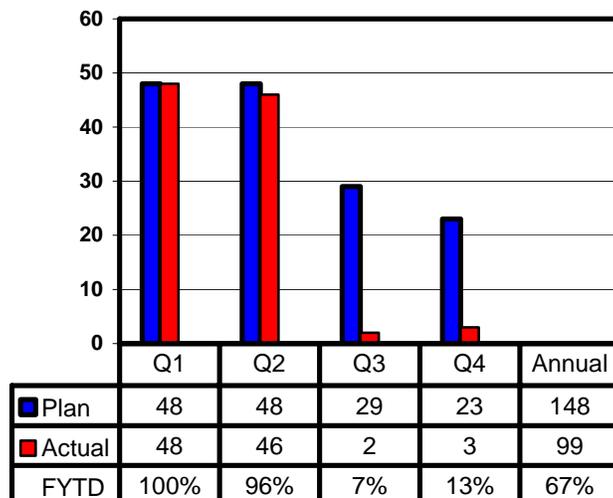

Right of Way

Right of Way Delivery Commitment

The Department's R/W delivery commitment is twofold. One delivery commitment is to utilize funds approved by the CTC for acquisition of R/W. The second delivery commitment is to secure all necessary R/W requirements and to certify R/W for all projects scheduled for delivery in the current year.

Right of Way Expenditures


R/W activities and expenditures are outlined by the categories below:

Category (\$millions)	Plan	FYTD	Percent
Capital Projects			
STIP	\$ 133.7	\$ 58.3	44
SHOPP	\$ 31.2	\$ 6.9	22
Subtotal	\$ 164.9	\$ 65.2	40
Specific Categories			
Post Certifications	\$ 51.8	\$ 12.2	24
Hardships	\$ 0.0	\$ 0.0	0
Inverse Condemnation*	\$ 20.0	\$ 2.6	13
Project Development	\$ 1.0	\$ 0.3	30
Subtotal	\$ 72.8	\$ 15.1	21
Pre-Project Mitigation	\$ 0.0	\$ 0.0	0
TOTAL	\$ 237.7	\$ 80.3	34

For FY 2009-10, the Department requested and received a R/W allocation of \$237.7 million.

Though the end of the second quarter of FY 2009-10, the Department expended \$80.3 million, or 34 percent of the allocation.

Right of Way Certifications

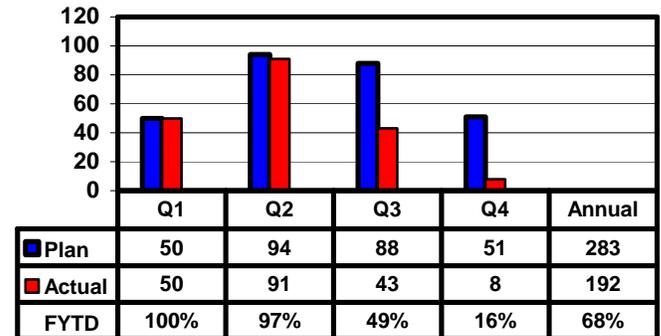

For FY 2009-10, the planned number of R/W certifications is 283. Through the second quarter, the Department completed a total of 192 R/W certifications, 68 percent of the annual plan. Of the completed milestones, 91 were delivered in an earlier quarter than the planned quarter.

Historical Delivery Comparisons

As a benchmark for comparison, below are historical R/W delivery trend charts for the current year and past four years.

Past 2nd Qtr Right of Way Expenditures

	09-10	08-09	07-08	06-07	05-06
Plan	\$237.7	\$231.3	\$284.0	\$302.0	\$171.0
FYTD	\$ 80.3	\$106.1	\$ 94.3	\$205.9	\$ 86.4
Percent	34	46	33	68	51

Past 2nd Qtr Right of Way Certifications

	09-10	08-09	07-08	06-07	05-06
Plan	283	304	245	277	174
FYTD	192	206	160	192	107
Percent	68	68	65	69	61

Construction Program


PLANNED CONSTRUCTION PROGRAM

(Excludes some projects such as minor, program amendments and emergency.)

Construction Delivery Commitment

Delivery in the eyes of our customers is achieved when capital improvements are delivered to the traveling public. This is best measured by when the construction contract is accepted.

Planned Construction Contracts Accepted

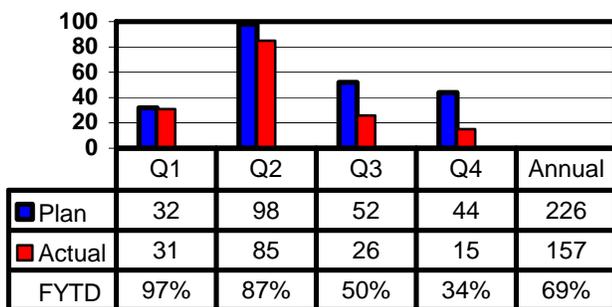

Through the end of the second quarter, FY 2009-10, the Department had accepted a total of 157 major construction contracts (69 percent) out of a total of 226 planned contracts identified in the Department's delivery plan. Of the completed milestones, 71 were delivered in an earlier quarter than the planned quarter.

Historical Delivery Comparison

As a benchmark for comparison, shown are historical delivery trend charts for planned major construction contract acceptances.

Past 2nd Qtr Construction Contracts Accepted

	09-10	08-09	07-08	06-07	05-06
Plan	226	213	248	237	164
FYTD	157	144	153	148	95
Percent	69	68	62	62	58


OVERALL CONSTRUCTION PROGRAM

(Includes planned programmed projects and additional minor A, amendments, and some minor B projects that are not programmed.)

Under Construction

At the end of the second quarter, FY 2009-10, the Department had 540 contracts valued at \$9,556 million under construction.

Value of Ongoing Contracts (\$ millions)

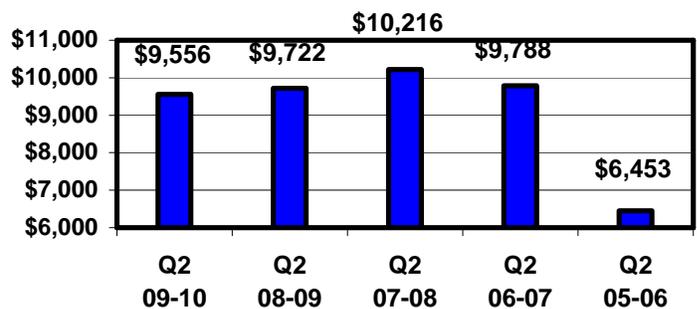

2nd Quarter Construction Program Results

Construction Starts – 70 construction contracts valued at \$862 million were started (including minor A and some minor B projects that are not programmed).

Accepted Contracts – 206 construction contracts valued at \$856 million were accepted.

Arbitration - The Department currently has 37 construction contracts in arbitration. Four new arbitration case was filed and two cases were settled or received an arbitrator's decision.

Appendix

- (A) Glossary
- (B) Prior Years' Contracts For Delivery Award Status
Projects Not Yet Awarded
- (C) Environmental Documents
- (D) Right of Way Status of Major Projects
- (E) Construction Contract Administration

Glossary

- #** 1st – First
2nd – Second
3rd – Third
4th - Fourth
- A** AB – Assembly Bill
- B** BATA – Bay Area Toll Authority
BIP –
BOND – Proposition 1B Bond Program
- C** Cap – Capital (has construction)
CE – Categorical Exemption
Cert - Certification
CTC – California Transportation Commission
Cty - County
- D** Doc – Document
D-EA – District and expenditure authorization
DED – Draft environmental document
- E** ED – Environmental Document
EIR – Environmental Impact Report
Emerg – Emergency funded project
Env - Environmental
- F** FED – Final environmental document
FY – Fiscal Year
FYTD – Fiscal year to date
- N** ND – Negative Declaration
NOP – Notice of Preparation
- P** PART – Partnership (local funded projects delivered by state including contributor funds on state funded projects (counts all non-STIP or non- SHOPP Funds)
PAED – Project approval and environmental document
PM – Post Mile
PSE – Plans, specifications and estimate
- Q** Q1 – First Quarter
Q2 – Second Quarter
Q3 – Third Quarter
Q4 – Fourth Quarter
Qtr – Quarter
- R** RTL – Ready to list
Rte – Route
R/W – Right-of-way
RWC – Right-of-way certification
- S** SDWLL – Retrofit Soundwall funded project
SHOPP – State Highway Operations and Protection Program
STIP – State Transportation Improvement Program
- T** TBSRA – Toll Bridge Seismic Retrofit Account
TCRF – Traffic congestion relief funds

Prior Years' Contracts for Delivery Award Status Projects Not Yet Awarded

Projects initial bid.

FY CFD	D-EA	Pgm	Cty	Rte	Description	Value	Ready to List	Vote	Advertise	Bid Opening	Status
08-09	03-2C860	SHOPP	PLA	80	Roadway Rehabilitation	\$ 166,750	04/15/09	05/14/09	07/27/09	10/20/09	
08-09	04-04463	TOLL	SF	80	Joint Repair At Piers E5, E12, E15 And E16, Etal	\$ 500	03/30/09	Bata	01/04/10	01/27/10	
08-09	06-35341	STIP	KER	46	2-Lane Conv To 4-Lane Exprwy	\$ 55,500	06/25/09	10/15/09	03/08/10	04/14/10	
08-09	07-12181 (1218V)	Bond CMIA	LA	5	Const Hov Lane	\$ 92,000	12/31/08	Loc	03/08/10	04/22/10	
08-09	07-12190 (1219U)	STIP	LA	5	Hov Ln *Oe Appt.=9/30/03	\$ 231,780	03/30/09	05/14/09	12/28/09	02/18/10	
08-09	09-31060	SHOPP	INY		Remodel Shop Facilities	\$ 2,483	11/21/08	01/13/10	03/01/10	04/06/10	
08-09	10-0N440	SHOPP	STA	108	Left Turn Channelization With New Signals	\$ 2,114	05/01/09	06/11/09	03/01/10	03/30/10	
08-09	12-0F920	SHOPP	ORA	5	Highway Planting Rehabilitation, Remove & Replace Dead Or Ill	\$ 2,718	07/08/08	10/15/09	02/22/10	03/25/10	
08-09	12-0G730	STIP	ORA	5	Provide Enhanced Gore Paving, Rock Blanket And Accent Planting	\$ 1,332	05/01/09	08/13/09	12/07/09	01/28/10	

\$ 555,177

Projects Bond allocation was delayed pending bond sales

FY CFD	D-EA	Pgm	Cty	Rte	Description	Value	Ready to List	Vote	Advertise	Bid Opening	Status
08-09	03-1A432	Bond RTE99	SUT	99	Widen To Provide 4 Lane Segment	\$ 73,126	06/26/09	01/13/10	02/22/10	03/24/10	Allocation delayed
08-09	03-2A690	Bond CMIA	NEV	49	Widen To 4 Lns With Cont Left Turn	\$ 21,000	05/05/09	01/13/10	02/22/10	03/23/10	Allocation delayed
08-09	05-0N250	Bond SHOPP	SCR	1	Construct Transportation Management System (Tms)	\$ 1,301	03/13/09	01/13/10	02/16/10	03/10/10	Allocation delayed
08-09	05-0N260	Bond SHOPP	MON	1	Construct Solar-Powered Transportation Management System	\$ 2,902	06/03/09	01/13/10	02/16/10	03/16/10	Allocation delayed
08-09	11-28930	Bond SHOPP	SD	5	Install Ramp Meters & Hov Lanes	\$ 6,500	06/29/09	01/13/10	02/22/10	03/25/10	Allocation delayed

\$ 104,829

Projects delivered early with with Future Year Funds

FY CFD	D-EA	Pgm	Cty	Rte	Description	Value	Ready to List	Vote	Advertise	Bid Opening	Status
07-08	06-48340	SHOPP	KER		Replace equipment shop and office	\$5,441	10/01/07				Fy 09-10 funds. (Reprogram balance amendment)
07-08	07-19963	STIP	LA	101	Widening of 2 US-101 off-ramps	\$8,136	05/15/08				FY 12/13 STIP funds

\$13,577

Projects delivered and not put out to bid yet

FY CFD	D-EA	Pgm	Cty	Rte	Description	Value	Ready to List	Vote	Advertise	Bid Opening	
08-09	03-0E870	STIP	YOL	5	Plant Establishment And Protection	\$ 500	11/26/08	09/10/09			
08-09	03-31800	SHOPP	NEV		Constr Resident Mechanic Facility (Bce-Osd)	\$ 2,814	01/29/09	01/13/10			
08-09	04-3S721	SHOPP	SOL	680	Replace Culvert, Backfill Sinkhole RSP	\$ 500	06/15/09	06/11/09			Redesign and drainage permit.
08-09	07-12184	Bond CMIA	LA	5	Const Hov Lane	\$ 150,000	06/29/09	Loc			Delivered with other funds. Fed auth, RW Cert 3W
08-09	07-1786A	STIP	LA	5	Modify Ic/Realign Ramps	\$ 11,000	06/29/09	10/15/09			Delivered list allocation
08-09	07-25060	PART	LA	210	Const. Soundwall With Masonry Block	\$ 21,097	11/14/08	Loc			
08-09	10-0G130 10-3A660 (3A66U)	STIP	MER	140	Replacing Bradley Oh Bridge Widen From 2 Lanes To 4 Lanes.	\$ 15,640	06/17/09	10/15/09			Fed auth, RW Cert 3, RR
		SHOPP			Bridge Replacement	\$ 17,696	06/17/09	10/15/09			

\$ 219,247

Final Environmental Document (FED) Milestone Delivery

First Quarter - 48 Planned Deliverables

D-EA	Pgm	Cty	Rte	Description	ED Type	
01-40280	SHOPP	MEN	101	Culvert Rehabilitation	Neg Dec	
02-1E210	SHOPP	TRI	299	Add Paved Shoulders	Cat Ex	
02-1E600	SHOPP	TRI	299	Bridge Maintenance	Cat Ex	
02-1E610	SHOPP	SHA	999	Treat Bridge Decks & Replace Joint	Cat Ex	
02-1E620	MTCE	SHA	005	Bridge Maintenance	Cat Ex	
02-1E630	SHOPP	SIS	999	Treat Bridge Decks & Replace Joint	Cat Ex	
02-1E670	MTCE	SHA	089	Bridge Maintenance	Cat Ex	
02-1E830	MTCE	LAS	395	Thin Blanket Overlay	Cat Ex	
02-1E850	MTCE	LAS	044	Thin Blanket Overlay	Cat Ex	
02-1E870	MTCE	PLU	070	Thin Blanket Overlay	Cat Ex	
02-27031	STIP	TRI	299	Upper Buckhorn Realignment	Env Imp	
02-2C950	SHOPP	SIS	096	Drainage System Restoration	Neg Dec	
02-32804	STIP	SHA	044	Install Landscaping And Irrigation	Neg Dec	
02-4C950	STIP	TRI	299	Traffic Calming Te	Cat Ex	
03-0E990	SHOPP	PLA	267	Repair Cut Slopes, Place Rsp, Culverts	Neg Dec	
03-0F640	SHOPP	BUT	162	Install Traffic Signal	Cat Ex	
03-0F910	SHOPP	SAC	016	Install Ground-In Rumble Strips	Cat Ex	
03-4E430	SHOPP	YUB	070	Thin Trees And Install Guardrail	Cat Ex	
04-15034	ARRA	SCL	280	Install & Implement Ramp Metering	Cat Ex	
04-15130	ARRA	SCL	280	Install And Implement Ramp Metering	Cat Ex	
04-1A521	TBSRA	CC	160	Seismic Retrofit Antioch Bridge	Env Imp	
04-1A522	TBSRA	SM	084	Seismic Retrofit Dumbarton Bridge	Env Imp	
04-1E720	MTCE	SM	092	Rubberized Hot Mix Asphalt Overlay	Cat Ex	
04-1E740	MTCE	SM	082	AC Resurfacing	Cat Ex	
04-26406	BOND	MRN	101	Construct NB Hov Lane	Env Imp	
04-26408	BOND	SON	101	Construct Interchange 101 Petaluma Blvd	Env Imp	
04-3A980	SHOPP	SCL	101	Bridge Rail Replacement/Upgrade	Cat Ex	
04-3S820	SHOPP	SM	084	Repair Slipout	Cat Ex	
04-4S130	SHOPP	SM	084	Storm Damage Repair / Slope	Cat Ex	
05-0G030	SHOPP	SLO	101	Highway Rehabilitation	Cat Ex	
05-0S210	MTCE	SB	001		Cat Ex	
05-0S220	MTCE	SB	154	OCAO Overlay	Cat Ex	
06-0J490	MTCE	KER	005	RHMA - Overlay	Cat Ex	
06-47100	BOND	MAD	099	Modify Interchange	Neg Dec	
08-0M860	MTCE	SBD	247	Place Seal Coat	Cat Ex	
08-0N120	MTCE	SBD	062	Place Seal Coat At Above Locations	Cat Ex	
08-0N130	MTCE	SBD	018	Place Seal Coat At Above Locations	Cat Ex	
08-0N300	MTCE	RIV	060	Cold Plane & Overlay, Rubberized AC	Cat Ex	
10-0A840	STIP	SJ	012	Operational Improvements	Neg Dec	
10-0N980	SHOPP	SJ	026	Install Traffic Signals'	Cat Ex	
10-0S520	MTCE	CAL	004	Chip Seal (Pme)	Cat Ex	
10-0T440	SHOPP	STA	005	Treat Bridge Decks; Replace Joint	Cat Ex	
10-0T960	MTCE	SJ	004	Rubberized Ac Overlay	Cat Ex	
11-29190	SHOPP	SD	015	Storm Water Mitigation Slope Repair	Cat Ex	
11-29900	SHOPP	IMP	111	Install Centerline Rumble Strip	Cat Ex	
11-2M020	SHOPP	SD	005	Treat Bridge Deck With Methacrylate	Cat Ex	
11-2M030	SHOPP	SD	005	Treat Bridge Deck With Methacrylate	Cat Ex	
11-2M040	MTCE	SD	005	Treat Bridge Deck With Methacrylate	Cat Ex	

Second Quarter - 48 Planned Deliverables

D-EA	Pgm	Cty	Rte	Description	ED Type	
01-39754	SHOPP	MEN	101	Decommission Existing Roadway	Cat Ex	
01-48280	SHOPP	VAR	000	Repair Bridge Decks	Cat Ex	
01-49040	SHOPP	HUM	299	Install Rumble Strips	Cat Ex	
01-49050	MTCE	HUM	101	Bonded Wearing Course	Cat Ex	
02-1E100	SHOPP	SHA	299	Increase Curve Radii, Widen Shoulders	Cat Ex	
02-2E060	SHOPP	TRI	036	Improve Curve, Widen Shoulders	Cat Ex	
03-0F110	PART	SUT	099	Expand Park And Ride Facility	Cat Ex	
03-0F580	SHOPP	SAC	080	Upgrade Weigh Station And CCTV	Cat Ex	★
03-1A731	SHOPP	ED	050	Storm Water Quality Improvements	Neg Dec	
03-1A732	SHOPP	ED	050	Storm Water Quality Improvements	Neg Dec	
03-1A842	SHOPP	ED	089	Storm Water Quality Improvements	Neg Dec	
03-1E14U	SHOPP	ED	050	Upgrade Rock Retaining Guard Wall	Neg Dec	
04-0A090	SHOPP	SOL	080	Lengthen On-Ramp, Widen Bridge.	Neg Dec	
04-0A790	SHOPP	CC	004	Upgrade Traffic Barrier, Guardrail	Cat Ex	
04-15340	ARRA	SM	280	Install Ramp Metering	Cat Ex	
04-1E600	MTCE	MRN	001	Bonded Wearing Course Overlay	Cat Ex	
04-1E730	MTCE	SON	001	Bonded Wearing Course Overlay	Cat Ex	
04-2A410	SHOPP	SM	001	Install Soft Median Barrier	Cat Ex	
04-3S830	SHOPP	SCL	017	Construct Headwall And Soil Wall	Cat Ex	★
04-42210	SHOPP	SON	001	Install Tie Back Wall	Cat Ex	
04-4S150	SHOPP	SM	280	Install Rsp	Cat Ex	
05-0N400	STIP	SLO	001	Transportation Enhancement	Neg Dec	
05-31580	BOND	MON	101	Construct New Interchange	Env Imp	
06-0G890	SHOPP	FRE	000	Remodel Or Replace Equipment Shop	Cat Ex	
06-0J520	SHOPP	KER	119	Widen Shoulders	Neg Dec	
06-0L740	MTCE	KER	065	Rubberized Hot Mix Asphalt Overlay	Cat Ex	
06-0L790	MTCE	FRE	168	Bonded Wearing Course Overlay	Cat Ex	★
06-48750	STIP	KIN	198	Reconstruct Interchange	Neg Dec	
07-26040	SHOPP	LA	039	Bridge Scour Mitigation	Neg Dec	
07-49160	STIP	LA	405	Construct South Half Interchange	Env Imp	★
08-0F630	PART	SBD	395	Widen Highway To 4 Lanes	Neg Dec	
08-33488	TCRP	RIV	215	Facilitate Managing Landscape	Cat Ex	
08-43890	SHOPP	SBD	178	Drainage Improvements	Neg Dec	★
09-34280	MTCE	MNO	395	Preventive Maintenance	Cat Ex	
10-0T420	SHOPP	MER	005	Treat Bridge Decks; Replace Joint	Cat Ex	
10-0T430	MTCE	SJ	005	Treat Bridge Decks; Replace Joint	Cat Ex	★
10-0T450	MTCE	SJ	004	Polyester Concrete Overlay 3 Bridges	Cat Ex	
10-0T830	MTCE	SJ	099	Treat Bridge Decks; Replace Joint	Cat Ex	
10-0T930	MTCE	AMA	088	Cured In Place Pipe Liner	Cat Ex	★
10-0U300	MTCE	STA	033	Drainage System Restoration	Cat Ex	
11-26400	SHOPP	IMP	008	Bridge Rehab With Seismic Retrofit	Cat Ex	
11-29780	SHOPP	SD	076	Install Traffic Signal & Widening	Cat Ex	
11-29850	SHOPP	SD	078	Install Centerline Rumble Strip	Cat Ex	
11-2M090	MTCE	SD	008	Repair PCC Slabs	Cat Ex	
12-0K250	MTCE	ORA	001	Full Removal/Repaint & Steel Repair	Cat Ex	★
12-0K590	MTCE	ORA	241	RHMA - Typ O Overlay	Cat Ex	★
12-0K640	MTCE	ORA	005	Replace Joint Expansion Units.	Cat Ex	★
12-0L060	MTCE	ORA	405	Pcc Profile Grinding	Cat Ex	★

★

Document Types

Cat Ex	Categorical Exemption
Env Imp	Environmental Impact Report
Neg Dec	Negative Declaration

Legend

	Completed
★	Completed Ahead of Planned Quarter
N	Not Needed due to Env Doc Change
P	Env Doc Done, Project Report Pending
	Behind Schedule
	To Be Completed
A	Delay Out of Year (see delay categories below)

Delay Categories

A	Optimistic Schedule
B	Environmental Document Change
C	Unanticipated Studies
D	Resource Issues
E	Late Alternative
F	Scope Change
G	External Reviews
H	Change Regulations

Final Environmental Document (FED) Milestone Delivery (page 2)

Third Quarter - 29 Planned Deliverables

D-EA	Pgm	Cty	Rte	Description	ED Type	
01-45090	SHOPP	HUM	169	Install Mbgr	Neg Dec	
01-46420	SHOPP	MEN	000	Reconstruct Guard Railing	Cat Ex	
01-46480	SHOPP	HUM	101	Staa Operational Improvement Project	Cat Ex	
01-47220	SHOPP	HUM	096	Reconstruct Roadway, Repair Slope	Cat Ex	
01-47550	SHOPP	HUM	036	Repair Storm Damage	Cat Ex	
01-48270	SHOPP	DN	199	Construct Cable Mesh Drapery System	Cat Ex	
02-2C221	SHOPP	MOD	299	Bridge Scour	Cat Ex	
02-2C222	SHOPP	SHA	299	Bridge Scour	Cat Ex	
02-2E000	SHOPP	PLU	070	Improve Curve, Widen Shoulders	Cat Ex	
02-4C401	STIP	SHA	005	Widen To 6 Lanes	Cat Ex	
03-0C470	SHOPP	YOL	016	Widen Sh & Intersec Improvemnt	Env Imp	★
04-01404	SHOPP	ALA	080	Construction South Yard Sfobb Mtce	Neg Dec	A
04-01407	SHOPP	ALA	080	Planting And Irrigation	Neg Dec	
04-2A440	SHOPP	SCL	152	Improve Sight Distance, Shoulders	Neg Dec	
04-2A620	SHOPP	SOL	012	Install Left Turn Pockets	Neg Dec	★
04-3A870	SHOPP	CC	680	Bridge Rehabilitation	Cat Ex	
04-3S900	SHOPP	MRN	001	Construct Tie-Back Wall	Cat Ex	
04-3S910	SHOPP	MRN	001	Construct Tie-Back Wall	Cat Ex	
04-4A070	BOND	ALA	580	Construct Eastbound Truck Climb Ln	Neg Dec	
04-4S110	SHOPP	SM	001	Install Rsp	Cat Ex	
05-0C640	STIP	SB	246	Passing Lanes, Operational Imp	Neg Dec	
05-0H371	STIP	SLO	101	Construct Auxiliary Lanes	Neg Dec	
06-0H180	SHOPP	KER	014	Bridge Replacement (Scour)		
08-0F660	SHOPP	SBD	247	Construct Shoulders, Various Loc	Neg Dec	
08-0G370	SHOPP	SBD	015	Seismic Retrofit	Cat Ex	
08-0G480	SHOPP	SBD	015	Seismic Retrofit Bridges	Cat Ex	
08-0L340	STIP	SBD	010	Corridor Visual Master Plan	Cat Ex	
10-0G800	SHOPP	SJ	012	Roadway Rehabilitation	Neg Dec	
10-41482	STIP	MER	099	Highway Planting And Irrigation	Neg Dec	

Fourth Quarter - 23 Planned Deliverables

D-EA	Pgm	Cty	Rte	Description	ED Type	
01-38572	SHOPP	MEN	1	Mitigation:Fish Passage/Culvert Rehab	Cat Ex	
01-46680	STIP	LAK	20	Construct Historic Interpretive Center	Cat Ex	
02-2C230	SHOPP	SHA	5	Seismic Retrofit	Cat Ex	
02-2C223	SHOPP	TEH	36	Bridge Scour	Cat Ex	
02-2E200	SHOPP	TRI	299	Improve Superelevation, Shoulders	Cat Ex	
02-37430	SHOPP	TRI	299	Rail Upgrade, Widen	Cat Ex	
04-1A551	SHOPP	SF	280	Replace Bridge Rails	Cat Ex	
04-2A250	SHOPP	SCL	152	Improve Sight Distance, Shoulders	Neg Dec	
04-2A430	SHOPP	SCL	9	Improve Sight Distance, Shoulders	Neg Dec	★
04-4A480	SHOPP	ALA	260	Repair Handrail And Sidewalk	Cat Ex	
05-49280	SHOPP	SLO	1	Realign Roadway	Env Imp	
06-0H170	SHOPP	FRE	180	Bridge Replacement		
06-0H940	SHOPP	FRE	168	Realign The Horizontal Curve		
06-44260	BOND	FRE	99	Widen 4-Lane Fwy To 6-Lane Fwy	Neg Dec	
07-26590	SHOPP	LA	101	Upgrade Bridge Rails	Neg Dec	★
07-27240	SHOPP	LA	5	Storm Water Source Control	Cat Ex	
07-27440	PART	LA	10	High Occupancy Toll Lanes	Neg Dec	
08-3401U	STIP	SBD	138	Widen To 4 Lns	Neg Dec	
09-28750	SHOPP	INY	190	Rockfall Mitigation	Neg Dec	
09-33400	STIP	INY	395	Historic Alignment Pullouts		
11-00270	SHOPP	SD	5	Construct Auxiliary Lanes/ Connector	Cat Ex	
11-07670	SHOPP	IMP		Construct Maintenance Station	Neg Dec	★
11-08163	PART	SD	805	Construct Managed Lanes-North	Neg Dec	

Document Types

Cat Ex	Categorical Exemption
Env Imp	Environmental Impact Report
Neg Dec	Negative Declaration

Legend

Completed
★ Completed Ahead of Planned Quarter
N Not Needed due to Env Doc Change
P Env Doc Done, Project Report Pending
Behind Schedule
To Be Completed
A Delay Out of Year (see delay categories below)

Delay Categories

A Optimistic Schedule
B Environmental Document Change
C Unanticipated Studies
D Resource Issues
E Late Alternative
F Scope Change
G External Reviews
H Change Regulations

Draft Environmental Document (DED) Milestone Delivery

First Quarter - 3 Planned DED Deliverables

D-EA	Pgm	Cty	Rte	Description	ED Type	
05-0C640	STIP	SB	246	Passing Lanes And Oper Imp	Neg Dec	■
08-0F660	SHOPP	SBD	247	Construct Shoulders at Various Loc	Neg Dec	■
08-43890	SHOPP	SBD	178	Drainage Improvements	Neg Dec	■

Second Quarter - 10 Planned DED Deliverables

D-EA	Pgm	Cty	Rte	Description	ED Type	
01-45090	SHOPP	HUM	169	Install Mbgr	Neg Dec	■
01-48270	SHOPP	DN	199	Construct Cable Mesh Drapery System	Neg Dec	■
03-1A843	SHOPP	ED	089	Storm Water Quality Improvements	Neg Dec	■
04-2A330	SHOPP	ALA	084	Improve Sight Distance, Shoulders	Neg Dec	★
04-2A430	SHOPP	SCL	009	Improve Sight Distance, Shoulders	Neg Dec	■
06-0H170	SHOPP	FRE	180	Bridge Replacement	Neg Dec	■
07-27440	PART	LA	010	High Occupancy Toll Lanes	Neg Dec	■
09-28750	SHOPP	INY	190	Rockfall Mitigation	Neg Dec	■
11-07670	SHOPP	IMP		Const Mtce Station	Neg Dec	★
11-08163	PART	SD	805	Managed Lanes North	Neg Dec	■

Third Quarter - 15 Planned DED Deliverables

D-EA	Pgm	Cty	Rte	Description	ED Type	
01-36432	SHOPP	MEN	20	Rehabilitate Drainage	Neg Dec	■
01-38572	SHOPP	MEN	1	Fish Passage/Culvert Rehab	Neg Dec	■
02-2C223	SHOPP	TEH	36	Bridge Scour	Neg Dec	■
03-1A845	SHOPP	ED	089	Storm Water Quality Improvements	Neg Dec	■
03-2C990	PART	SAC	5	Reconstruct Interchange	Env Imp	■
03-3E620	SHOPP	BUT	99	Replace Bridge (Scour)	Neg Dec	■
04-28120	STIP	NAP	29	Construct Southbound Flyover	Neg Dec	■
04-2A250	SHOPP	SCL	152	Improve Sight Distance	Neg Dec	■
06-0H940	SHOPP	FRE	168	Realign The Horizontal Curve	Neg Dec	■
06-0J040	SHOPP	KIN	41	Construct Left-Turn Lanes	Neg Dec	■
08-3401U	STIP	SBD	138	Widen To 4 Lns	Neg Dec	★
10-0P920	SHOPP	MPA	140	Clear Landslide	Neg Dec	■
11-05631	BOND	SD	11	Construct Freeway & Port Of Entry	Env Imp	■
11-23580	STIP	SD	5	Construct HOV Ln	Env Imp	■
11-25711	PART	SD	76	Construct 4 Lane Highway	Env Imp	■

Fourth Quarter - 6 Planned DED Deliverables

D-EA	Pgm	Cty	Rte	Description	ED Type	
01-47690	SHOPP	DN	101	Remove & Reconstruct Hinges	Neg Dec	■
02-2C112	SHOPP	TEH	099	Repair Bridge Scour	Neg Dec	■
03-1E510	SHOPP	BUT	070	Seismic Retrofit	Neg Dec	■
03-3C000	PART	SAC	005	Const Hov Lanes	Env Imp	★
05-0A050	SHOPP	SB	001	Reconstruct Slope Protection	Neg Dec	■
08-04351	STIP	SBD	58	Realign & Widen 2 To 4 Lane Expwy	Env Imp	■

Document Types

Cat Ex	Categorical Exemption
Env Imp	Environmental Impact Report
Neg Dec	Negative Declaration

■	Completed
★	Completed Ahead of Schedule
■	Behind Schedule
■	To Be Completed
A	Delay Out of Year (see delay categories below)

Delay Categories

A	Optimistic Schedule
B	Environmental Document Change
C	Unanticipated Studies
D	Resource Issues
E	Late Alternative
F	Scope Change
G	External Reviews
H	Change Regulations

Status Of Major Projects With R/W for the 09-10 FY (Dollars in Thousands)

Dist	Co	Rte	EA(s)	PPNO	Project Description	Cert Dates	Program Capital Amt	Total R/W Capital Project Budget (All Funds)	Total Current Project Estimate	FY 09-10 Allocation				FY Expenditures Detail by Qtr			
										Allocation FY	Total YTD Expenditures	% Allocation Expended	Allocation Remaining	1st Qtr Actual	2nd Qtr Actual	3rd Qtr Actual	4th Qtr Actual
01	MEN	101	262001	0125F	CONSTRUCT 4-LANE FREEWAY, PHASE 1	01/01/10	26,750	33,000	33,020	5,300	2,518	47.51%	2,782	80	2,438		
03	YOL	016	0C4701	8655	WIDEN SH & CONSTR LEFT TURN LANE RT TRN POCKETS, INTERSEC IMPROVEMNT	04/01/12	9,800	9,800	9,848	2,800	4	0.14%	2,796	0	4		
03	NEV	020	1A5301	3982	REALIGNMENT AND WIDENING ROADWAY	03/17/06	6,380	6,380	6,183	3,593	0	0.00%	3,593	0	0		
03	NEV	49	2A6900	4107	WIDEN TO 4 LNS WITH CONT LEFT TURN	04/01/09	9,000	9,000	6,720	1,181	698	59.10%	483	680	18		
03	YOL	5	374220	0301X	CONSTR N/B I5 TO S/B 113 CONNECTOR	07/01/10	2,926	7,730	7,730	2,496	50	2.00%	2,446	49	1		
04	ALA	880	165421	0040E	REPLACE BRIDGES, CONSTRUCT ROADWAY, RETAINING WALLS, AND PUMPING PLANT	06/18/08	20,107	48,607	29,307	3,566	2,770	77.68%	796	0	2,770		
04	NAP	012	264111	0367D	CONSTRUCT TWO ADDITIONAL LANES FOR THE EASTBOUND DIRECTION, ADD A	04/01/10	7,655	13,414	13,919	2,040	0	0.00%	2,040	0	0		
05	MON	101	0161E1	0058G	CONSTRUCT INTERCHANGES AND OPERATIONAL IMPROVEMENTS	04/15/10	50,475	64,147	64,147	5,098	8,914	174.85%	-3,816	176	8,738		
05	SLO	046	330721	0226C	CONVERT TO 4-LANE EXPRESSWAY	09/24/09	10,400	10,400	10,400	4,632	1,226	26.47%	3,406	1,126	100		
05	SBT	156	344900	0297	WIDEN 2 TO 4 LANES	01/16/12	14,636	14,636	13,480	3,630	0	0.00%	3,630	0	0		
06	KER	58	243401	0258	CONSTRUCT 4 LANE FREEWAY	06/15/00	11,306	11,306	11,306	1,215	209	17.20%	1,006	0	209		
06	TUL	216	430700	0106	WIDEN AND REALIGNMENT OF HOUSTON AVENUE (SR 216)	08/01/12	2,200	2,200	7,751	1,506	0	0.00%	1,506	0	0		
06	KER	046	442521	3386A	2-LN CONVENTIONAL TO 4-LN CONVENTIONAL - EXPRWY	03/19/10	10,603	10,603	10,603	9,339	5,021	53.76%	4,318	5,020	1		
07	VEN	101	107201	1200U	MODIFY IC *VCE*OVERSIGHT ONLY*PE=LO*RW:LMF	12/23/99	0	0	9,200	2,412	190	7.88%	2,222	61	129		
07	LA	5	121901	0158K	HOV LN *OE APPT.=9/30/03	03/30/09	10,900	39,000	39,000	1,162	58	4.99%	1,104	13	45		
07	LA	138	127271	0694Q	WIDEN CONVENTIONAL HIGHWAY (SEG 12) *SPLIT=1272U1	03/15/10	6,606	6,606	7,795	1,765	0	0.00%	1,765	0	0		
07	LA	30	172151	2022C	FREEWAY CONSTRUCTION	06/16/00	31,739	31,739	23,066	1,807	0	0.00%	1,807	0	0		
07	LA	005	2159C1	2808A	CARMENITA INTERCHANGE IMPROVEMENT *POR/=21590K*TCRP APP'D 7/6/01	05/18/10	37,263	168,330	168,330	11,987	11,512	96.04%	475	12	11,500		
08	SBD	215	007171		WIDEN FREEWAY AND CONSTRUCT NEW OVERPASSES	12/14/06	33,672	65,294	71,736	2,075	441	21.25%	1,634	397	44		
08	SBD	215	0071V0	0247P	ADD TWO HOV LANES AND OPERATIONAL IMPROVEMENTS	01/15/09	49,705	96,905	96,905	10,192	6,222	61.05%	3,970	4,505	1,717		

Dist	Co	Rte	EA(s)	PPNO	Project Description	Cert Dates	Program Capital Amt	Total R/W Capital Project Budget (All Funds)	Total Current Project Estimate	Allocation FY	Total YTD Expenditures	% Allocation Expended	Allocation Remaining	1st Qtr Actual	2nd Qtr Actual	3rd Qtr Actual	4th Qtr Actual	
08	SBD	015	355560	0174L	ADD N/B MIXED FLOW LANE W/AUX LANE. RECON "D" & "E" ST ICS & STODDARD	03/07/11	13,245	13,245	21,400	12,605	893	7.08%	11,712	0	893			
08	SBD	210	443111	0193N	CONST 6 LANE FREEWAY & 2 HOV LNS & CAMPUS AVE UC	07/01/00	0	0	133,834	3,000	326	10.87%	2,674	12	314			
08	SBD	215	444071	0194Q	POR SEG 11/210 PROJECT REPLACE 27TH ST OC CONSTRUCT RAMPS IMPROVE LOCA	11/24/08	8,437	8,437	8,332	3,336	1,150	34.47%	2,186	1,150	0			
08	RIV	010	456001	0007D	CONST BOB HOPE DR EXT W/NEW DIAMOD IC	04/01/09	14,400	14,400	16,735	5,271	2,442	46.33%	2,829	2,011	431			
10	STA	219	0A8721	9940C	WIDEN TO 4 LANES AND INTERSECTION IMPROVEMENTS	04/01/10	14,760	17,000	17,000	13,054	1,137	8.71%	11,917	741	396			
10	TUO	108	340421	0021B	CONSTRUCT STAGE 2 OF SONORA BYPASS	03/30/10	19,200	19,200	12,707	9,163	1,798	19.62%	7,365	1,009	789			
10	MER	99	415701	5414	4E TO 6F ON 8F R/W ALIGNMENT	01/02/10	24,900	24,900	24,900	16,401	1,051	6.41%	15,350	96	955			
11	SD	005	0301U1	0129X	WIDEN FREEWAY AND BRIDGES	08/06/01	15,763	16,863	29,538	3,553	11	0.31%	3,542	0	11			
11	SD	905	091821	0374K	CONSTRUCT NEW FREEWAY - PHASE 1A	05/18/07	50,000	219,677	218,891	2,528	1,195	47.27%	1,333	1,189	6			
11	IMP	078	167891	0021G	CONSTRUCT FOUR-LANE EXPRESSWAY (STAGE 3)	4//2010	17,078	15,460	17,078	4,335	2,690	62.05%	1,645	2,690	0			
12	ORA	090	056201	4434	CONSTRUCT GRADE SEPARATION	05/01/04	29,691	29,691	35,963	1,804	86	4.77%	1,718	78	8			
12	ORA	055	0H2101	3577B	REPAIR DAMAGED SLOPE	10/17/06	10,200	10,200	28,606	3,903	289	7.40%	3,614	2	287			
											156,749	52,901	33.75%	103,848	21,097	31,804	0	0
											Projected Quarterly Expenditure Plan				23,512	32,917	48,592	51,727
											Historical Percentage for Quarterly Commitments				15%	21%	31%	33%
											Actual Percentage Committed FYTD				13%	20%		



Division of Construction
CONTRACT ADMINISTRATION
Q2 Fiscal Year 2009/10 (\$ in Millions)



Construction Contracts - Quarterly Status Report^a

	Q2 08/09		Q3 08/09		Q4 08/09		Q1 09/10		Q2 09/10	
	Number	Value								
1. Ongoing Contracts @ Beginning of Quarter	646	\$ 9,937	549	\$ 9,722	607	\$ 9,502	732	\$ 9,429	676	\$ 9,550
2. New Contracts this Quarter	106	692	164	357	249	697	158	658	70	862
3. Accepted Contracts this Quarter	203	907	106	577	124	770	214	537	206	856
Ongoing Contracts @ End of Quarter (1+2-3)	549	\$ 9,722	607	\$ 9,502	732	\$ 9,429	676	\$ 9,550	540	\$ 9,556
4. Accepted Contracts @ Beginning of Quarter	815	\$ 5,056	933	\$ 5,688	892	\$ 4,141	871	\$ 4,536	972	\$ 4,588
5. Accepted Contracts this Quarter	203	907	106	577	124	770	214	537	206	856
6. Contracts Closed this Quarter	83	251	145	2,016	141	265	111	483	150	955
7. New Contracts in Arbitration this Quarter	2	24	2	108	4	110	2	2	4	74
Accepted Contracts @ End of Quarter (4+5-6-7) ^b	933	\$ 5,688	892	\$ 4,141	871	\$ 4,536	972	\$ 4,588	1,024	\$ 4,415
Accepted Contracts with claims only @ End of Quarter	432	\$ 4,839	440	\$ 3,278	429	\$ 3,844	411	\$ 3,716	446	\$ 3,200
8. Contracts in Arbitration @ Beginning of Quarter ^c	37	\$ 468	37	\$ 379	36	\$ 464	38	\$ 568	35	\$ 447
9. New Contracts in Arbitration this Quarter	2	24	2	108	4	110	2	2	4	74
10. Contracts with Arbitration Settlements/Awards this Quarter	2	113	3	23	2	6	5	123	2	17
Contracts in Arbitration @ End of Quarter (8+9-10)	37	\$ 379	36	\$ 464	38	\$ 568	35	\$ 447	37	\$ 504

^a Quarterly figures updated to reflect revised or new data at the end of the current quarter.

^b Accepted Contracts with close-out activities in progress. Contracts in Arbitration are not included.

^c A Contractor may file for Arbitration 240 days after project acceptance, or within 90 days after final determinations on claims have been made. Contractors must file within 90 days after the Department makes a final determination on claims or lose opportunity for arbitration. (Contractors have 180 days to file on Contracts that were approved prior to January 1, 1999.)

Total dollar amount of claims at end of current quarter = \$345M

Total dollar amount filed for in arbitration at end of current quarter = \$53M
