

Job Stamp
04-0120F4
SFOBB SAS

Construction Calendar	419
Project working days no.	619
Date	02/05/2008
Inspectors Hours	Start 5:30 Stop 21:30
Shift Hours	Start 6:00 Stop 23:00

**Description of Operation:**

- See Lalit Mathur's diary for ABF labor, equipment, materials, weather, and comments.
- Daily activity of contractors
  - Concrete is poured at south side of W2 from 7:30 to 14:15.

Fig 1 (around 7:30, first truck on site)



Fig 2 (around 11:00)



Fig 3 (around 15:00)


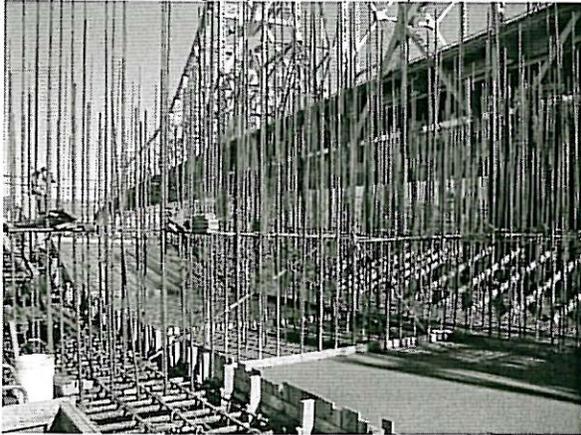


Fig 4 (around 15:00)

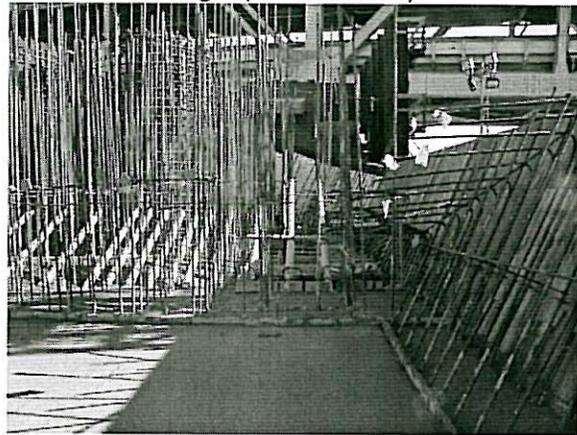

- Blankets are placed for curing purpose from 19:00.

Fig 5 (east slope)


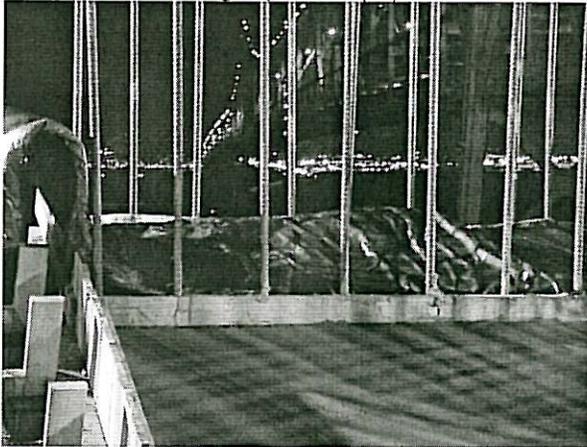


Fig 6 (west side)

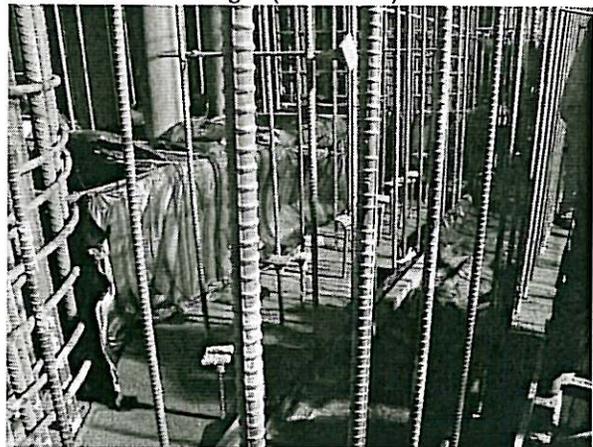

➤ Note

- See Art Pannu and Lalit Mathur's diary for collecting tags, field calculation and field tests
- Accident at east bound of Bay bridge around 8:30

Fig 7




- concretes come out through holes

Fig 8




- Concrete crack starts to occur around 18:00.

Fig 9

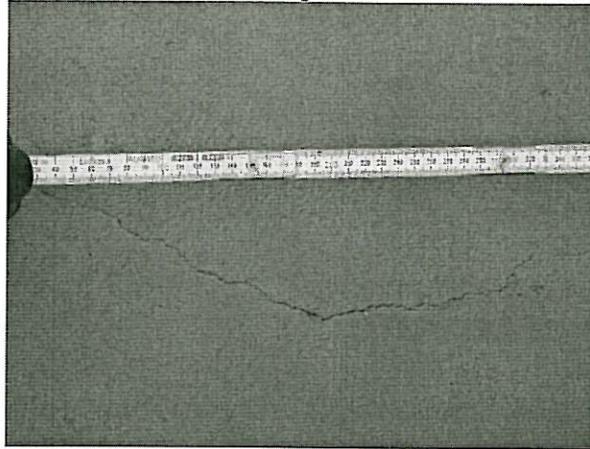

- Blanket placed doesn't cover the concrete properly around column cages and cable tie down.

Fig 10

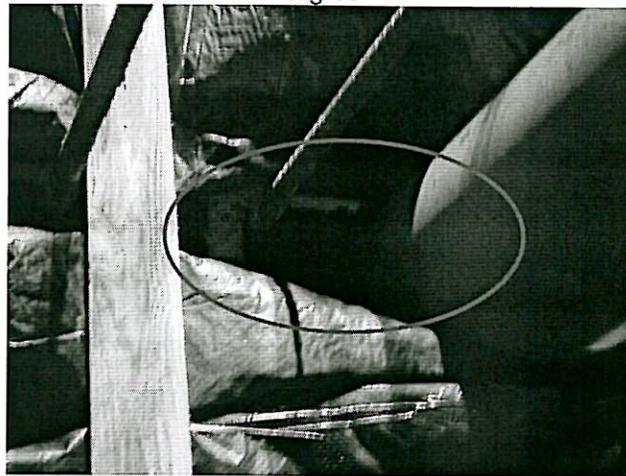

- 7 hours overtime due to field work.

Inspector:

SeongHyeok Song

Trans Engineer (D)/Asst. Struct. Rep
