

Job Stamp  
04-0120F4  
SFOBB SAS

Const. Calendar: 437  
Project Work Day No.: 647  
Date: 02/23/2008  
Inspectors Start 09:00 Stop 11:30  
Hours  
Shift Hours 08:40 12:40

ASSISTANT RESIDENT ENGINEER'S CONTRACTOR - ABFJV, Sub RPS

EQUIPMENT AND/OR LABOR:			HOURS - ITEM NO.										REMARKS				
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)	#38 Str. Concrete, Bridge												IDLE OR DOWN	Name	Contractor
1	1	Pile Driver Lead/Foreman	5													Leo Vega	ABF
2	1	Pile Driver	5													Tony Creighton	ABF
3	1	Pile Driver	5													George McNeil	ABF
4	1	Pile Driver	5													Luke Paulk	ABF
5	1	Pile Driver J/M	5													Audre Hudson	ABF
6	1	Elevator Operator	5													Howard Schroyer	ABF
7	1	Surveyor	5													James Allen	ABF
8	1	Surveyor Apprentice	5													Chris Roberts	ABF
	1	Liebeherr Crane LR 1300												5		330 T	ABF
	1	1" Man Lift S-125												5			Hertz Rental
	1	Lincoln Vantage Welding M/C 768-50-4005												5			ABF, deck NE
	1	Lincoln Vantage Welding M/C 768-50-4014												5			Hertz Rental
	1	MQ Power Generator 220	5														ABF Main power
	1	MQ Whisper Watt 7000 549-07-5006												5			ABF
	1	MQ Whisper Watt 7000 549-20-4007												5			ABF
	1	Ingersoll Rand Air Compressor 20-2183												5			ABF central
	1	Ingersoll Rand Air Compressor 006-18-4293												5			ABF
	1	Ingersoll Rand Air Compressor 006-18-4297												5			ABF
	1	Ditch Witch FX60 500 Gal 679-09-2004												5			ABF Hertz Rental
	1	Genie TML-4000N Flood Lights												5			ABF Hertz Rental deckNW
	1	Genie TML-4000N Flood Lights												5			ABF Hertz Rental deckSW
	1	Genie 541-4000N Flood Lights 536-40-4839												5			ABF Hertz Rental deck E
	1	Genie 541-4000N Flood Lights 536-40-4843												5			ABF Hertz Rental deck SE
	1	Genie TML-4000N Flood Lights												5			ABF Hertz Rental

1	Genie TML-4000N Flood Lights											5		ABF Hertz Rental
1	Genie TML-4000N Flood Lights											5		ABF Hertz Rental
1	Forklift Hertz Rental 544D-10											5		ABF
1	Pickup											5		ABF
1	Elevator	5												ABF

**Weather:** Overcast with mild to cool temperature - Hi 53 F Lo 44 F (per weather.com forecast)

**Description of Operations @ W2 Cap Beam:**

ABF

- Surveyors established 0.5m offset points for the void area formwork.
- Removed curing mats placed on the center base slab section and cleaned up debris.
- Completed removing formwork for the jacking saddle.


**Office Work:**

- Wrote today's diary.

**Inspector:**


Matt Bruce     *Matt Bruce*     Transportation Engineer (D)

EA	04-0120F4
Co-Rte-KP (PM)	SF-080-13.2/13.9 (8.2/8.7)
Structure Rep.	Rick Morrow

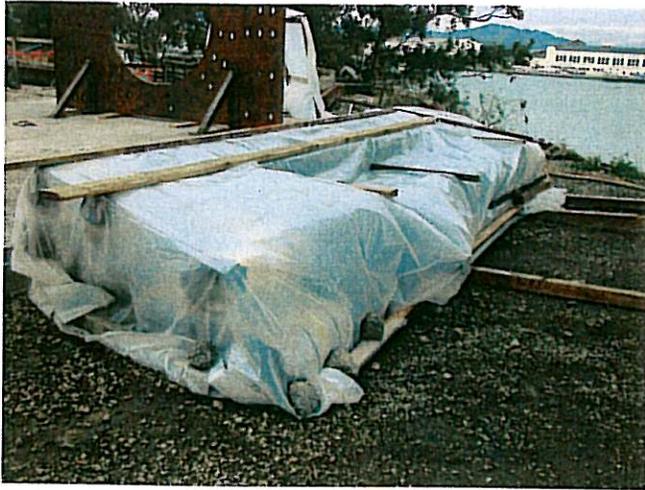

File Name:	DSC00911
Date:	02-23-08
By Int:	M Bruce
Description: Macalloy rods covered with plastic, which was secured down with rocks, rebar, and lumber.	

File Name:	DSC00999
Date:	02-23-08
By Int:	M Bruce
Description: Surface cracks on the east sloped portion of the center base slab.	

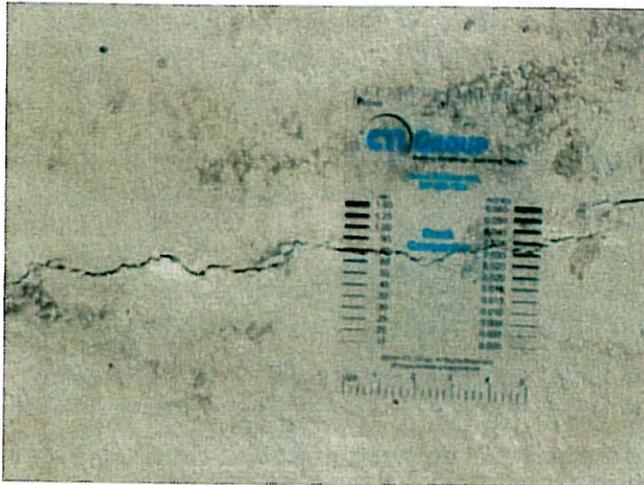

File Name:	DSC01001
Date:	02-23-08
By Int:	M Bruce
Description: Crack found on the east slope which was 0.80mm using a crack comparator.	

File Name:	DSC01005
Date:	02-23-08
By Int:	M Bruce
Description: Removal of the jacking saddle forms.	
