

Job Stamp 04-0120F4 SFOBB SAS

Const. Calendar:	481			
Project Work Day No.:	691			
Date	04/07/2008			
Inspectors	Start	10:00	Stop	11:30
Hours		12:40		14:30
Shift Hours		07:00		15:30

ASSISTANT RESIDENT ENGINEER'S **CONTRACTOR – ABFJV, Sub RPS**

Weather: Sunny with mild temperature - Hi 64 F Lo 45 F (per weather.com forecast)

Description of Operations @ W2 Cap Beam:

ABF

- Miscellaneous cleanup and material mobilization.
- Installed channel strongbacks for north and south transverse diaphragm blockouts.
- Continued to install form ties in the transverse diaphragm.
- Installed ladder rungs for top deck access opening in the south, see sheet 454 for details.
- Surveyors set points for transverse tendons 1-8 on the west forms and set offset points for the east wall rebar for RPS.

RPS

- Finished installing #25 horizontal ties in the east wall.
- Removed some of the 29HVTD02 vertical bars over the access opening blockouts in the transverse diaphragm, see sheets 497S2, and 497S3.
- Placed 25V11 vertical bars in the east wall see sheet 497S15.
- Placed longitudinal bars 4-25L11L20 thru 4-25L15L20, see sheets 497S4R1 and 497S5.


Office Work:

- Attended weekly staff (Temp. Towers and Caps) meeting at 8:00am.
- Reviewed plans for W2 cap beam.
- Wrote today's diary.

Inspector:

Matt Bruce Matt Bruce Transportation Engineer (D)

EA	04-0120F4
Co-Rte-KP (PM)	SF-080-13.2/13.9 (8.2/8.7)
Structure Rep.	Rick Morrow

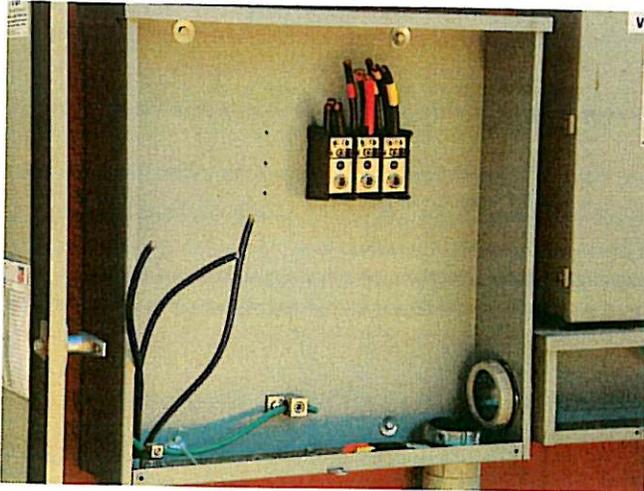

File Name:	DSC01327
Date:	04-07-08
By Int:	D Chung

Description: ABFs operations were limited with the main power source down as copper wire was stolen the previous night.

File Name:	DSC01337
Date:	04-07-08
By Int:	D Chung

Description: East wall rebar placement in the north void area.



File Name:	DSC01345
Date:	04-07-08
By Int:	D Chung

Description: Installation of the ladder rungs for the access opening from the top deck on the south side of the W2 cap beam.



File Name:	DSC01342
Date:	04-07-08
By Int:	D Chung

Description: First day of placing reinforcement in the longitudinal diaphragm.
