

Job Stamp 04-0120F4 SFOBB SAS

Const. Calendar:	490			
Project Work Day No.:	700			
Date	04/16/2008			
Inspectors	Start	12:15	Stop	14:10
Hours				
Shift Hours		07:00		15:30

ASSISTANT RESIDENT ENGINEER'S **CONTRACTOR – ABFJV, Sub RPS**

Weather: Sunny with mild temperature - Hi 73 F Lo 48 F (per weather.com forecast)

Description of Operations @ W2 Cap Beam:

ABF

- Erected/closed southeast longitudinal diaphragm forms.
- Erected/closed southeast wall forms.
- Completed installation of form ties in the northwest wall and began installing form ties on the southwest wall.
- Miscellaneous work and cleanup around forms erected/closed today.

RPS

- Completed placement of 29HT02, and 29HT03 bars for the jacking saddle in the longitudinal diaphragm, see sheets 497S6R1 and 497S8R1.
- Completed adjusting 6-36HV02 bars in the longitudinal diaphragm, see sheets 497S6R1 and 497S8R1.


Office Work:

- Attended weekly Team Concrete meeting with ABF and TY-Lin at 8:00am.
- Reviewed plans for W2 cap beam.
- Wrote today's diary.

Inspector:

Matt Bruce *Matt Bruce* Transportation Engineer (D)

EA	04-0120F4
Co-Rte-KP (PM)	SF-080-13.2/13.9 (8.2/8.7)
Structure Rep.	Rick Morrow

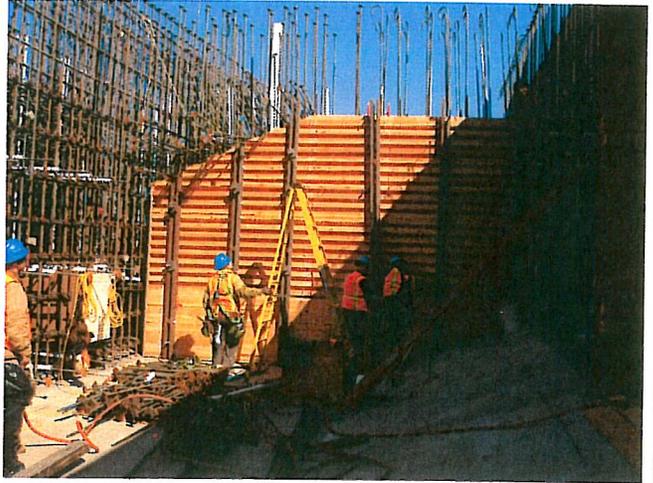

File Name:	DSC01435
Date:	04-16-08
By Int:	D Chung

Description: Placement of 29HT02, and 29HT03 bars for the jacking saddle in the longitudinal diaphragm

File Name:	DSC01439
Date:	04-16-08
By Int:	D Chung

Description: Southeast longitudinal diaphragm forms.



File Name:	DSC01458
Date:	04-16-08
By Int:	M Bruce

Description: Southeast wall form erection.
