

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 476
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 676
Form HC-10A (Rev. 6/80)	04-0120F4	Date	04/02/2008

01

Inspectors Hours	Start	0700	Stop	1530
Shift Hours	Start	0630	Stop	1500

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR - ABFJV

HOURS - ITEM NO.												REMARKS		
EQUIPMENT AND/OR LABOR:			48 - Bar Reinforcing Steel (Bridge)								IDLE OR DOWN	Name Contractor		
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)										Name	Contractor	
		Regional Steel												
1	1	Superintendent	8									Gaige, Lance	RSC	
2	1	Foreman	0									Van Brusselen, Jon	RSC	
3	1	Ironworker	0									Jobe, Jason	RSC	
4	1	Ironworker	8									Manzano, Jose	RSC	
5	1	Ironworker	0									Lopez, Jorge	RSC	
6	1	Ironworker	8									Greenlee, Tim	RSC	
7	1	Ironworker	0									Rodriguez, Ernesto	RSC	
8	1	Ironworker	0									Gomez, Daniel	RSC	
9	1	Ironworker	0									Balderrama, Julio	RSC	
10	1	Ironworker	0									Ortiz, Roberto	RSC	
11	1	Ironworker	0									Mortenson, Kurt	RSC	
12	1	Ironworker	8									Bell, Joe	RSC	
13	1	Ironworker	0									Vasquez, Reynaldo	RSC	
14	1	Ironworker	0									Stockton, Luke	RSC	
15	1	Ironworker	0									Quiroz, Victor	RSC	
16	1	Ironworker	0									Raprasnussen, John	RSC	
17	1	Ironworker	8									Leon, Moises	RSC	

Weather: Partly cloudy, mild, wet ground, Hi 60 F Lo 46 F.

Description of Operation:

ABF

See L. Mathur's diary for labor, equipment and daily activities. Also see M. Bruce's diary for additional comments.

REC'D *08 MAY-31 #004963


Daily for Regional Steel

Continue installing horizontal #36L15-L8T41 bars in transverse diaphragm wall.
Started placing #25VTDO1 and #29VTDO1-DO2 bars in transverse diaphragm wall.
Start installing horizontal ties in transverse diaphragm wall.


NOTES:

Inspector:

Pamela Gagnier



Trans Engineer (C)/Asst. Struct. Rep

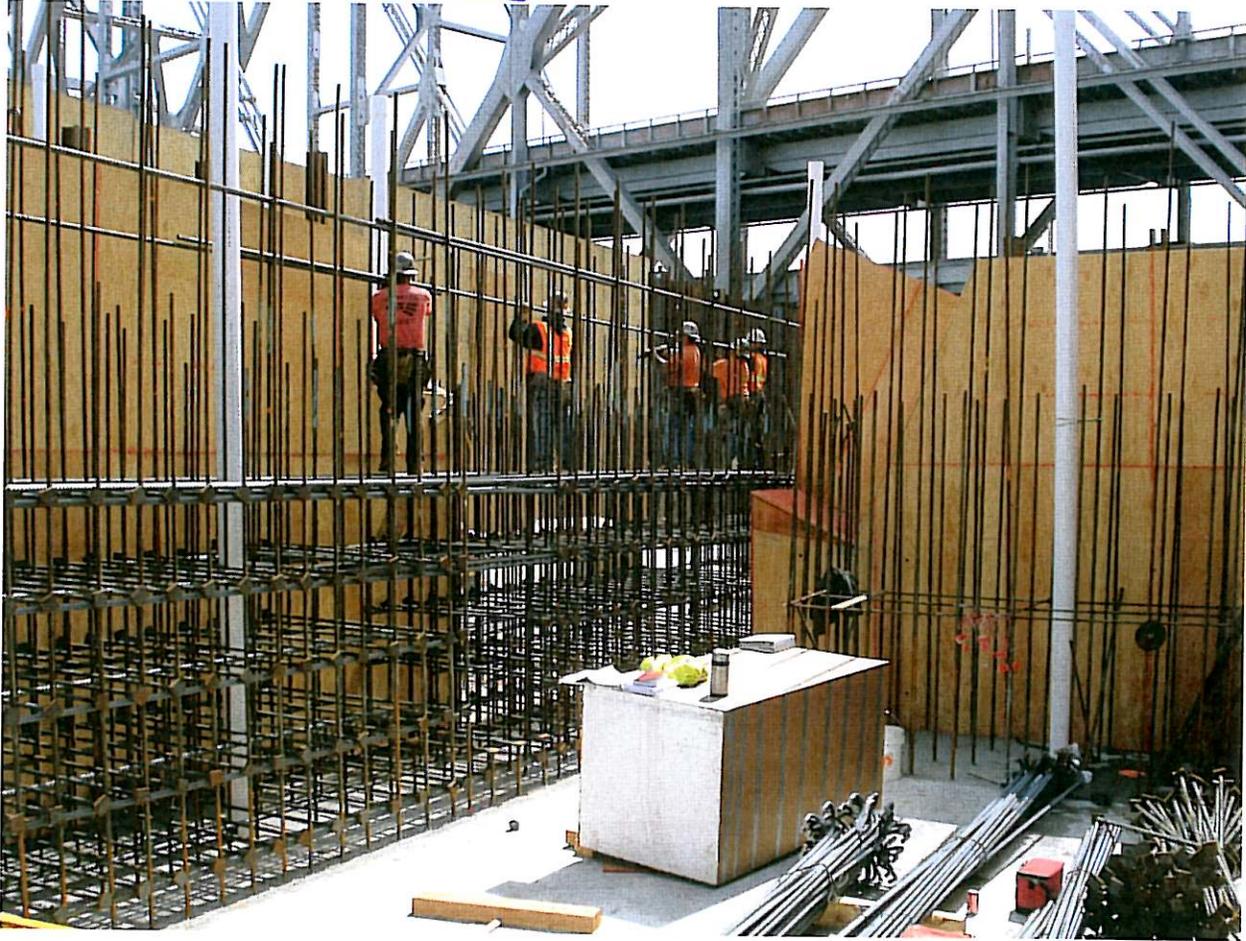

Installing #36L8-L15T41 bars in transverse wall.



Placing #25VTDO1 and #29VTDO2 bars in transverse diaphragm wall.



Horizontal ties transverse wall.
