


STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION
SCHEDULER WEEKLY FIELD REPORT
Larry Gustafson – Senior Scheduler

Week Ending 06-20-08

Tuesday June 17, 2008 – Clear, Warm, Calm

- A1, A2, B1, and B2 (shown below) as well as A3, A4 B3, and B4 foundations have been completed since early June

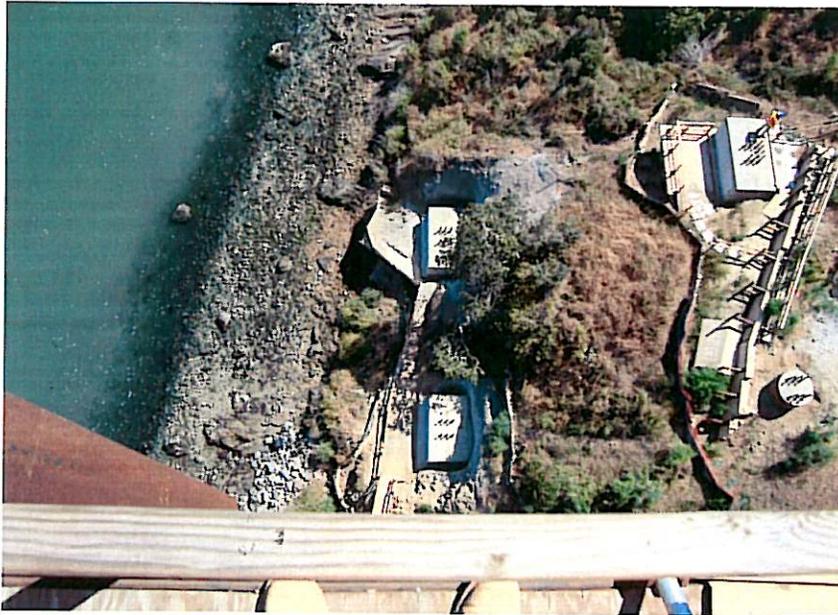

- W2
 - Forming for pour 3 continues



- **Rebar and PT Duct installation continues**
 - **All four Macalloy rod assemblies have been lowered, threads tested satisfactorily and placed back into position.**
-
- **TEMP TOWER “C” Area**



- **Work in “C” area has not yet commenced as of this date**



- **Monitoring devices continue in place in window sills at Torpedo Factory during pile drilling and driving operations**

- **TEMP TOWERS “D” – No pile driving observed on this date.**
- **E2 FALSEWORK continues in background**



Friday June 20, 2008 Sunny, Clear, Hot

- W2
 - Forming for pour 3 lost deck continuing



- **Rebar & PT Ducts continue**



- **Torpedo Factory Roof adjacent to TT “C” – observed Traylor Dutra personnel discussing commencement of work.**
- **Note TEMP TOWER “D” offshore – no observed pile driving progress since prior to Tuesday 6/17/08.**



E2

- **E2 falsework continues – see photo below**

