

STATE OF CALIFORNIA  
DEPARTMENT OF TRANSPORTATION  
Contract 0120F4 – SAS SFOBB  
Larry Gustafson – Senior Scheduler

Week Ending 6-27-08

Tuesday June 24, 2008 Hazy Sun (Fires in Northern California) Warm, Calm

- Site Work at TT “C” not yet started
- Pile Driving in progress at TT “D” South




- E2 – Falsework erection continues



REC'D '08 JUL-10 #005543

- **Forming on False deck for Pour 3 continues**

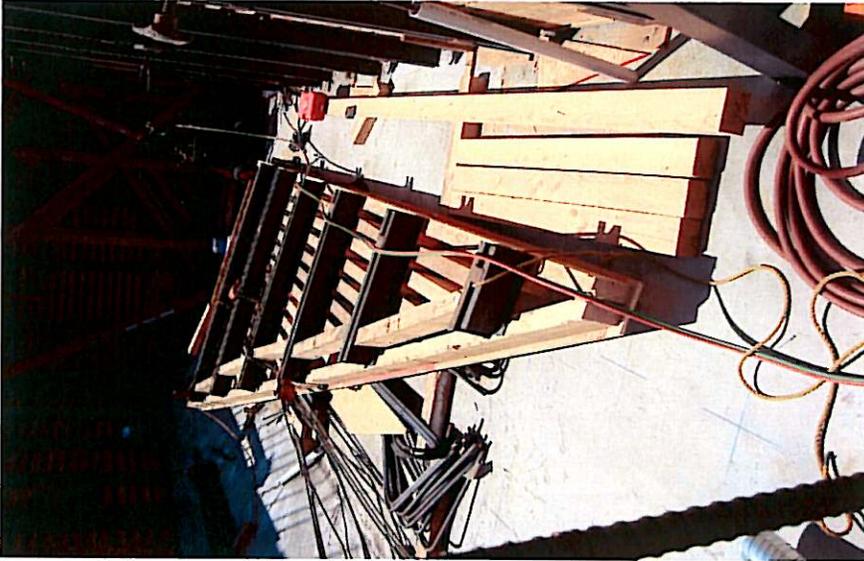

- **Miscellaneous**

**Assembling Manatowac 4100 Crane on East Side of W2. Will be moved to West side to assist in W2 construction. Liebherr 1300 Crane to be moved to East side.**



**Thursday June 26, 2008 Overcast, Windy Cold at 10:00 AM**

- **Sitework has not started at TT “C.”**
- **TT “D” North – North Driving Frame Beams B-1 in place**



- **Work in progress at TT “D” North Driving Frame**



## Western Gull Nesting in South B-1



- E2- Falsework erection continues



- W2 False Deck Forming Continues

