

*dfm*

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 555
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 755
Form HC-10A (Rev. 6/80)	04-0120F4	Date	06/20/2008

Inspectors Hours	Start	0630	Stop	1500
Shift Hours	Start	0630	Stop	1500

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR – ABFJV

HOURS - ITEM NO.													REMARKS	
EQUIPMENT AND/OR LABOR:			Item 48 – Bar Reinforcing Steel (Bridge)	CCO 34S1 – Cutting Vertical Bar	CCO 34S1 – Survey PT Ducts							IDLE OR DOWN	Name Contractor	
Equ. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)  Regional Steel											Name	Contractor
1	1	General Foreman	0	0									Bobnaes, Bob	RSC
2	1	Assistant General Foreman	0	8									Bell, Joe	RSC
3	1	Foreman	0	8									Greenlee, Tim	RSC
4	1	Ironworker	0	0									Ortiz, Lucino	RSC
5	1	Ironworker	0	8									Gomez, Daniel	RSC
6	1	Ironworker	0	8									Quiroz, Fermin	RSC
7	1	Ironworker	0	8									Arroyo, Fidel	RSC
8	1	Ironworker	0	8									Quiroz, Victor	RSC

Weather: Clear, sunny, hot, dry soil, Hi 89 F Lo 65 F.

**Description of Operation:**

ABF

- See L. Mathur's diary for labor, equipment and daily activities.

Daily for Regional Steel

- Torque T-heads on field cut vertical rebar in columns on north side.
- Relocating/tie hoops north side per previous layout.
- Profiling ducts south side (T. Greenlee & V. Quiroz) with M. Bruce (CT)
- Also see M. Bruce's diary for additional information.

RECT\*08 JUL-22 H005743

NOTES:

- M. Bruce notified ABF/RSC that he would not provide QC on the duct profile/rebar work. Is requesting an ABF representative direct RSC to correct/make changes to duct/rebar within column region.
- RSC replaced 3 t-heads and re-mushroomed 1 field cut vertical t-head on the north side.
- Torque wrench used 2007/253086


- Torqued – 18 t-heads WSE  
15 t-heads WSW  
12 t-heads WNE

Office


- Wrote diaries.
- Check email.

**Inspector:**

Pamela Gagnier



Trans Engineer (C)/Asst. Struct. Rep

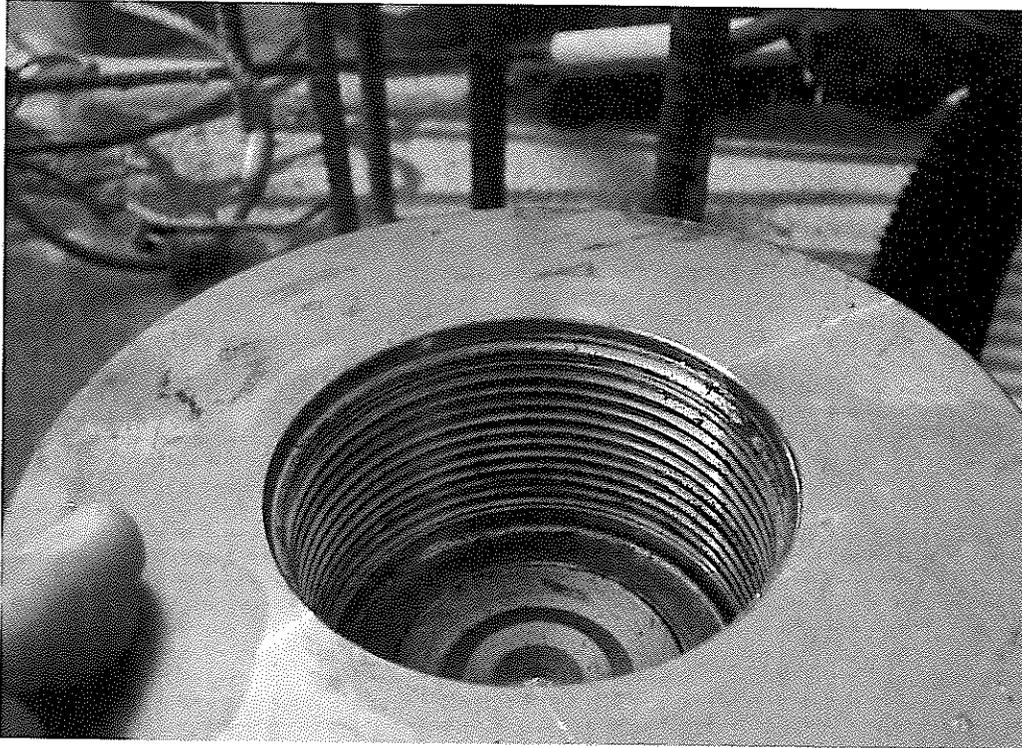

Replaced damaged t-head – threads stripped. North side.

FIELD AUTHORIZATION FOR WORK TO BE PERFORMED

WORK ORDER 4039

TO: REINFORCING, POST-TENSIONING SERVICES INC./REGIONAL STEEL CORP.

Job Name: SFOBB SAS W2 Date Performed 6-20-03 Job No. 2306

Location: \_\_\_\_\_ Contractor American Bridge / Floor

YOU ARE HEREBY AUTHORIZED TO PROCEED WITH THE FOLLOWING EXTRA WORK

Description of work to be performed: [ ] F.O.B. [ ] Installed Cost Code \_\_\_\_\_

Replace ducts on south Pier  
Relocate hoops and torque T-heads on north Pier

Reference Drawing No. \_\_\_\_\_

Employee Name	Craft	Sub	Straight Time		Overtime		Premium Time	
			Hours		Hours		Hours	
Joe Bell			8					
Alberto Quiroz			8					
Fidel Arroyo			8					
Daniel Gomez			8					
Fernan Quiroz			8					
Tim Greenlee			8					
			<u>48</u>					

Material Description	Quantity

Equipment	Hours

The Above Record is complete and correct.

Date 7-1-03 Accepted by: [Signature] Contractor's Representative Calltrans Rep Title TEC

[Signature]  
 Reinforcing, Post-Tensioning Services Inc./Regional Steel Corp. Representative

Contr. Ref. No.

Craft Designation: G.F. (General Foreman) J.W. (Journeyman Ironworker)  
 OPR (Operator) APP. (Apprentice)
