

gkm

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 574
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 774
Form HC-10A (Rev. 6/80)	04-0120F4	Date	07/09/2008

Inspectors Hours	Start	0630	Stop	1500
Shift Hours	Start	0630	Stop	1500

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR – ABFJV

HOURS - ITEM NO.													REMARKS		
EQUIPMENT AND/OR LABOR:			Item 48 – Bar Reinforcing Steel (Bridge)	CCO 34S1 – Cutting Vertical Bar	CCO 34S1 – Survey PT Ducts								IDLE OR DOWN	Name	Contractor
Equ. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)													
		Regional Steel													
1	1	General Foreman	8											Bobnaes, Bob	RSC
2	1	Assistant General Foreman	0											Bell, Joe	RSC
3	1	Foreman	8											Greenlee, Tim	RSC
4	1	Ironworker	8											Ortiz, Lucino	RSC
5	1	Ironworker	0											Garnita, Alejandro	RSC
6	1	Ironworker	8											Quiroz, Fermin	RSC
7	1	Ironworker	0											Arroyo, Fidel	RSC
8	1	Ironworker	8											Enrique, Jose	RSC
9	1	Ironworker	8											Franco, Jose	RSC
10	1	Ironworker	8											Quiroz, Victor	RSC

Weather: Sunny, hot, breezy, dry soil, Hi 80 F Lo 63 F.

Description of Operation:

ABF

- See L. Mathur's diary for labor, equipment and daily activities.

Daily for Regional Steel

- Installed L-bars in ESE & ESW per RFI 659R00.
- Laid out L-bars for WSW & WNW per RFI 659R00.
- Laid out T-bars between ENE & ENW per RFI 659R00.
- Tied L & T bars previously installed on south side.

NOTES:

- RSC needs to order additional L&T bars.


REC'D \*08 JUL-22 #005813

Office


- Wrote diaries.
- Attended weekly concrete meeting.
- Check email.

**Inspector:**

Pamela Gagnier



Trans Engineer (C)/Asst. Struct. Rep

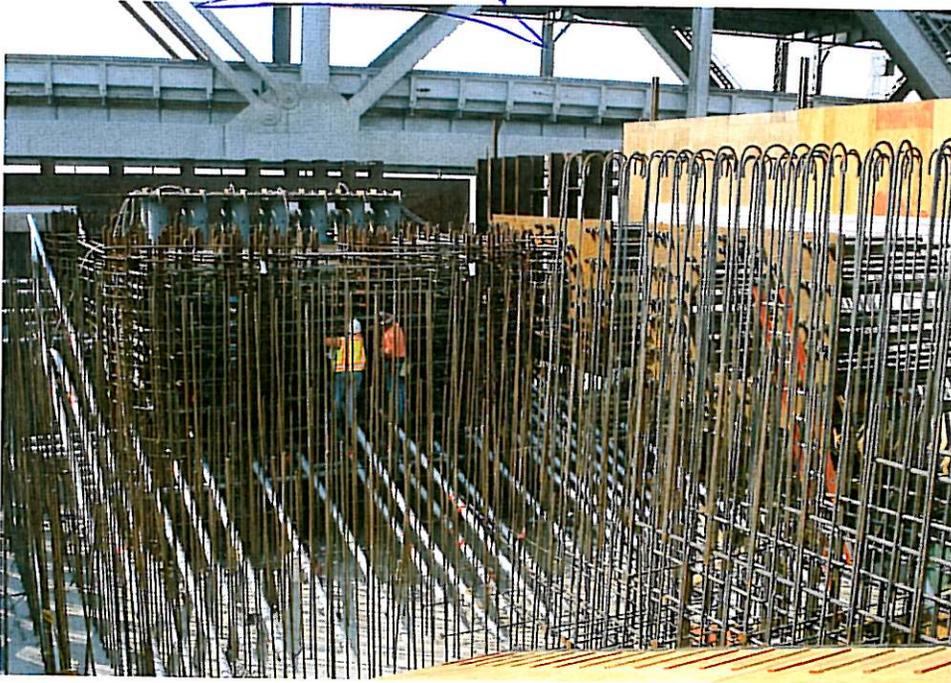

Laid out T-bars between ENE & ENW per RFI 659R00.
