

okm

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 541
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 741
Form HC-10A (Rev. 6/80)	04-0120F4	Date	06/06/2008

Inspectors Hours	Start	0630	Stop	1500
Shift Hours	Start	0630	Stop	1500

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR – ABFJV

HOURS - ITEM NO.											REMARKS	
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)	Item 48 – Bar Reinforcing Steel (Bridge)	CCO 34S1 – Cutting Vertical Bar						IDLE OR DOWN	Name Contractor	
											Name	Contractor
1	1	General Foreman	0	8							Bobnaes, Bob	RSC
2	1	Assistant General Foreman	0	0							Bell, Joe	RSC
3	1	Foreman	0	8							Greenlee, Tim	RSC
4	1	Ironworker	0	0							Raprasnussen, John	RSC
5	1	Ironworker	0	8							Gomez, Daniel	RSC
6	1	Ironworker	0	8							Quiroz, Victor	RSC

Weather: Sunny, clear, cold, dry soil, Hi 77 F Lo 53 F.

Description of Operation:

ABF

- See L. Mathur's diary for labor, equipment and daily activities.

Daily for Regional Steel

- Continue removing cut vertical rebar on the north side.
- Finished prepping for t-head installation on south side. This includes moving hoops up/down, cutting one bar in pair ~7" lower than bar to have t-head and re-cutting bar for t-head with smooth level cut.
- Start prepping for t-head installation on north side. This includes moving hoops up/down, cutting one bar in pair ~7" lower than bar to have t-head and re-cutting bar for t-head with smooth level cut.
- Finished cutting vertical rebar on south side.


NOTES:

Requested from Chuck Kanapicki paperwork to certify qualifications for ironworkers to perform mushroom head and install t-head on field cut vertical rebar. Paper work sent via email however is incorrect. Requested correct paperwork.

Office


Prepared safety presentation for next weeks meeting.  
Wrote diaries.  
Check email.  
1 hour sick leave family.

**Inspector:**

Pamela Gagnier  Trans Engineer (C)/Asst. Struct. Rep



Prepared for t-head vertical rebar in south side piles.

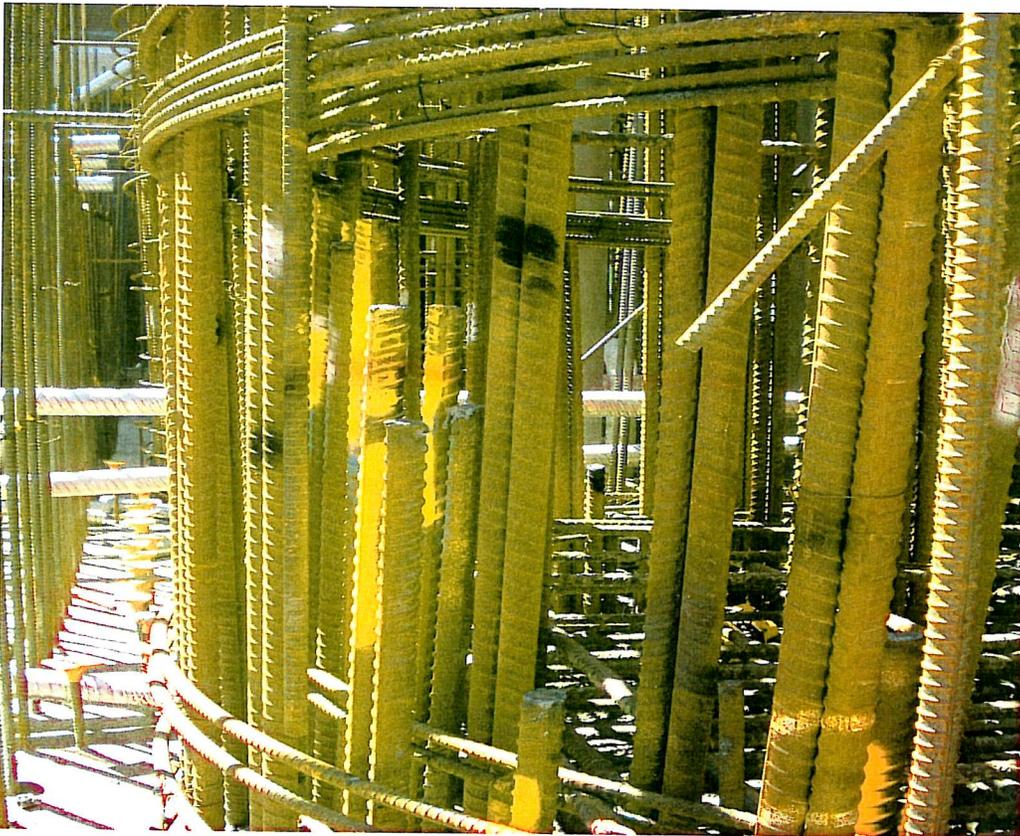

Prepared for t-head vertical rebar in south side piles.

