

AKM

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 544
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 744
Form HC-10A (Rev. 6/80)	04-0120F4	Date	06/09/2008

Inspectors Hours	Start	0630	Stop	1500
Shift Hours	Start	0630	Stop	1500

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR – ABFJV

HOURS - ITEM NO.												REMARKS	
Equip. #	NO. OF MEN	DESCRIPTION (Of Equipment or Labor) Regional Steel	Item 48 - Bar Reinforcing Steel (Bridge)	CCO 34S1 - Cutting Vertical Bar							IDLE OR DOWN	Name Contractor	
												Name	Contractor
1	1	General Foreman	8	0								Bobnaes, Bob	RSC
2	1	Assistant General Foreman	0	0								Bell, Joe	RSC
3	1	Foreman	8	0								Greenlee, Tim	RSC
4	1	Ironworker	0	0								Raprasnussen, John	RSC
5	1	Ironworker	8	0								Gomez, Daniel	RSC
6	1	Ironworker	8	0								Quiroz, Victor	RSC

Weather: Sunny, clear, hot, dry soil, Hi 77 F Lo 53 F.

Description of Operation:

ABF

- See L. Mathur's diary for labor, equipment and daily activities.

Daily for Regional Steel

- Installing hairpins in south transverse wall. Per conversation with T. Greenlee.
- Installing vertical rebar in south transverse wall. Per conversation with T. Greenlee.
- Also see M. Bruce's diary for additional information.

NOTES:

Requested from Chuck Kanapicki paperwork to certify qualifications for ironworkers to perform mushroom head and install t-head 500/551 on field cut vertical rebar. Paper work sent via email however is incorrect. Requested correct paperwork.

Danny with RSC contacted me to discuss required paperwork to certify qualifications for ironworkers (see above) I explain should be identical paperwork per submittal 293R0. T. Greenlee will be only qualified to torque t-heads in addition D. Gomez, V. Quiroz and T. Greenlee will all be certified to perform mushroom head procedure. RSC intention is to submit official and unofficial paperwork by 6/10/08 and deliver equipment. Wants to start t heading

@ own risk if paperwork not approved on Wednesday 6/11/08. I agreed if paperwork submitted then can start work @ own risk.


Office

Spent day in office working on:


- Safety presentation for next weeks meeting.
- Estimate 26.
- Wrote diaries.
- Check email.

Inspector:

Pamela Gagnier



Trans Engineer (C)/Asst. Struct. Rep

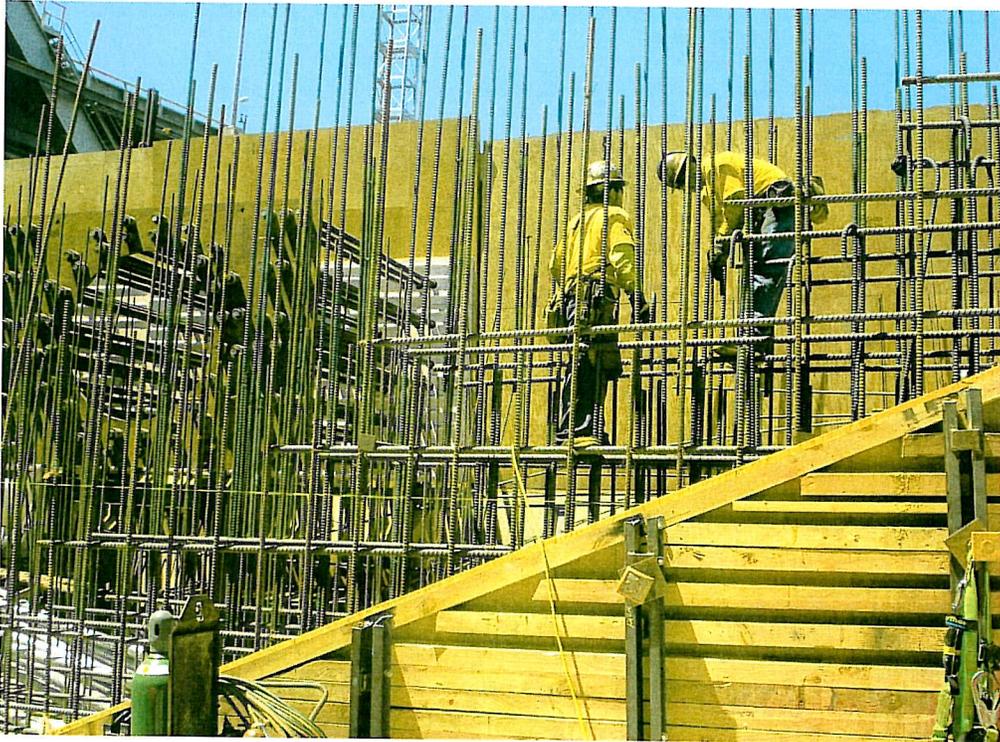

Installing vertical candy cane rebar in south transverse wall.



Installing vertical candy cane rebar in south transverse wall.
