

Job Stamp 04-0120F4 SFOBB SAS

Const. Calendar:	609			
Project Work Day No.:	819			
Date	08/13/2008			
Inspectors	Start	09:20	Stop	15:20
Hours				
Shift Hours		07:00		15:30

ASSISTANT RESIDENT ENGINEER'S CONTRACTOR – ABFJV, Sub RPS

Weather: Sunny with mild temperature and westerly breezes - Hi 85F Lo 59F (per weather.com forecast)

Description of Operations @ W2 Cap Beam:

ABF

- Began connecting water cooling system hoses to the PVC pipes in the east wall and to the manifolds located on the northwest quadrant void area sloped forms.
- Continued placing 50mm polystyrene blockout for W2W deviation saddle grout pad.
- Installed additional tie-rods with bearing plates in the south bulkhead.
- Continued to clean the soffit and the pour 2 construction joint for pour 3 scheduled next Thursday.
- Installed chamfer strip and 2"x4" screed on the west and east walls.
- Built support frame for the ironworkers to place the tails of the #43 transverse bars.

RPS

- Removed the remaining #43 bars previously mobilized on the top of pour 3 rebar to the ground.
- Continued to mushroomhead the #43 bars in the horizontal position with the male coupler for the ultimate butt splice already on the bar. General Foreman Bob Bogneas heated the bar and ran the hydraulic pump while Tim Greenlee placed the jack on the bar. See Lalit and Damon's diary for details on the mushroomheading operation the samples selected for QC/QA testing.
- Began to place 43L1T01* through 43L1T06* (bottom transverse bar) within and past the pour 3 limits.

Surveying Work:

- Began to shoot pour 3 perimeter elevations on the south end with Damon Brown. The south bulkhead forms were approximately 25mm lower than the bottom transverse bar of 43L1T01* through 43L1T06*. ABF foreman Nigel Lohse informed Damon prior to shooting the elevations which was confirmed after the surveying was completed.

Office Work:


- Attended weekly Team Concrete meeting with ABF and TY-Lin at 8:00am.
- Wrote today's diary.

Inspector:

Matt Bruce Matt Bruce Transportation Engineer (D)

REC'D *08 SEP-06 #006518

EA	04-0120F4
Co-Rte-KP (PM)	SF-080-13.2/13.9 (8.2/8.7)
Structure Rep.	Rick Morrow


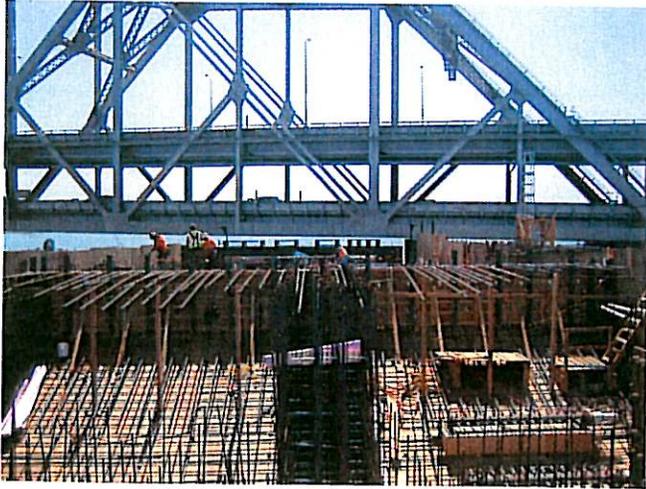


File Name:	Aug-13-2008 W2 Cap 003
Date:	08-13-08
By Int:	M Bruce

Description: Construction progress for Pour 3 to date looking south from the north cable tie-down pipes.

File Name:	Aug-13-2008 W2 Cap 006
Date:	08-13-08
By Int:	M Bruce

Description: Mushroomheading operation looking down to the ground from the W2 falsework.

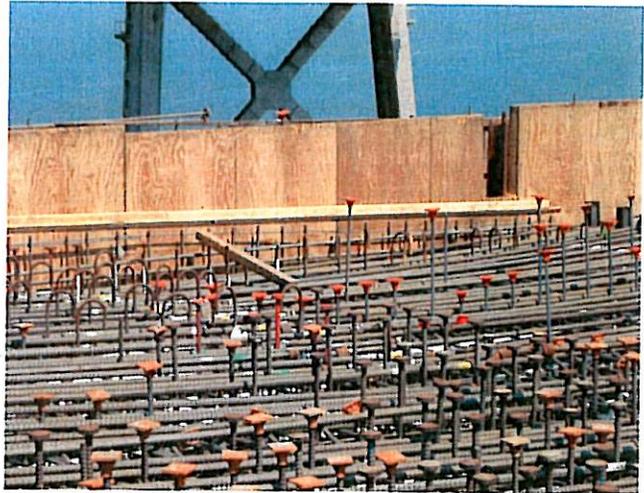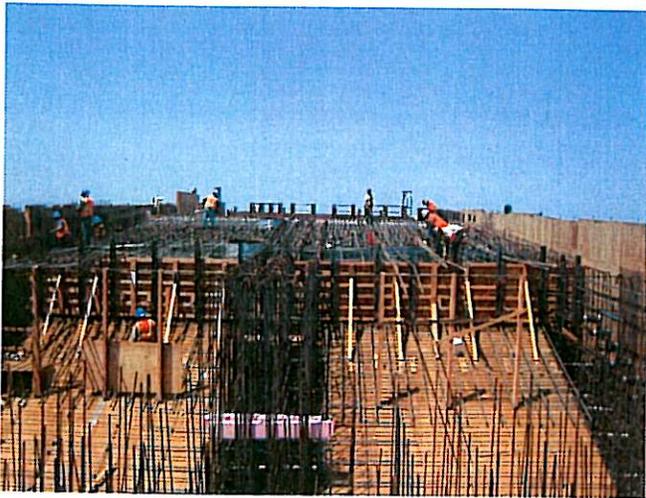

File Name:	Aug-13-2008 W2 Cap 009
Date:	08-13-08
By Int:	M Bruce

Description: Construction progress for Pour 3 to date looking north from the south cable tie-down pipes.

File Name:	Aug-13-2008 W2 Cap 010
Date:	08-13-08
By Int:	M Bruce

Description: Chamfer strip and 2"x4" screed on the east wall.
