

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 587
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 787
Form HC-10A (Rev. 6/80)	04-0120F4	Date	07/22/2008

Inspectors Hours	Start	0630	Stop	1700
Shift Hours	Start	0630	Stop	1700

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR – ABFJV

HOURS - ITEM NO.											REMARKS		
Equ ip. #	NO. M E E N	DESCRIPTION  (Of Equipment or Labor)  Regional Steel	Item 48 – Bar Reinforcing Steel (Bridge)	CCO 34S1 – Cutting Vertical Bar	CCO 34S1 – Survey PT Ducts						IDLE OR DOWN	Name Contractor	
												Name	Contractor
1	1	General Foreman	4									Bognaes, Bob	RSC
2	1	Assistant General Foreman	0									Bell, Joe	RSC
3	1	Foreman	3.5									Greenlee, Tim	RSC
4	1	Ironworker	0									Ortiz, Lucino	RSC
5	1	Ironworker	0									Garnita, Alejandro	RSC
6	1	Ironworker	0									Quiroz, Fermin	RSC
7	1	Ironworker	0									Arroyo, Fidel	RSC
8	1	Ironworker	0									Enrique, Jose	RSC
9	1	Ironworker	0									Franco, Jose	RSC
10	1	Ironworker	3.5									Quiroz, Victor	RSC

Weather: Overcast (am), partly cloudy (pm), mild, breezy, dry soil, Hi 66 F Lo 52 F.

Description of Operation:

ABF

- See L. Mathur's diary for labor, equipment and daily activities.
- 2 OT Hour Activities
  - \* Continue to erect falsework form bents in northwest void quadrant.
  - \* Installing cooling pipes for pour 3 in lower longitudinal wall and lower east wall.
  - \* Welding slope form braces on north west wall.
  - \* Cleaning rebar pieces and debri from inside of forms.

Daily for Regional Steel

- T. Greenlee & V. Quiroz cut vertical t-heads and candy canes embedded in concrete at the wrong elevation per RFI 1437R00.

NOTES:


- RSC only worked 3.5 hours. No work to do per B. Bognaes and will not return until Monday, July 28, 2008.
- Cut approximately 28 candy canes in east interior wall.
- Cut approximately 20-candy canes & t-heads in longitudinal wall east of transverse wall.
- Cut approximately 31-candy canes & t-heads in transverse wall south of longitudinal wall.
- Cut approximately 4 candy canes in west wall south of longitudinal wall.
- Work 2 hours OT to cover ABF fieldwork.

Office

- Wrote diaries.
- Check email.

**Inspector:**


Pamela Gagnier



Trans Engineer (C)/Asst. Struct. Rep



Cut vertical candy canes per RFI 1437 – transverse wall south side of longitudinal wall.

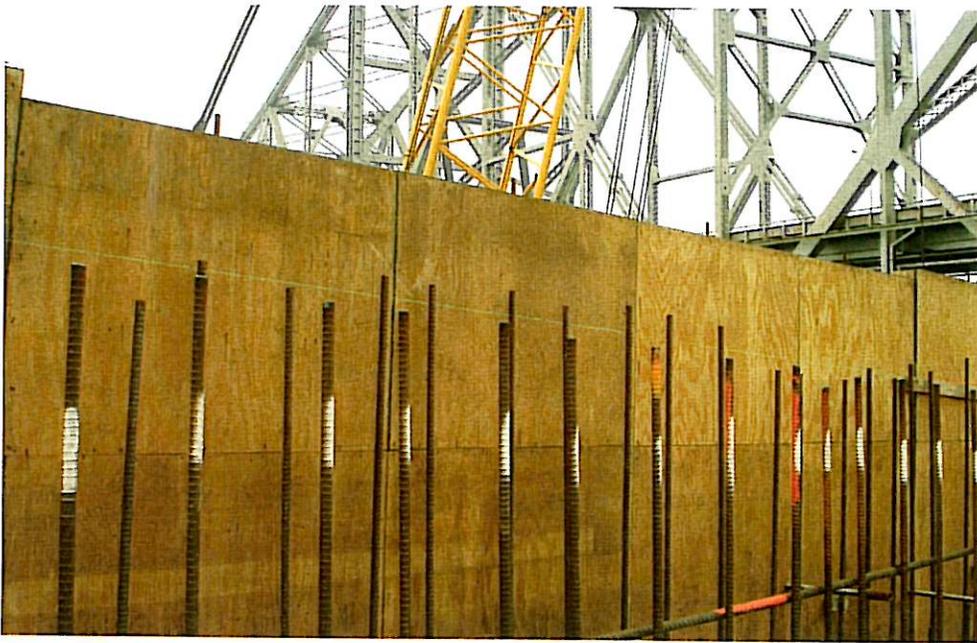

Cut vertical candy canes per RFI 1437 – east wall north of longitudinal wall.



Cut vertical candy canes & T-heads per RFI 1437 – transverse wall south of longitudinal wall.
