

STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION
Contract 0120F – SFOBB – SAS Superstructure

Larry Gustafson – Senior Scheduler

Week Ending 2008-09-19

Tuesday September 16, 2008 – Observation via Engineer’s Boat between 09:30 and 12:00
Noon : Partly overcast, Light Wind, Cool

- E2 – Building PT Duct Assembly at Pier 7



REC'D '08 SEP-22 #006649

E2 Bulkhead Form Panels at Pier 7



- **E2 Cross Beam now being serviced by 2 Cranes**



Added crane on barge to South of E2




Flying Rebar and PT Ducts



Installing rebar – note vertical PT Ducts in place



Rebar Mechanical connection

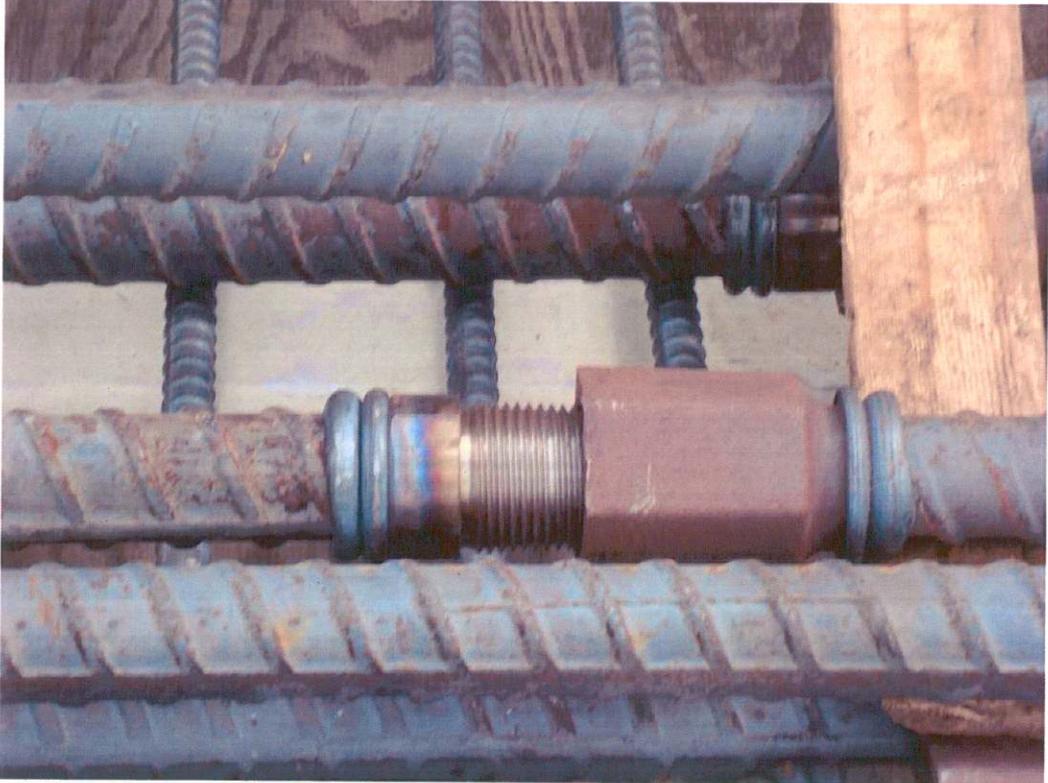

- Temporary Tower "D" Grout operation shut down awaiting approval of SWPPP



TT "D" View from E2



- **Temporary Tower “C” Area – No observed activity – North Area**



TT Area “C” - No observed activity South Area



- W2 – Truss W3 – W4 being on “1” Line being installed



Thursday September 18, 2008 Observation from Yerba Buena Island between 1300 and 1400. Clear, Warm, Calm at sea level, wind at top of W2


- **E2 – View from top of W2 – 2 Cranes servicing rebar and PT Dicts.**



- **TT “D” View from top of W2 (no identified activities)**



• Area "C" – Poured CIDH
North Area

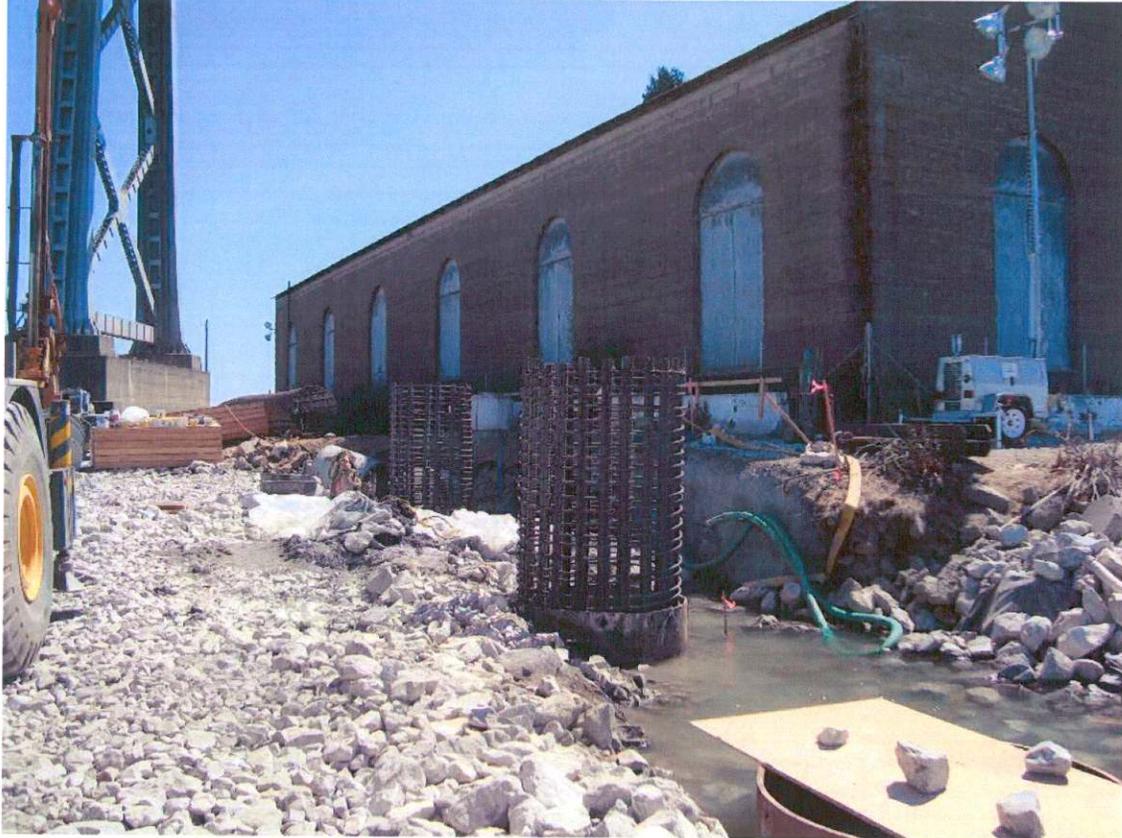

South Area




- W2

Fabbing Bulkhead forms



Placing inserts



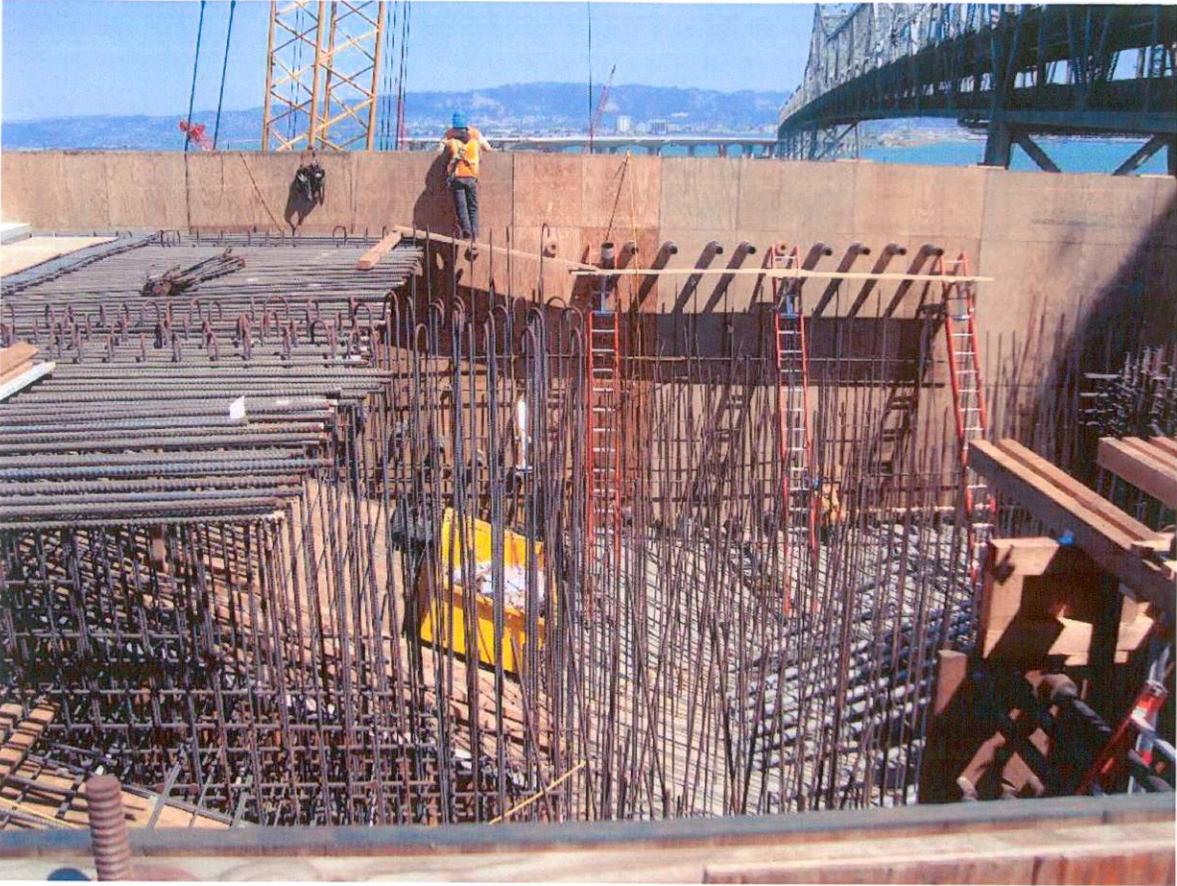

• TT AB West Area - Both (W3-W4) trusses in place



Bolting continues

