

Job Stamp:  
04-SF-80-13.2/13.9 04-0120F4  
SFOBB SAS  
San Francisco Co. in San Francisco  
Fm 0.6 km to 1.3 km East of Yerba Buena  
Tunnel East Portal

Report No. 7-day const. cal.: 595  
Project work day: 805

Date the Shift Began: 7/30/08

NIGHTWORK WEDNESDAY

Shift Hrs Start 6:30 Stop 15:00  
Engineer's Hrs Start 7:00 Stop 15:30

**ASSISTANT RESIDENT ENGINEER'S DAILY**

**BRIDGE**

**REPORT**

Location: W2 Cap Beam	Weather: cloudy
Remark: ironwork/manhole void	HI 68F/Lo 57F

Description of Operation:  
ABF - set manhole blockout in northwest void.  
RPS - continue ironwork. Place #25 bars through intermediate transverse diaphragm.

		HOURS - ITEM NO.						CONTRACTORS		
EQUIPMENT AND/OR LABOR:		38	48	133				Prime	American Bridge / Fluor JV	(P)
EQPT. NO.	NO. MEN	DESCRIPTION (Of Equipment or Labor)	RT	RT	RT			Sub #1	Regional	(1)
								Sub #2		(2)
								Sub #3		(3)
								Sub #4		(4)
								Sub #5		(5)
								REMARKS		
								Name	Classification	Prime / Sub


For equipment and personnel hours, please see LALIT MATHUR'S diaries.

Weekly mtg with ABF

In the southwest void area, I noticed two panels that have excessive negative undulations (DSC02173). Normally, the weight of the ironwork would press these down but in this case the undulations were stiff enough to resist my weight. I notified Nigel (ABF foreman) and asked him to secure these panels. He acknowledged me and said that Jesse (ABF carpenter) has this as an item on his punchlist. 10:44  
ABF has set the manhole blockout - corrugated steel tube with shear lags at the top perimeter - for the northwest void (DSC02171).  
ABF has completed plumbing the external forms on the west face by the Hinge at the E-line - started yesterday (DSC02169).

#43 bars were not started by RPS as planned. Ironworkers continued to place #25 bars on the bottom mat. They have placed #25 bars for both northeast and southeast voids. They are moving forward with the southwest void.

brackets used to tie forms to vertical member

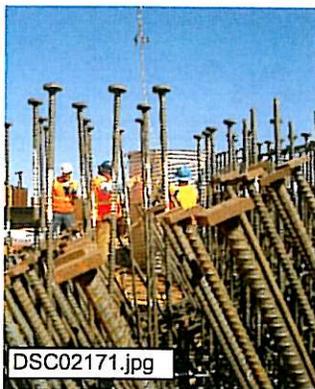

excessive undulation



08DCT-01 #006793

Materials:

Insp. Hrs.	
REG: 8.0	INTERMITTENT
OT:	INSPECTION

*David Chung*  
DAVID CHUNG

TE/CT  
Title
