

Job Stamp:
04-SF-80-13.2/13.9 04-0120F4
SFOBB SAS
San Francisco Co. in San Francisco
Fm 0.6 km to 1.3 km East of Yerba Buena
Tunnel East Portal

Report No. 7-day const. cal.: 623
Project work day: 833

Date the Shift Began: 8/27/08

NIGHTWORK WEDNESDAY

Shift Hrs Start 6:30 Stop 15:00
Engineer's Hrs Start 6:50 Stop 15:20

TOLL PROGRAM/DIST. 4 CONSTR.

ASSISTANT RESIDENT ENGINEER'S DAILY BRIDGE REPORT

Location: E2 Cross Beam/Pier 7
Remark: formwork/ironwork
Weather: clear/warm
Hi 83F/Lo 61F

Description of Operation:
ABF - continue formwork for PT blockouts at Pier 7/continue layout of HS rods and lay out donuts

EQUIPMENT AND/OR LABOR:			HOURS - ITEM NO.						CONTRACTORS		
EQPT. NO.	NO. MEN	DESCRIPTION (Of Equipment or Labor)	Structural Concrete, Bridge		Construction Surveying		IDLE OR DOWN/ ELSEWHERE	Name	Classification	Prime / Sub	
			RT	OT	RT	OT					RT
								Prime	American Bridge / Fluor JV	(P)	
								Sub #1		(1)	
								Sub #2		(2)	
								Sub #3		(3)	
								Sub #4		(4)	
								Sub #5		(5)	
	1	Foreman	8.00				Pier 7	Karl Nisley	Pilebutt	P	
	1	Journeyman	8.00				Pier 7	Jason Matlock	Pilebutt	P	
	1	Journeyman	8.00				Pier 7	Edward Mendoza	Pilebutt	P	
	1	Apprentice	8.00				Pier 7	Richie Yambao	Pilebutt	P	
	1	Foreman	8.00				E2	Ben Neal	Pilebutt	P	
	1	Journeyman	8.00				E2	Allen Briney	Pilebutt	P	
	1	Journeyman	8.00				E2	Luke Paulk	Pilebutt	P	
	1	Apprentice	8.00				E2	Garrieth Nelson	Pilebutt	P	
	1	Journeyman	8.00				E2	Kevin Fitzgerald	Operator	P	
	1	Apprentice	8.00				E2	David Bian	Oiler	P	
	1	Apprentice			8.00		E2	Chris Roberts	Surveyor	P	
	1	Journeyman			8.00		E2	Terry Dennis	Surveyor	P	
	1	Ringer Barge	4.00				E2 4.00	Manitowac Crane		P	
002062	1	Lincoln Electric					E2 8.00	Vantage 500	6008088	P	
002083	1	Lincoln Electric					E2 8.00	Vantage 500	6008091	P	
002068	1	MQ Power Generator	8.00				E2	Whisperwatt 25	6007939	P	
002069	1	MQ Power Generator					E2 8.00	Whisperwatt 25		P	
	1	Honda 115 Horse Skiff					E2 8.00			P	
002075	1	Ingersoll Rand P185R					E2 8.00			P	
	1	Flex Anchor					E2 8.00	Equipment Barge	@ Pier 7	P	
002077	1	Ingersoll Rand P185R	4.00				Pier 7 4.00			P	
768504005	1	Lincoln Electric	4.00				Pier 7 4.00	Vantage 500	000073	P	
002067	1	MQ Power Generator	8.00					Whisperwatt 25		P	

Weekly meeting with ABF.
I was "rodman" for David Bradd. Checked layout of ABF's points layed out on the soffit of E2
Ironwork continued to be delivered to Pier 7 and loaded onto barges (DSC02274).
ABF's survey crew continued to lay out points for the shear keys/bearings at the south end of the cross beam (DSC02273).
Not much carpentry performed at E2 (DSC02271) besides drilling holes in the east panel for tie-back rods. More tin was laid down at the panel edges where the tent used to be for the south column cage.
At Pier 7, PT blockouts were being prefabricated with Karl Nisley as foreman.

RECT-01 #006808

STATE OF CALIFORNIA
 DEPARTMENT OF TRANSPORTATION
 CP-CEM 4601 (Rev. 4/99) (Old HC-10A)

TOLL PROGRAM/DIST. 4 CONSTR.

Job Stamp:
 04-SF-80-13.2/13.9 04-0120F4
 SFOBB SAS
 San Francisco Co. in San Francisco
 Fm 0.6 km to 1.3 km East of Yerba Buena
 Tunnel East Portal

Report No. 7-day const. cal.: 623
 Project work day: 833

Date the Shift Began: 8/27/08

NIGHTWORK WEDNESDAY

Shift Hrs Start 6:30 Stop 15:00
 Engineer's Hrs Start 6:50 Stop 15:20


ASSISTANT RESIDENT ENGINEER'S DAILY

BRIDGE

REPORT

Location: E2 Cross Beam/Pier 7

Weather: clear/warm

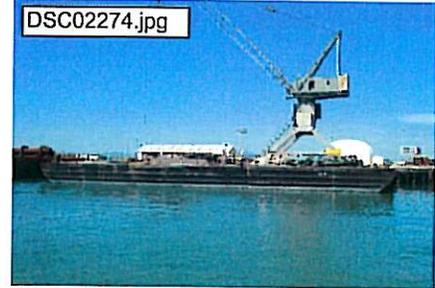

Materials:

Insp. Hrs.	
REG: 8.0	INTERMITTENT
OT:	INSPECTION

David Chung
 DAVID CHUNG

TE/CT
 Title
