

Job Stamp 04-0120F4 SFOBB SAS

Const. Calendar:	638			
Project Work Day No.:	838			
Date	09/11/2008			
Inspectors	Start	08:00	Stop	11:10
Hours		13:00		14:00
Shift Hours		07:00		15:30

ASSISTANT RESIDENT ENGINEER'S **CONTRACTOR – ABFJV**

Weather: Overcast with mild temperature in the morning and sunny in the afternoon with mild temperature – Hi 79°F Low 56°F (per weather.com forecast)

ABF

- Continued to strip the pour 3 north bulkhead forms in the areas where grouting was completed.
- Began to clean the south blockout for the bottom of the vertical bars.
- The row of VB-102 to VB-108 at the W2W Hinges was corrected in the north south direction to match the cross-slope of the concrete. I asked ABF foreman Nigel Lohse twice during the day if the Y-offset or spacing for the W2E vertical bars was checked. He told me that he is still waiting for the results from ABF surveyors who shot the rods yesterday. I took my measurements with a tape measure from the Hinge plate, which is sufficient for this application.
- Continued to construct steps to be installed from the W2 falsework soffit to the Temporary Tower walkways on the north end.
- Began to prepare for placing E-1B through E-14B blockouts by cutting and moving rebar.
- Erected last vertical east bulkhead form in the southeast corner of the W2 cap beam.
- Began to fill in the voids with plywood on the east walkways from the vertical forms with strongbacks to the walkway.

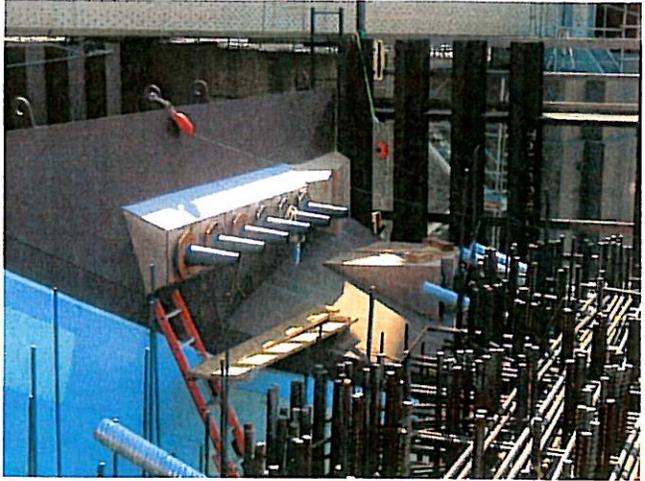
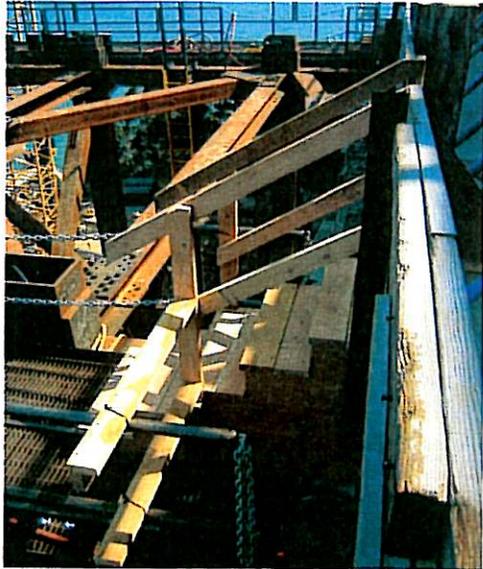
Office work:

- Wrote today's diary.

Inspector:

Matt Bruce Matt Bruce Transportation Engineer (D)

REC'D *08 OCT-07 #006952

EA	04-0120F4		
Co-Rte-KP (PM)	SF-080-13.2/13.9 (8.2/8.7)		
Structure Rep.	Rick Morrow		
			
File Name:	Sept-11-2008 W2 Cap 002		
Date:	09-11-08	By Int:	M Bruce
Description: North pour 3 construction joint form removal. The exposed concrete appeared to be in good condition with no cracks, honeycombs, or spalling.			
File Name:	Sept-11-2008 W2 Cap 007		
Date:	09-11-08	By Int:	M Bruce
Description: CBT-1 through CBT-15 blockouts at W2E end of the cap beam.			
			
File Name:	Sept-11-2008 W2 Cap 008		
Date:	09-11-08	By Int:	M Bruce
Description: Rebar cut to facilitate of E-1B through E-14B blockouts.			
File Name:	Sept-11-2008 W2 Cap 009		
Date:	09-11-08	By Int:	M Bruce
Description: Steps installed from the W2 falsework soffit to the Temporary Tower walkways on the north end.			
