

Job Stamp
04-0120F4
SFOBB SAS

Construction Calendar no. 651
Project working days no. 861
Date **09/24/2008**
Inspectors Start 09/23 Stop 10:30
Hours 22:30
Shift Hours Start 22:00 Stop 14:00

Assistant Structure Rep.'s Daily Report

Location & Description of Operation	SAS-Temporary towers, Tower C foundation
Weather	HI: 79 F Low: 54 F Partly cloudy

Equipment and/or labor			Hours - ITEM no.							Remarks
Equip no.	# personnel	Description (of equipment or labor)	Regular	OT	DT	Rental			IDLE	
	C	Bauer BG 24H	8	6						Drill Tech
	1	Grove RT 760E crane	8	6						T.D.
261-45-5018	R	John Deere 644J Loader	4							T.D.
246-05-5023	R	John Deere 135C RTS Excavator	4							T.D.
TD040802TB	2	Bossltg Light	8							T.D.
8M70628	C	3500 Dodge Ram	8	6						Drill Tech
6S43539	C	Ford F-450	8	6						Drill Tech
15092184 (Temp. Ident.)	C	Ford F-550	8	6						Drill Tech
	1	Brad Middleton	8	6						Foreman (Drill Tech)
	1	Gerado Trujillo	8	6						Drill Tech
	1	Eric Higuerg	8	6						Drill Tech
	1	Raul Melsoza	8	6						Drill Tech
	1	Pete Leavdlit	8	6						Drill Tech
	1	Ernie Hamilton	8	6						O.E. (Traylor - Dutra)
	1	Randle Leslie	4							O.E. (T.D.)
	1	Don Adams	4							O.E. (T.D.)
	1	Levis	4							O.E. (T.D.)

Description of Operation:

- Daily activity of contractors
 - D.T. Finished drilling C106 and 107 holes (27') (see Figs 1 and 2) and poured concrete (see Figs 3 and 4).
 - Before pouring concrete, D.T. pumped water out of the hole to make it dry condition (Fig 5).
 - ABF's subcontractor collected 4 concrete samples.
 - Pile cages of C105 and C108 are on-site (Fig 6)
 - See Art Pannu and Ali's diary for additional contractors' activities and comments.

- Note
 - Ali and I collected 4 concrete samples. The temperature is 80 F and slump is 6.5".
 - Ali and I brought 4 samples to water batch.
 - Manuel from KCB and Myo Heine from EMI are on-site.
 - See Ali's diary for the concrete tickets.
 - 7 hours O.T.

REC'D *08 OCT-08 #007064



Fig 1

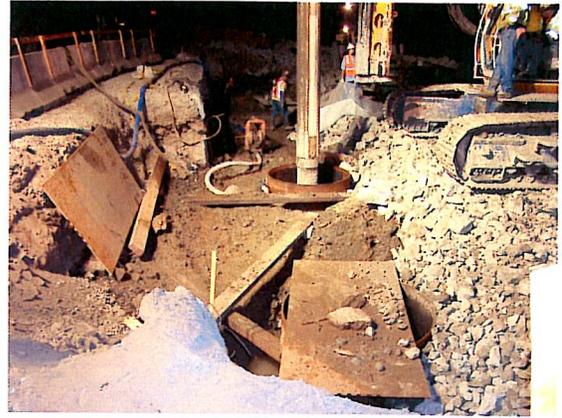


Fig 2



Fig 3



Fig 4

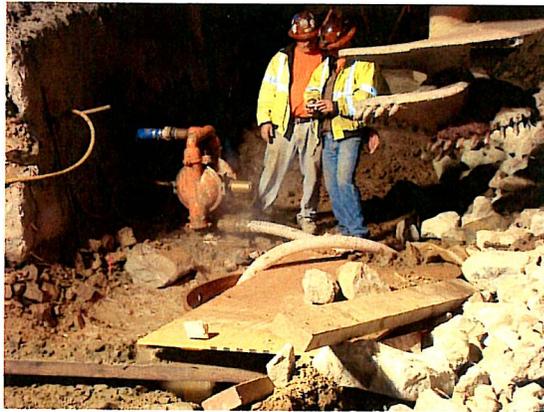


Fig 5



Fig 6

Inspector:
SeongHyeok Song

Trans Engineer (Civil) / Asst. Struct. Rep
