

STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION
CP-CEM 4601 (Rev. 4/99) (Old HC-10A)

TOLL PROGRAM/DIST. 4 CONSTR.

Job Stamp:
04-SF-80-13.2/13.9 04-0120F4
SFOBB SAS
San Francisco Co. in San Francisco
Fm 0.6 km to 1.3 km East of Yerba Buena
Tunnel East Portal

7-day Const. Cal.: 604
Project Work Day: 814
Date the Shift Began: 8/8/08
 NIGHTWORK FRIDAY
Shift Hrs Start 6:30 Stop 15:00
Engineer's Hrs Start 7:00 Stop 15:30

**ASSISTANT RESIDENT ENGINEER'S DAILY REPORT
BRIDGE**

Location: Temporary Tower D - Big Digger Remark:			Report No. 46.B			Weather: Fog and Wind, 59° - 62°		
ITEM NO. >>			8			HOURS - ITEM NO.		
EQUIPMENT AND/OR LABOR:			Furnish Temporary Towers			IDLE OR DOWN/ ELSEWHERE		
EQPT. NO.	NO. MEN	DESCRIPTION (Of Equipment or Labor)	RT				< RT/OT	
		Big Digger Manitowoc 2250 Crane	8.00					
		CB-11 Manitowoc 4000					IDLE	
		DB-5 Crane					ELSE	
		APE600 Vibratory Hammer					EL/IDLE	
		Delmag D100-13 Diesel Hammer					EL/IDLE	
		Mench MHU500T Hydraulic Hammer					EL/IDLE	
P241		Genie Boom					IDLE	
P242		Genie Boom					IDLE	
#005		Lincoln Electric Welder	3.00					
#003		Lincoln Electric Welder	3.00					
#001		Lincoln Electric Welder	3.00					
#002		Lincoln Electric Welder	3.00					
L472		Power Generator	3.00					
L478		Power Generator					ELSE	
L479		Multiquip Generator					ELSE	
L480		Multiquip Air Compressor					ELSE	
L269		D185Q Sullivan Air Compressor					IDLE	
L291		D185Q Sullivan Air Compressor	8.00					
L660		Diesel Generator					ELSE	
P44		Catepillar Forklift					ELSE	
		PLDR	8.00					Terry Murray FOR S1
		PLDR	8.00					Lee Tacker FOR S1
		PLDR	8.00					Bud Germany OPER S1
		PLDR	8.00					Danny Vega JRNY S1
		PLDR	8.00					Gilert Moya JRNY S1
		PLDR	8.00					Kurt Dillard JRNY S1
		PLDR	8.00					Theo Rohr OPER S1
		PLDR	8.00					Ventura Ochoa JRNY S1










Description of Operation:
 - Traylor Dutra completed welds as noted on the attachment
 - Kevin Meyers (CWI) was present for all weld operations and performed VT/MT inspection to D1.1 on all completed welds
 - Traylor Dutra removed seven (7) birds from the south piles. The distribution is as follows:
 D109: 1 D111: 2 D113: 1
 D110: 1 D112: 1 D116: 1
 The birds were fished out of the piles using a long handle net and placed into trash bags. Laura Ivey was present and took the bags. The total bird removal operation took 30 minutes to complete. Traylor Dutra placed plywood covers on all the South piles.
 - The rest of the day workers prepared for the North pile retapping which is planned for Monday.

Materials:

Insp. Hrs.	
REG: 8.0	INTERMITTENT
OT: 0.0	INSPECTION

Gina Rizzardo
 GINA RIZZARDO TE/CT
 First Name Last Name Title

REC'D *08 OCT 08 #007222

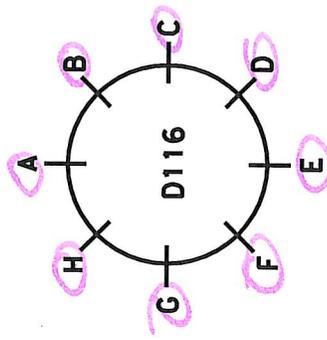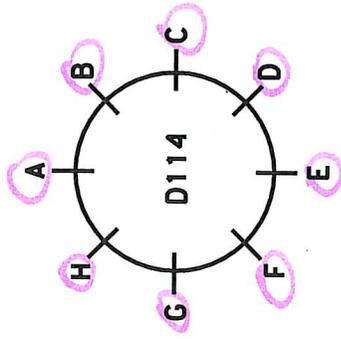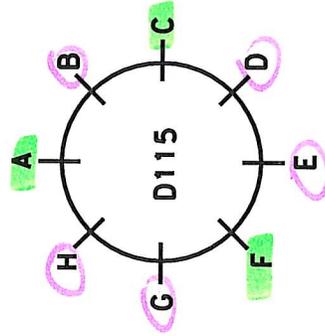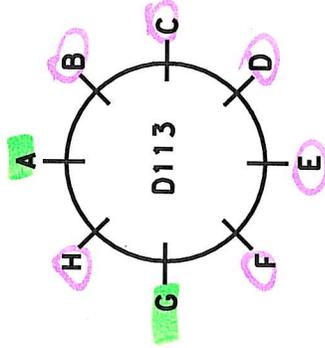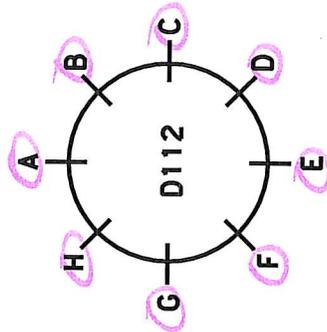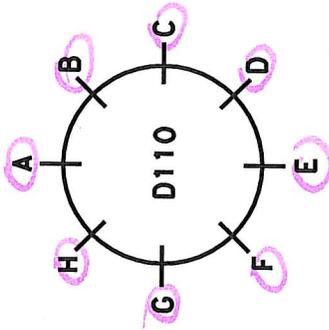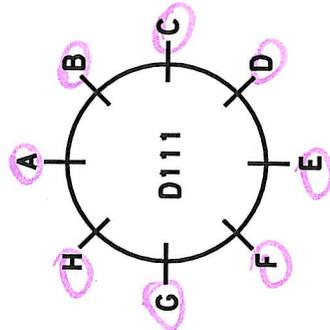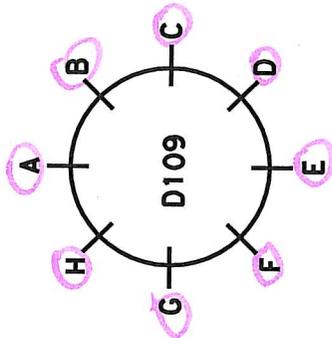

○ YIELDS PREVIOUSLY COMPLETED
■ YIELDS COMPLETED ON 08 AUG-08
