

TOLL PROGRAM/DIST. 4 CONSTR.

Job Stamp:
04-SF-80-13.2/13.9 04-0120F4
SFOBB SAS
San Francisco Co. in San Francisco
Fm 0.6 km to 1.3 km East of Yerba Buena
Tunnel East Portal

7-day Const. Cal.: 610
Project Work Day: 820
Date the Shift Began: 8/14/08
 NIGHTWORK **THURSDAY**
Shift Hrs Start 6:30 Stop 17:00
Engineer's Hrs Start 7:30 Stop 17:30

ASSISTANT RESIDENT ENGINEER'S DAILY REPORT
BRIDGE

Location: Temporary Tower D - Big Digger and DB5			Report No. 46.B		Weather: Sun and Wind, 61° - 78°						
Remark:			HOURS - ITEM NO.					REMARKS			
EQUIPMENT AND/OR LABOR:			Furnish Temporary Towers					Prime American Bridge / Fluor JV (P)			
EQUIPMENT AND/OR LABOR:			IDLE OR DOWN/ ELSEWHERE					Sub #1 Traylor-Dutra JV (1)			
EQUIPMENT AND/OR LABOR:			IDLE OR DOWN/ ELSEWHERE					Sub #2 (2)			
EQUIPMENT AND/OR LABOR:			IDLE OR DOWN/ ELSEWHERE					Sub #3 (3)			
EQUIPMENT AND/OR LABOR:			IDLE OR DOWN/ ELSEWHERE					Sub #4 (4)			
EQUIPMENT AND/OR LABOR:			IDLE OR DOWN/ ELSEWHERE					Sub #5 (5)			
EQPT. NO.	NO. MEN	DESCRIPTION (Of Equipment or Labor)	RT	OT					Name	Classification	Prime / Sub
		Big Digger Manitowoc 2250 Crane	8.00	2.00							
		CB-11 Manitowoc 4000						ELSE.			
		DB-5 Crane	8.00	2.00							
		APE600 Vibratory Hammer	8.00	2.00							
		Delmag D100-13 Diesel Hammer						IDLE			
		Mench MHU500T Hydraulic Hammer						IDLE			
P241		Genie Boom						IDLE			
P242		Genie Boom	4.00								
#005		Lincoln Electric Welder	8.00	2.00							
#003		Lincoln Electric Welder	8.00	2.00							
#001		Lincoln Electric Welder	8.00	2.00							
#002		Lincoln Electric Welder	8.00	2.00							
L472		Power Generator	8.00	2.00							
L478		Power Generator	4.00								
L480		Multiquip Air Compressor	8.00	2.00				IDLE			
L269		D185Q Sullivan Air Compressor	8.00	2.00							
L291		D185Q Sullivan Air Compressor	8.00	2.00							
L660		Diesal Generator	8.00	2.00							
P44		Catepillar Forklift						IDLE			
		PLDR	8.00	2.00					Dan Adams	JRNY	2
		PLDR	8.00	2.00					Richard Hiebert	FOR	2
		PLDR	8.00	2.00					Terry Murray	FOR	2
		PLDR	8.00	2.00					Lee Tacker	FOR	2
		PLDR	8.00						Adam Price	JRNY	2
		PLDR	8.00	2.00					Bud Germany	OPER	2
		PLDR	8.00	2.00					Danny Vega	JRNY	2
		PLDR	8.00	2.00					Doug Brewer	JRNY	2
		PLDR	8.00	2.00					Ernest Hamilton	OPER	2
		PLDR	8.00	2.00					Gary Lewis	APPR	2
		PLDR	8.00	2.00					Gilert Moya	JRNY	2
		PLDR	8.00	2.00					Joe Boracci	OPER	2
		PLDR	8.00	2.00					Kurt Dillard	JRNY	2
		PLDR	8.00	2.00					Randall Lesley	FOR	2
		PLDR	8.00	2.00					Richard Hiebert Jr	APPR	2
		PLDR	8.00	2.00					Robert Utley	JRNY	2
		PLDR	8.00	2.00					Theo Rohr	OPER	2
		PLDR	8.00	2.00					Travis Logsdon	JRNY	2
		PLDR	8.00	2.00					Ventura Ochoa	JRNY	2

08 OCT-08 #007225

STATE OF CALIFORNIA
 DEPARTMENT OF TRANSPORTATION
 CP-CEM 4601 (Rev. 4/99) (Old HC-10A)

TOLL PROGRAM/DIST. 4 CONSTR.

Job Stamp:
 04-SF-80-13.2/13.9 04-0120F4
 SFOBB SAS
 San Francisco Co. in San Francisco
 Fm 0.6 km to 1.3 km East of Yerba Buena
 Tunnel East Portal

7-day Const. Cal.: 610
 Project Work Day: 820
 Date the Shift Began: 8/14/08
 NIGHTWORK THURSDAY
 Shift Hrs Start 6:30 Stop 17:00
 Engineer's Hrs Start 7:30 Stop 17:30

ASSISTANT RESIDENT ENGINEER'S DAILY REPORT
BRIDGE

Description of Operation:










- Traylor Dutra removed two (2) plumb temporary temporary piles under the South Driving Frame. The vibratory hammer was used to loosen the pile about 15' then the DB-5 crane picked and completely removed the pile.
- Welding continued on the North Driving Frame at piles: D103, 105, 106 & 108. Smith Emery's Kevin Meyes (CWI) was present for entire operation and performed VT & MT for all completed welds. See attachment for welds that were completed.
- The pile tips of D101 and D102 were cut off. No seagulls were found in the piles.
- Randall Lesley and Dan Adams worked on forms for the B1 beam grout
- Worked 1 hr O.T.

Materials:

Insp. Hrs.	
REG: 8.0	INTERMITTENT
OT: 1.0	INSPECTION

Gina Rizzardo

 GINA RIZZARDO TE/CT
 Title
 First Name Last Name

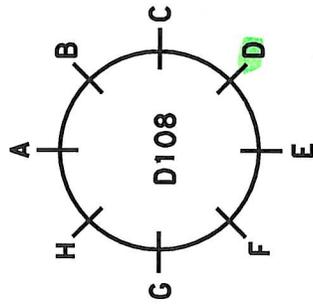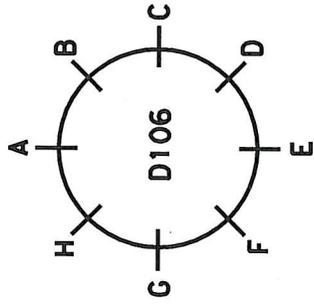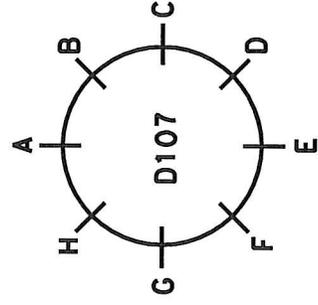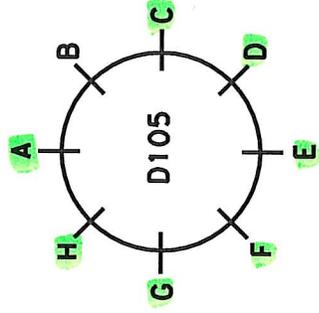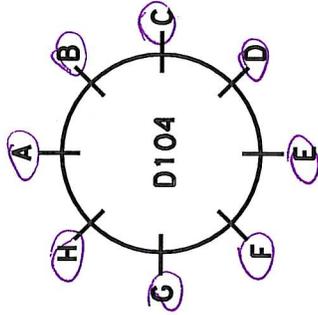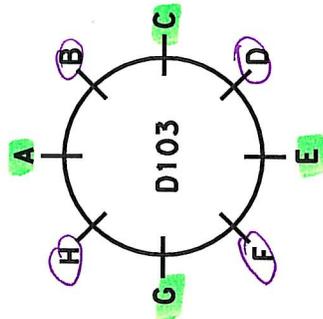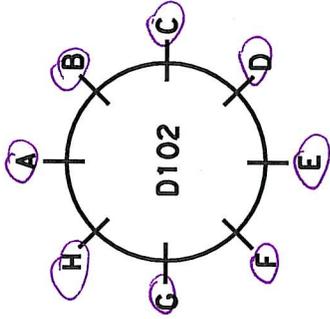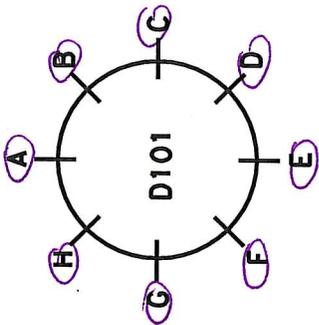

0 FIELDS PREVIOUSLY COMPLETED
FIELDS COMPLETED ON 14-AUG-2008
