

STATE OF CALIFORNIA  
DEPARTMENT OF TRANSPORTATION  
CP-CEM 4601 (Rev. 4/99) (Old HC-10A)

TOLL PROGRAM/DIST. 4 CONSTR.

Job Stamp:  
04-SF-80-13.2/13.9 04-0120F4  
SFOBB SAS  
San Francisco Co. in San Francisco  
Fm 0.6 km to 1.3 km East of Yerba Buena  
Tunnel East Portal

7-day Const. Cal.: 616  
Project Work Day: 826  
Date the Shift Began: 8/20/08  
 NIGHTWORK WEDNESDAY  
Shift Hrs Start 6:30 Stop 17:00  
Engineer's Hrs Start 7:30 Stop 16:00

**ASSISTANT RESIDENT ENGINEER'S DAILY REPORT  
BRIDGE**

Location: Temporary Tower D - Big Digger Report No. 46.B Weather: Sun, 65° - 78°  
Remark:










EQUIPMENT AND/OR LABOR:			HOURS - ITEM NO.							Furnish Temporary Towers	IDLE OR DOWN/ ELSEWHERE	REMARKS	Name	Classification	Prime / Sub	
EQPT. NO.	NO. MEN	DESCRIPTION (Of Equipment or Labor)	RT	OT					< RT/OT							
		Big Digger Manitowoc 2250 Crane	8.00	1.00												
		CB-11 Manitowoc 4000									ELSE.					
		DB-5 Crane									ELSE.					
		APE600 Vibratory Hammer									ELSE.					
		Delmag D100-13 Diesel Hammer									ELSE.					
		Mench MHU500T Hydraulic Hammer									ELSE.					
P241		Genie Boom									ELSE.					
P242		Genie Boom									IDLE					
#005		Lincoln Electric Welder									IDLE					
#003		Lincoln Electric Welder									IDLE					
#001		Lincoln Electric Welder									IDLE					
#002		Lincoln Electric Welder									IDLE					
L472		Power Generator									IDLE					
L478		Power Generator									IDLE					
L479		Multiquip Generator									ELSE.					
L480		Multiquip Air Compressor									IDLE					
L269		D185Q Sullivan Air Compressor	8.00													
L291		D185Q Sullivan Air Compressor	8.00	1.00												
L660		Diesel Generator									ELSE.					
P44		Catepillar Forklift									ELSE.					
		PLDR	8.00	1.00								Terry Murray	FOR	2		
		PLDR	8.00	2.00								Lee Tacker	FOR	2		
		PLDR	8.00	1.00								Bud Germany	OPER	2		
		PLDR	8.00	2.00								Ernest Hamilton	OPER	2		
		PLDR	8.00	1.00								Frank Wouters	OPER	2		
		PLDR	8.00	2.00								Gary Lewis	APPR	2		
		PLDR	8.00	2.00								Gilbert Moya	JRNY	2		
		PLDR	8.00	1.00								Kurt Dillard	JRNY	2		
		PLDR	8.00	1.00								Matt Morton	OPER	2		
		PLDR	8.00	2.00								Ventura Ochoa	OPER	2		

Description of Operation:  
 -DB5 is at Alameda preparing to pick up the precast concrete fenders  
 -Traylor Dutra installed the remaining 3 B6 beams on the east side of the South Driving Frame.  
 - Jason Wilcox and I visually inspected the completed welds on the North Driving Frame. Jason informed Lee Tacker and Terry Murray of his concerns of some of the weld's acceptability and recommended Smith Emery's Andrew Cauffman comes out to inspect them. The issue will be brought to ABF's attention for their decision.  
 -Traylor Dutra cut the tack welds on the bracing and top plates at the plumb and battered temporary temporary piles in order to prepare the their removal.  
 -Created drawing showing when welds were completed on the North Driving Frame, see attached

Materials:

Insp. Hrs.	
REG: 8.0	INTERMITTENT
OT: 0.0	INSPECTION

*GINA RIZZARDO*  
 GINA RIZZARDO TE/CT  
 Title  
 First Name Last Name  
 REC'D #08 OCT 08 #007228

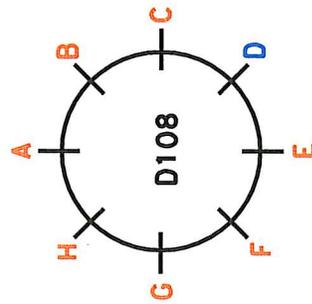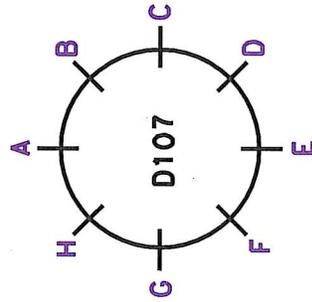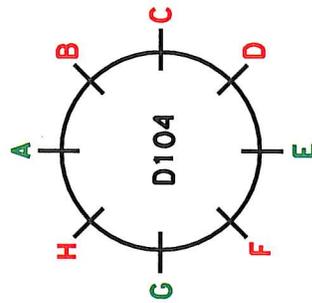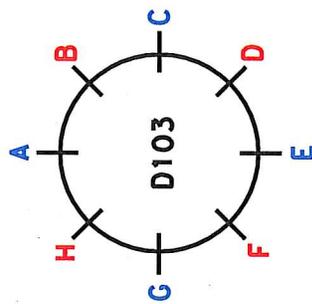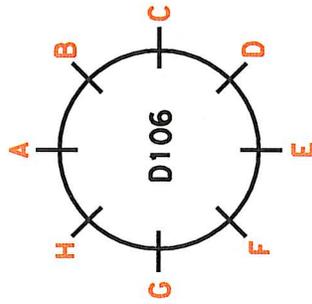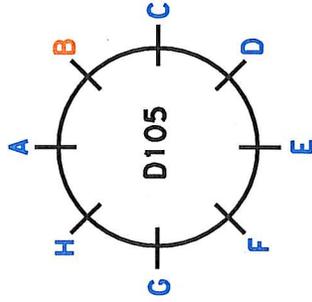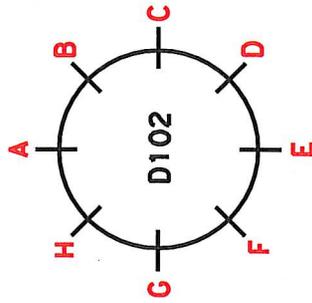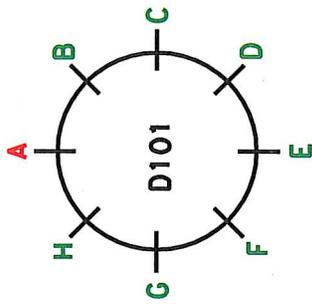

NORTH DRIVING FRAME PILES

12-AUG-2008

15-AUG-2008

13-AUG-2008

18-AUG-2008

14-AUG-2008
