

Job Stamp
04-0120F4
SFOBB SAS

Const. Calendar Day No. 642
Project Work Day No. 852
Date **09/15/2008**
Shift Hours Start 6:30 Stop 3:00
Inspector Shift 6:30 AM to 3:00 PM


ASSISTANT RESIDENT ENGINEER'S CONTRACTOR - ABFJV

HOURS - ITEM NO.													
EQUIPMENT AND/OR LABOR:			#38 Str. Concrete, Bridge	# 48 Bar Reinforcement Steel							IDLE OR DOWN	REMARKS	
Equip. #	N O · M E N	DESCRIPTION (Of Equipment or Labor)										Name	Contractor
1	1	Gen. Foreman									8	Terry Cronk	ABF Pier 7
2	1	Pile Driver	8									Tony Crieghton	ABF
3	1	Pile Driver	8									George Mcneil	ABF
4	1	Laborer	8									Jose Molina	ABF
5	1	Laborer	8									Rickie Campos	ABF
6	1	Pile Driver J/M	8									Audre Hudson	ABF
7	1	Pile Driver/Welder	8									Henry Wheat	ABF
8	1	Elevator Operator	8									Howard Schroyer	ABF
9	1	Pile Driver Foreman	8									Nigel Lohse	ABF
10	1	Pile Driver	8									Paul Mason	ABF
11	1	Pile Driver	8									Andy Adam	ABF
12	1	Pile Driver	8									Kurt Chassion	ABF
13	1	Pile Driver	8									Jesse Johnasen	ABF
14	1	Crane Operator	8									Jeff Scott	ABF
15	1	Operator Apprentice/oiler	8									Scott Ross	ABF
16	1	Pile Driver	8									Abasi Delley	ABF
17	1	Pile Driver	8									Kenny Reynolds	ABF
17	1	Labor										Doug Evans	ABF off
	1	Iron worker	8									Victor Quiroz	RSC
	1	Iron worker	8									Tim Greenlee etc	RSC
	1	Manitowoc 4100 W										New crane	ABF
	1	1 st Man Lift S-125											Hertz Rental
	1	Lincoln Vantage Welding M/C 768-50-4005									8		ABF
	1	Lincoln Vantage Welding M/C 768-50-4009									8		ABF
	1	Lincoln Vantage Welding M/C 768-30-4032									8		Hertz Rental
	1	Lincoln Vantage Welding M/C 768-30-4014	8										Hertz Rental, deck
	1	MQ Power Generator 220	8										ABF Main power
	1	MQ Whisper Watt 7000 549-07-5006	8										ABF deck



Installing 10-3/4
" PT pipe

Installing deviation
saddle PT rods

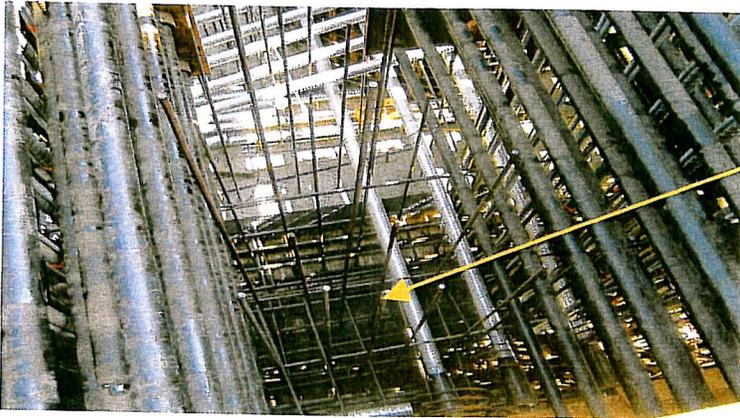

Vertical rebar in PT rod
block-out.
