

TOLL PROGRAM/DIST. 4 CONSTR.

Job Stamp:  
04-SF-80-13.2/13.9 04-0120F4  
SFOBB SAS  
San Francisco Co. in San Francisco  
Fm 0.6 km to 1.3 km East of Yerba Buena  
Tunnel East Portal

Report No. **46.B**  
Date the Shift Began: **9/15/08**  
 NIGHTWORK **MONDAY**  
Shift Hrs Start  Stop   
Engineer's Hrs Start  Stop

**ASSISTANT RESIDENT ENGINEER'S DAILY**

**BRIDGE**

**REPORT**

Location: Pier E2 & Berth 7	7-day const. cal.: 642	Weather: Overcast and mild
Remark:	Project work day: 852	

Description of Operation: Install Reinforcing Steel and Assemble Anchor Rods

EQUIPMENT AND/OR LABOR:			HOURS - ITEM NO.					REMARKS		
EQPT. NO.	NO. MEN	DESCRIPTION (Of Equipment or Labor)	RT	RT				Name	Classification	Prime / Sub
		<b>Pier E2</b>								
		Pile Driver		8.00				Karl Nisley	Foreman	p
		Pile Driver		8.00				Richard Yambao	Journeyman	p
		Pile Driver		8.00				Ed Mendoza	Journeyman	p
		Pile Driver		8.00				Jason Matlock	Journeyman	p
		Pile Driver		8.00				Alan Briney	Journeyman	p
		Pile Driver		8.00				Luke Paulk	Journeyman	p
		Pile Driver		8.00				Garrieth Nelson	Journeyman	p
		Pile Driver		8.00				Harry Wheat	Journeyman	p
		Laborer		8.00				Byron Contreras	Laborer	p
		Laborer		8.00				Rigoberto Carreon	Laborer	p
		Iron worker		8.00				Robert Bognaes	Foreman	S
		Iron worker		8.00				Tim Greenly	Journeyman	S
		Iron worker		8.00				Lucino Ortiz	Journeyman	S
		Iron worker		8.00				Alberto Quiroz	Journeyman	S
		Iron worker		8.00				Carlos Morales	Journeyman	S
		Iron worker		8.00				Jose Playo	Journeyman	S
		Pile Driver	8.00					Ben Neal	Foreman	p
		Deck Engineer	8.00					Ryan Oku	Journeyman	p
		Operator	8.00					Kevin Fitzgerald	Journeyman	p
		Oiler	8.00					David Bian	Apprentice	p
		Operator	8.00					Mark Mom	Journeyman	p
		Oiler	8.00					Kevin Alger	Journeyman	p
			8.00					Terry Denis	Surveyor	p
			8.00					Chris Roberts	Surveyor	p
		<b>Berth 7</b>								
		Superintendent		8.00				Tom Gibson		p
		Foreman		8.00				Rick Clayborne		p
		Iron worker		8.00				Richard Bazewicz		p
		Iron worker		8.00				Barry Rothman		p
		Iron worker		8.00				Casey Lux		p
		Iron worker		8.00				Joseph Ruiz, II		p
		Laborer		8.00				Erevardo Hernandez		p
		Laborer		8.00				Froilan Ruis		p



Job Stamp:  
04-SF-80-13.2/13.9 04-0120F4  
SFOBB SAS  
San Francisco Co. in San Francisco  
Fm 0.6 km to 1.3 km East of Yerba Buena  
Tunnel East Portal


Report No. **46.B**  
Date the Shift Began: **9/15/08**  
 NIGHTWORK **MONDAY**  
Shift Hrs Start      Stop       
Engineer's Hrs Start      Stop     

**ASSISTANT RESIDENT ENGINEER'S DAILY**

**BRIDGE**

**REPORT**

Location: Pier E2 & Berth 7	7-day const. cal.: 642	Weather: Overcast and mild
Remark: <span style="background-color: yellow;"> </span>	Project work day: 852	<span style="background-color: yellow;"> </span>

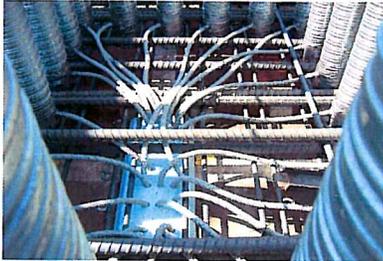

This meeting was followed up by a trip to Berth 7, where the ABF folks were putting together the Shear Key Anchor Rod Assemblies. This was the work that they were to commence on Saturday but cancelled **WITHOUT** informing Caltrans. As a result, CT inspector M. Modanlou showed-up without any knowledge of ABF's cancellation of the job.

There are 96 anchor rods that need to be assembled per **Submittal 689R1**. 48 anchor rods per Shear Key for each column, 60 of which are 4500mm inside the column and the other project 2250mm inside the column. ABF's assembly line were intent to finish the assembly by Wenesday. At this time they were greasing the rods with the Denzo Paste and Denzo tape.



At the dock, while inspecting the assembly of the Anchor Bolts, an ABF field inspector named Cthriene approached us and told us that she was looking for Ajai. She added that she was told to get a hold of him for all issues concerning the Anchor Bolts. She continued that Ajai has not returned her phone calls. Back at the office, I spoke to Ajai about this work and he told Massoud & I that it is actually our job to look after the assembly of the Anchor Bolts and that the decision has been made at the highest level of management. Following a few friendly exchanges and verifications, Massoud & I agreed to be the responsible parties for this inspection.

Materials:

Insp. Hrs.	
REG:	<b>INTERMITTENT</b>
OT:	<b>INSPECTION</b>

Saman Soheili

ASR/CT  
Title
