

STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION
Contract 0120F – SFOBB – SAS Superstructure
Week Ending 2008-11-14

Tuesday November 11, 2008 – No observation due to Veterans Day Holiday

Friday November 14, 2008 – Observation from Yerba Buena Island between 1000 and 1230: Clear, Warm, Calm

- E2 – view from top of W2 – Forming continues



- TT "D" – No observed activity




D*08 NOV-17 #007650

- **TT "F" East Bound (Southerly) Driving Frame –2 lifts of battered piles complete -In wait period for re-tap of piles**



Closer view of TT "F" East Bound driving Frame

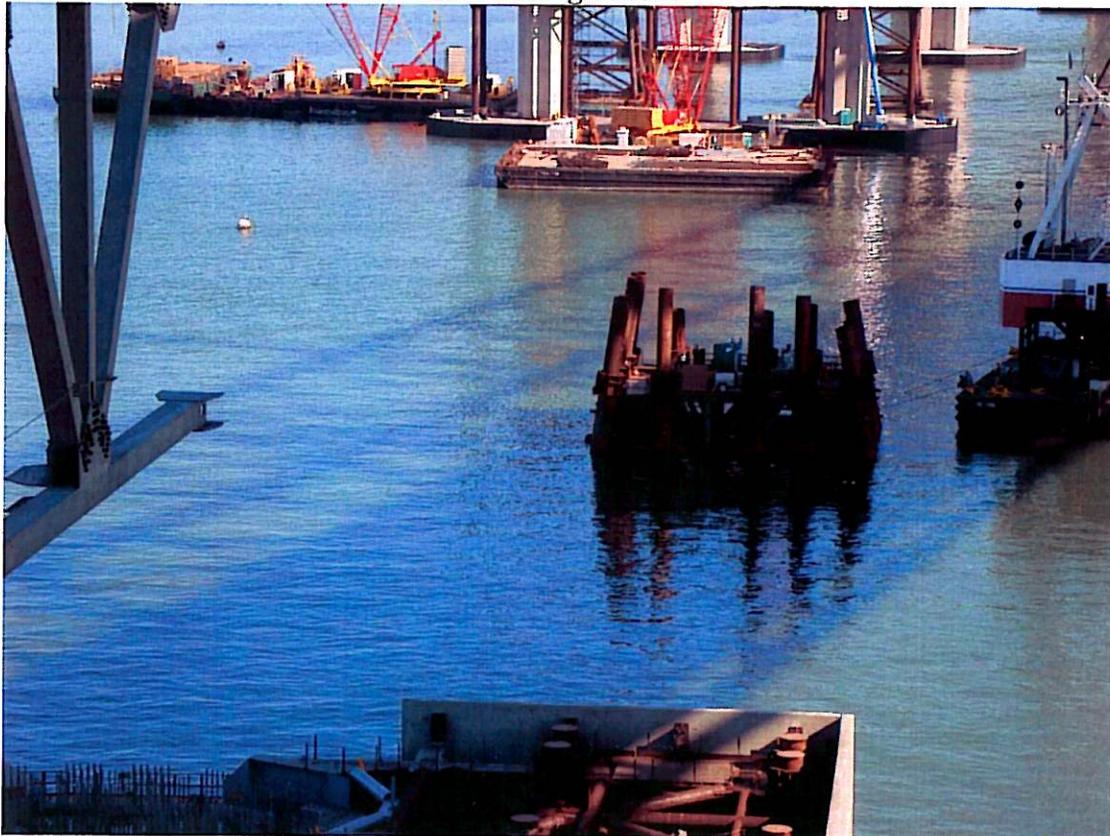


- Area "C" – No activity observed – Told that E Line Temporary Tower C has been delivered to Pier 7 by ABM



- W2 – Thermal Control & Curing of Pour #4 of Friday night November 7/8th



Thermal Control Piping and manifold

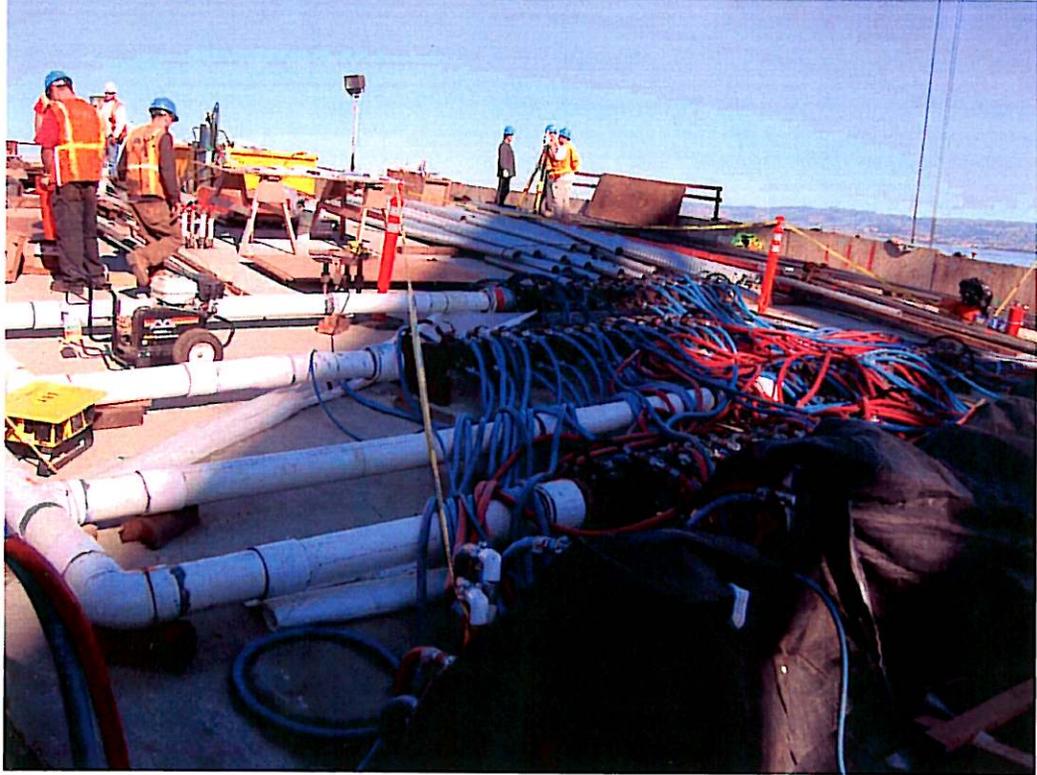

Pour #4 Curing area




Re-starting rebar installation in West Bound Northerly area for Pour #5




More work in northerly East Bound Area



- **East Line addition to E3 + Truss – To the East of Temporary Tower “B”**

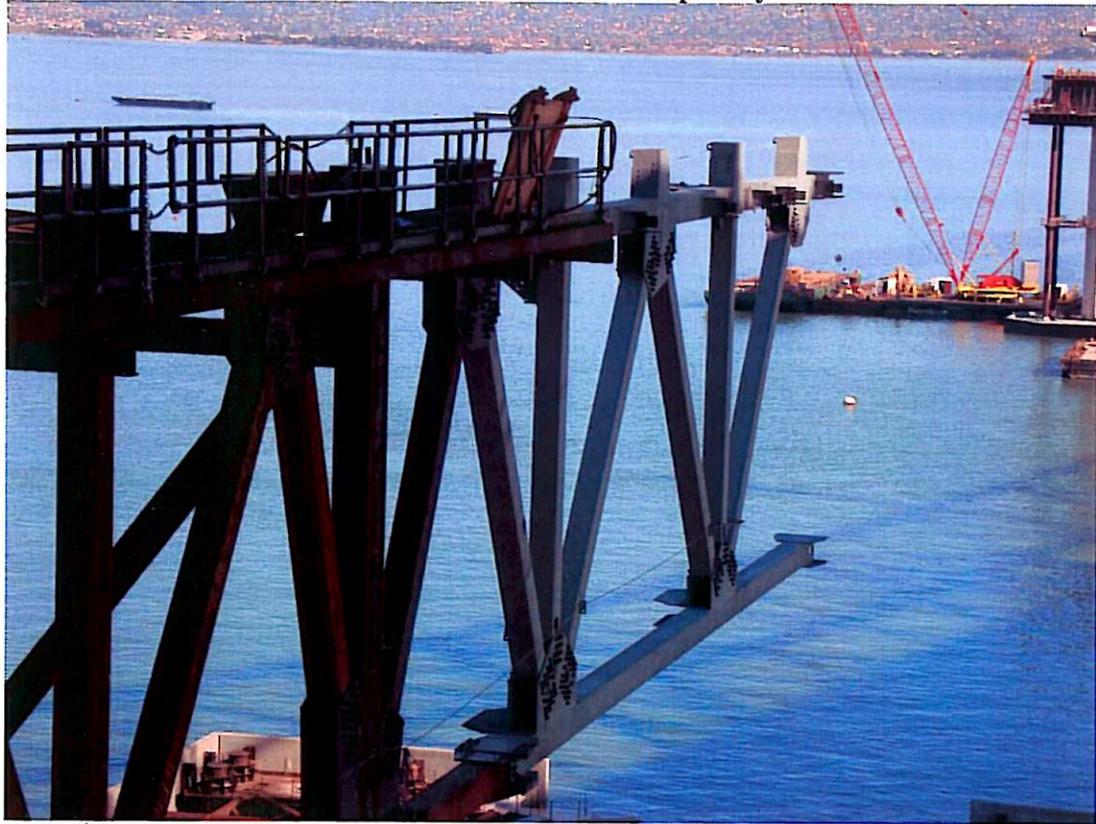

View from ground of E3 + Truss

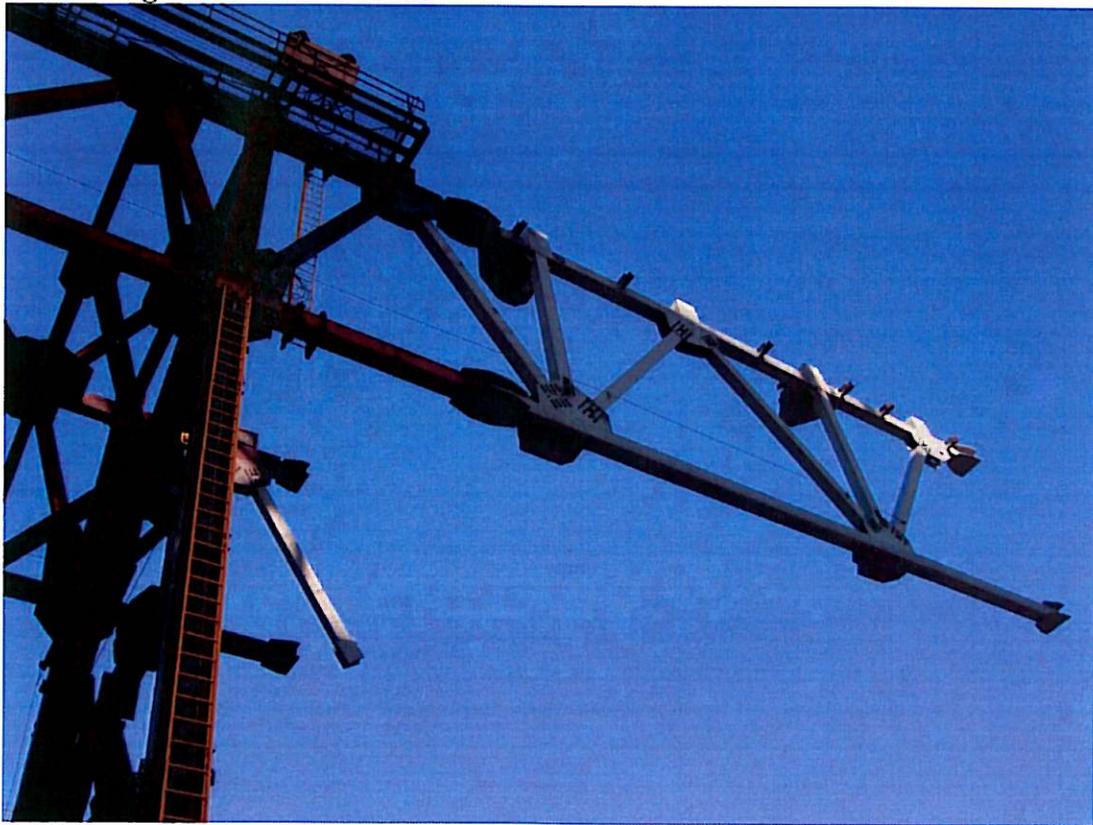

Assembling Northerly E 3 + Line Truss



Golden Gate Bridge on a Clear Day from W2 (for reference purposes)

