

Job Stamp 04-0120F4 SFOBB SAS

Const. Calendar:	700			
Project Work Day No.:	910			
Date	11/12/2008			
Inspectors	Start	08:40	Stop	10:40
Hours		12:50		13:40
Shift Hours		07:00		15:30

ASSISTANT RESIDENT ENGINEER'S **CONTRACTOR – ABFJV, subs CMC-RS**

Weather: Overcast with mild temperature – Hi 63°F Low 51°F (per weather.com forecast)

Description of Operations @ W2 Cap Beam:

ABF

- Continued thermal control of the pour 4 concrete with the manifolds starting from the north going south reading the following; 60°F, 60°F/19psi, 61°F, and 62°F.
- Continued to install "Short" vertical PT bars near the W2W Hinge K assemblies. Piledrivers were seen sealing the connections of the grout tubes with additional duck tape and replacing damaged tubes.
- Resumed cleaning the pour 5 base slab.
- Resumed placing PVC pipes for the pour 5 thermal control.
- Continued to install starter tie rods through the HP strongbacks. Also began connecting/placing tie rods in the east/west direction between the south end of the W2W column cages and the sloped void forms.

CMC-RS

- Began to place grillage around the CBT-9 to 15 blockouts on the north end of the cap beam near W2W.
- Mobilized #25 horizontal ties and #36 east and west wall transverse bars on the median surface. Also began layout for these bars in the pour 5 area.

Surveying work:

- Assisted Gil with checking the slope of Macalla Road, road leading up to the W2 cap beam, and the access trestle to the Eastbound structure of the Skyway.

Office work:


- Attended weekly Team Concrete meeting with ABF and TY-Lin at 8:00am.
- Wrote today's diary.

Inspector:

Matt Bruce Matt Bruce Transportation Engineer (D)

REC'D *08 NOV-18 #007681

EA	04-0120F4
Co-Rte-KP (PM)	SF-080-13.2/13.9 (8.2/8.7)
Structure Rep.	Rick Morrow

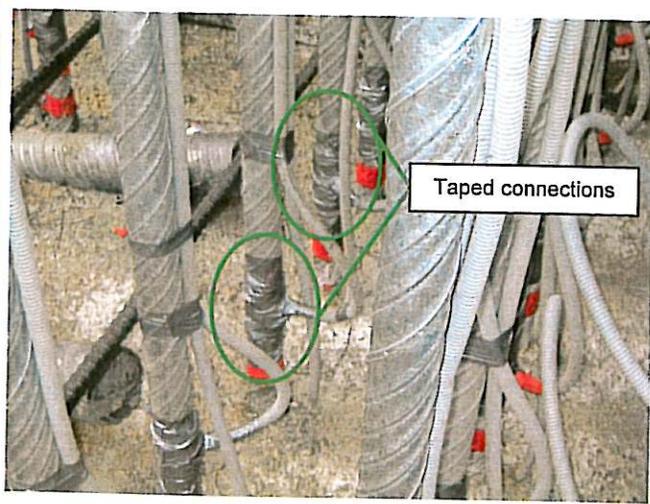

File Name:	Nov-12-2008 W2 Cap 006
Date:	11-12-08
By Int:	M Bruce

Description: Photo of the long vertical PT bars at the south W2W Hinge K assembly. The grout saddle connections are taped up and some grout tubes have been replaced. This was an item on the pour 4 punchlist.

File Name:	Nov-12-2008 W2 Cap 008
Date:	11-12-08
By Int:	M Bruce

Description: Ironworkers placing grillage for CBT-9 to 15 on the north end of the cap beam near W2W.
