

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 691
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 901
Form HC-10A (Rev. 6/80)	04-0120F4	Date	11/03/2008

Inspectors Hours	Start	0630	Stop	1500
Shift Hours	Start	0630	Stop	1500

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR - ABFJV

HOURS - ITEM NO.													
EQUIPMENT AND/OR LABOR:			Regular	OT							IDLE OR DOWN	REMARKS	
Equip. #	NO. OF MEN	DESCRIPTION (Of Equipment or Labor)										Name	Contractor
		DB # 5 Marine barge	8	0									
		APE 600 Vibration hammer	8										
		Superintendant	0	8								Terry Murray	Traylor Dutra
		Pile driver Journeyman	0	0								Gilbert Moya	Traylor Dutra
		Pile driver Journeyman	0	8								Adams Price	Traylor Dutra
		Operator	0	8								Joe Boracci	Traylor Dutra
		Pile driver Journeyman	0	0								Ventura Ochoa	Traylor Dutra
		Operator	0	8								Theo Roth	Traylor Dutra
		Pile driver Journeyman	0	0								Phillip Baker	Traylor Dutra
		Pile driver Journeyman	0	0								Robert Utley	Traylor Dutra
		Pile driver Journeyman	0	0								Bradly Mc Malley	Traylor Dutra
		Pile driver Journeyman	0	8								Lee Tacker	
		Pile driver Journeyman	0	0								Danny Vagas	Traylor Dutra
		Pile driver Journeyman	0	0								Stephen Mc Grew	Traylor Dutra
		Pile driver Journeyman	0	0								Jake Lavash	Traylor Dutra
		Pile driver Journeyman	0	0								Gary Lewis	Traylor Dutra
		Operator	0	0								Bud Germany	Traylor Dutra
		Operator	0	0								Steve Gordon	Traylor Dutra
		Pile driver Journeyman	0	0								Travis Logsdon	Traylor Dutra
		Operator	0	8								Joe Boracci	Traylor Dutra
		Operator	0	0								Ernie Hamilton	Traylor Dutra
		Pile driver Apprentice	0	8								Richard Hiebert J.	Traylor Dutra
		Pile driver Journeyman	0	0								Todd Labarb	Traylor Dutra
		Pile driver Journeyman	0	8								Richard Hiebert	Traylor Dutra
		Pile driver Journeyman	0	0								Randell Lesley	Traylor Dutra

Weather: Partly Cloudy Hi 67 °F, Lo 46 °F.

Description of Operation:

Temperary Tower F - Pile splicing

Activities:

- Office work:

46.02

- Review plans, special provisions, RFI and ABF submittals for TTF.
- Staff meeting at 0800.


2. Field work:

- DB 5 crew installed working platforms for pile splicing operation for piles F123 and F127.
- Micheal Johson and Gary Erhsm were present for QA/QC welding inspection.
- See Jason's diary for more information.


WILCOX

3. Overtime reason:

Thanh V Le



Trans Engineer (D)/Asst. Struct. Rep

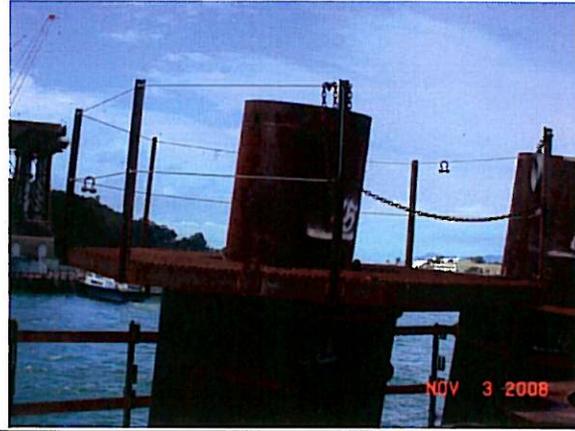

Working platform for pile splicing operation.
