

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 693
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 903
Form HC-10A (Rev. 6/80)	04-0120F4	Date	11/05/2008

Inspectors Hours	Start	0630	Stop	1500
Shift Hours	Start	0630	Stop	1500

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR - ABFJV

EQUIPMENT AND/OR LABOR:		HOURS - ITEM NO.										REMARKS		
Equip. #	N O M E N	DESCRIPTION (Of Equipment or Labor)	Regular	OT								IDLE OR DOWN	Name	Contractor
		DB # 5 Marine barge	8											
		APE 600 Vibration hammer	8											
		Diesel - Delmag 100	8											
		Superintendant	8	1									Terry Murray	Traylor Dutra
		Pile driver Journeyman	8	1									Gilbert Moya	Traylor Dutra
		Pile driver Journeyman	0	0									Adams Price	Traylor Dutra
		Operator	8	1									Joe Boracci	Traylor Dutra
		Pile driver Journeyman	8	1									Ventura Ochoa	Traylor Dutra
		Operator	8	1									Theo Roth	Traylor Dutra
		Pile driver Journeyman	0	0									Phillip Baker	Traylor Dutra
		Pile driver Journeyman	8	1									Robert Utley	Traylor Dutra
		Pile driver Journeyman	8	1									Bradly Mc Malley	Traylor Dutra
		Pile driver Journeyman	0	0									Lee Tacker	
		Pile driver Journeyman	0	0									Danny Vagas	Traylor Dutra
		Pile driver Journeyman	0	0									Stephen Mc Grew	Traylor Dutra
		Pile driver Journeyman	0	0									Jake Lavash	Traylor Dutra
		Pile driver Journeyman	0	0									Gary Lewis	Traylor Dutra
		Operator	0	0									Bud Germany	Traylor Dutra
		Operator	0	0									Steve Gordon	Traylor Dutra
		Pile driver Journeyman	8	1									Travis Logsdon	Traylor Dutra
		Operator	8	1									Joe Boracci	Traylor Dutra
		Operator	0	0									Ernie Hamilton	Traylor Dutra
		Pile driver Apprentice	0	0									Richard Hiebert J.	Traylor Dutra
		Pile driver Journeyman	0	0									Todd Labarb	Traylor Dutra
		Pile driver Journeyman	8	1									Richard Hiebert	Traylor Dutra
		Pile driver Journeyman	0	0									Randell Lesley	Traylor Dutra

Weather: Partly Cloudy Hi 67 °F, Lo 46 °F.

Description of Operation:

46-02

Temporary Tower F – Pile splicing and driving


Activities:

1. Office work:
 - Review plans, special provisions, RFI and ABF submittals for TTF.
2. Field work:
 - Welding crew finished splicing piles F127 and F123.
 - Micheal Johson and Gary Erhsm were present to perform QA/QC inspection.
 - F123: UT testing at 1003 was OK by M.J.
 - F127: UT testing at 0935 was OK by M.J.
 - After UT testing, DB # 5 crew vibrated two pile to elev. 60m
 - Mike Halaway was present for PDA testing.
 - Manuel S. Reyes from KCB was present for driving pile monitoring.
 - Bryan O'Sullivan was present for blow count.
 - Melinda Corner and Mellinda Fella from SRS consultant were present for mammal monitoring.
 - By late afternoon, DB 5 had problem with Diesel Hammer, therefore they couldn't drive the pile today, pile driven operation postpone to next day.

3. Overtime reason:

Work 1.5 hours overtime for construction observation because contractor worked overtime one hour and meeting with lead half hour.


Thanh V Le




Trans Engineer (D)/Asst. Struct. Rep



UT testing

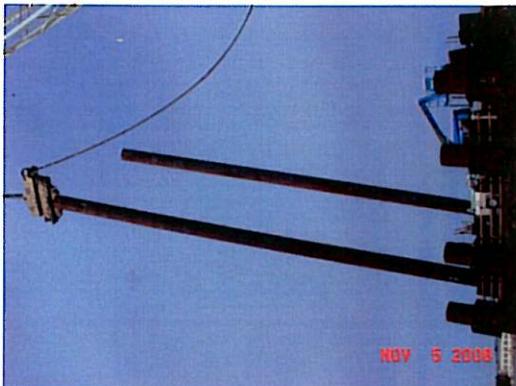

Vibration hammer

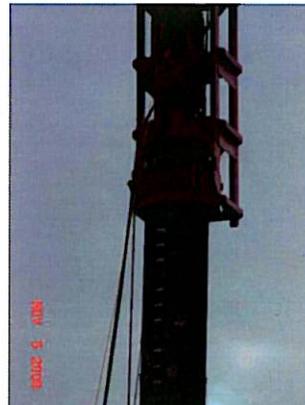

Diesel hammer
