

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 695
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 905
Form HC-10A (Rev. 6/80)	04-0120F4	Date	11/07/2008

Inspectors Hours	Start	0630	Stop	1500
Shift Hours	Start	0630	Stop	1500

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR - ABFJV

EQUIPMENT AND/OR LABOR:		HOURS - ITEM NO.										REMARKS		
Equip. #	N O M E N	DESCRIPTION (Of Equipment or Labor)	Regular	OT								IDLE OR DOWN	Name	Contractor
		DB # 5 Marine barge	8											
		APE 600 Vibration hammer	8											
		Diesel - Delmag 100	8											
		Superintendant	8	0									Terry Murray	Traylor Dutra
		Pile driver Journeyman	8	0									Gilbert Moya	Traylor Dutra
		Pile driver Journeyman	0	0									Adams Price	Traylor Dutra
		Operator	8	0									Joe Boracci	Traylor Dutra
		Pile driver Journeyman	8	0									Ventura Ochoa	Traylor Dutra
		Operator	8	0									Theo Roth	Traylor Dutra
		Pile driver Journeyman	0	0									Phillip Baker	Traylor Dutra
		Pile driver Journeyman	8	0									Robert Utley	Traylor Dutra
		Pile driver Journeyman	8	0									Bradly Mc Malley	Traylor Dutra
		Pile driver Journeyman	0	0									Lee Tacker	Traylor Dutra
		Pile driver Journeyman	0	0									Danny Vagas	Traylor Dutra
		Pile driver Journeyman	0	0									Stephen Mc Grew	Traylor Dutra
		Pile driver Journeyman	0	0									Jake Lavash	Traylor Dutra
		Pile driver Journeyman	0	0									Gary Lewis	Traylor Dutra
		Operator	0	0									Bud Germany	Traylor Dutra
		Operator	0	0									Steve Gordon	Traylor Dutra
		Pile driver Journeyman	8	0									Travis Logsdon	Traylor Dutra
		Operator	8	0									Joe Boracci	Traylor Dutra
		Operator	0	0									Ernie Hamilton	Traylor Dutra
		Pile driver Apprentice	0	0									Richard Hiebert J.	Traylor Dutra
		Pile driver Journeyman	0	0									Todd Labarb	Traylor Dutra
		Pile driver Journeyman	8	0									Richard Hiebert	Traylor Dutra
		Pile driver Journeyman	0	0									Randell Lesley	Traylor Dutra

Weather: Partly Cloudy Hi 67 °F, Lo 46 °F.

Description of Operation:

46.02


Temporary Tower F – Pile splicing and driving

Activities:

1. Office work:
 - Review plans, special provisions, RFI and ABF submittals for TTF.
2. Field work:
 - Mike Halaway was present for PDA testing.
 - Manuel S. Reyes from KCB was present for driving pile monitoring.
 - Bryan O'Sullivan was present for blow count.
 - Melinda Corner and Cory Champagne from SRS consultant were present for mammal monitoring.
 - DB5 performed pile driving operation today for piles :
 1. F128: Vibrated to 44.50 , Diesel hammer to 64.00
 2. F124: Vibrated to 44.5, Diesel hammer to 63.00
 - According to PDA for F128 results, the capacity of pile was lower than expectation.

3. Overtime reason:


Thanh V Le



Trans Engineer (D)/Asst. Struct. Rep



Driven pile operation

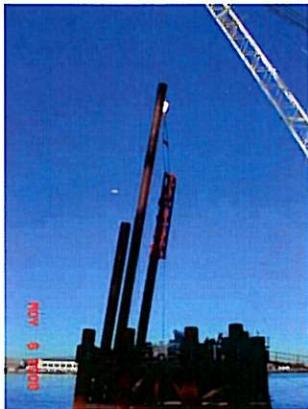

Delmag 100 hammer
