

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 702
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 912
Form HC-10A (Rev. 6/80)	04-0120F4	Date	11/13/2008

Inspectors Hours	Start	0630	Stop	1700
Shift Hours	Start	0630	Stop	1700

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR – ABFJV

HOURS - ITEM NO.											REMARKS	
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)	Regular	OT						IDLE OR DOWN	Name Contractor	
											EQUIPMENT AND/OR LABOR:	
		See Gina's diary for labor and equipment of the day.										

Weather: Partly Cloudy Hi 67 °F, Lo 46 °F.

Description of Operation:

Temporary Tower F – Pile splicing/piles driving

Activities:


1. Office work:
 - Review plans, special provisions, RFI and ABF submittals for TTF.
2. Field work:
 - DB5 crew drove three piles today F113, F107 and F114 .
 - Splicing F106, root MT at 1535.
 - Sean Hanson and Melinda Corner from SRS consultant were present for mammal monitoring.
 - Manuel Reys from KCB was present for pile driving monitoring.
 - Michael Johnson and Gary Erhsam were present for QA/QC inspection. (from Smith Emery)

3. Overtime reason:

Thanh V Le

Trans Engineer (D)/Asst. Struct. Rep

46-02

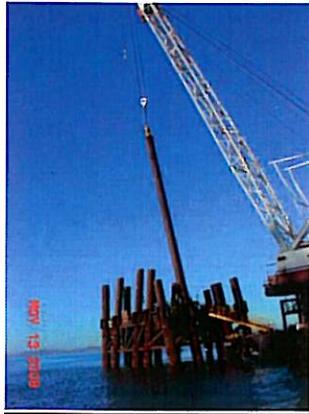

Pile splicing operation
