

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 714
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 924
Form HC-10A (Rev. 6/80)	04-0120F4	Date	11/26/2008

Inspectors Hours	Start	0630	Stop	1500
Shift Hours	Start	0630	Stop	1500

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR – ABFJV

HOURS - ITEM NO.												REMARKS	
Equip. #	NO. MEEN	DESCRIPTION (Of Equipment or Labor)	Regular	OT							IDLE OR DOWN	Name Contractor	

Weather: Partly Cloudy Hi 67 °F, Lo 46 °F.

Description of Operation:


Temperary Tower F – North Node Assembly

Activities:


1. Office work:
 - Review plans, special provisions, RFI and ABF submittals for TTF.

2. Field work:
 - BD 5 crew continued drilled and installation bolts for driving frame connections.
 - Carpenter crew continued installation working platform and safety handrail system for the driving frame.
 - Welder crew continued installation attachment for jacking systems.
 - One location on bottom deck, location of the bolts in B1 beam too close to the edge <50mm (photo attached)
 - See Gina's diary for more information.


3. Overtime reason:

Thanh V Le  Trans Engineer (D)/Asst. Struct. Rep

46.02

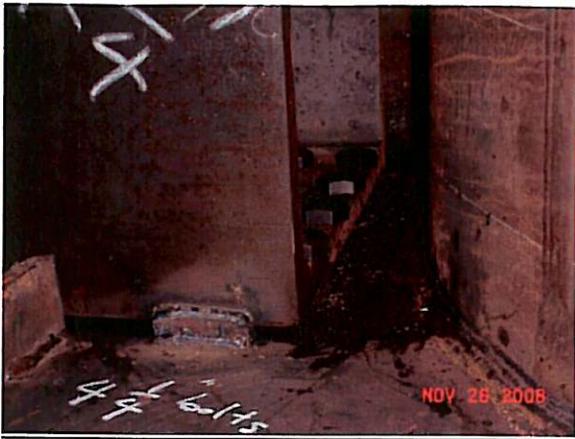

Bolts too close to the edge

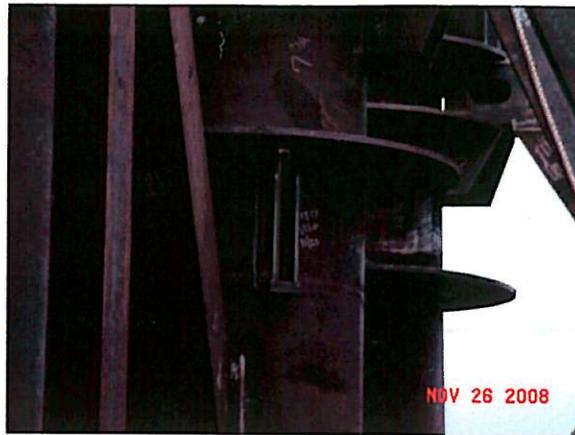

Jacking system attachment



Working platform
