

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 721
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 931
Form HC-10A (Rev. 6/80)	04-0120F4	Date	12/03/2008

Inspectors Hours	Start	0630	Stop	1700
Shift Hours	Start	0630	Stop	1700

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR - ABFJV

EQUIPMENT AND/OR LABOR:		HOURS - ITEM NO.										REMARKS	
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)	Regular	OT							IDLE OR DOWN	Name	Contractor
		DB # 5 Marine barge	0										
		APE 600 Vibration hammer	0										
		Delmag 100 - Diesel hammer	0										
		Superintendant	8	2								Terry Murray	Traylor Dutra
		Pile driver Journeyman	8	2								Gilbert Moya	Traylor Dutra
		Pile driver Journeyman	8	2								Adams Price	Traylor Dutra
		Operator	8	2								Joe Boracci	Traylor Dutra
		Pile driver Journeyman	8	2								Ventura Ochoa	Traylor Dutra
		Operator	8	2								Theo Roth	Traylor Dutra
		Pile driver Journeyman	0	0								Phillip Baker	Traylor Dutra
		Pile driver Journeyman	8	2								Robert Utley	Traylor Dutra
		Pile driver Journeyman	8	2								Bradly Mc Malley	Traylor Dutra
		Pile driver Journeyman	0	0								Lee Tacker	
		Pile driver Journeyman	0	0								Danny Vagas	Traylor Dutra
		Pile driver Journeyman	0	0								Stephen Mc Grew	Traylor Dutra
		Pile driver Journeyman	0	0								Jake Lavash	Traylor Dutra
		Pile driver Journeyman	0	0								Gary Lewis	Traylor Dutra
		Operator	8	2								Bud Germany	Traylor Dutra
		Operator	0	0								Steve Gordon	Traylor Dutra
		Pile driver Journeyman	8	2								Travis Logsdon	Traylor Dutra
		Operator	0	0								Joe Boracci	Traylor Dutra
		Operator	0	0								Ernie Hamilton	Traylor Dutra
		Pile driver Apprentice	8	2								Richard Hiebert J.	Traylor Dutra
		Pile driver Journeyman	0	0								Todd Labarb	Traylor Dutra
		Pile driver Journeyman	8	2								Richard Hiebert	Traylor Dutra
		Pile driver Journeyman	8	2								Randell Lesley	Traylor Dutra

REC'D 09 JAN 05 #008188

Weather: Partly Cloudy Hi 67 °F, Lo 46 °F.

46.02

Description of Operation:

Temporary Tower F – North Node driving frame assemble


Activities:

1. Office work:
 - Review plans, special provisions, RFI and ABF submittals for TTF and TTG
 - Concrete pour team meeting for E2 cap beam at 1030.




2. Field work:
 - Big Digger crew continued drilling and bolting on the top and bottom decks of TTF North node.
 - According to Terry Murray, no Sat work for his crew this week and they planned to mobilize the North node to the site on Tue next week.

3. Overtime reason:
Work two hours overtime for construction observation because contractor worked overtime.

Thanh V Le



Trans Engineer (D)/Asst. Struct. Rep

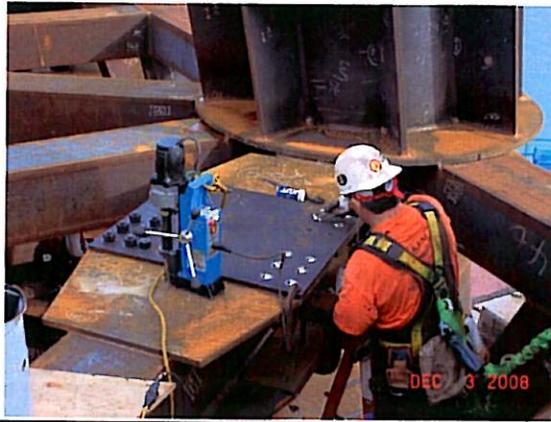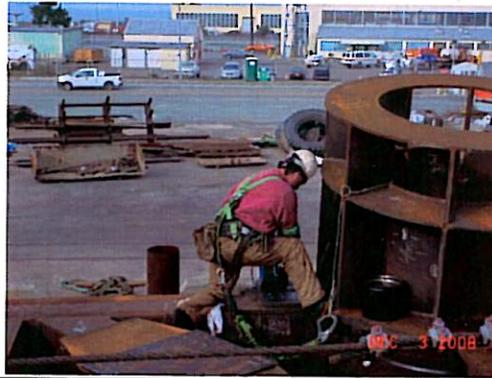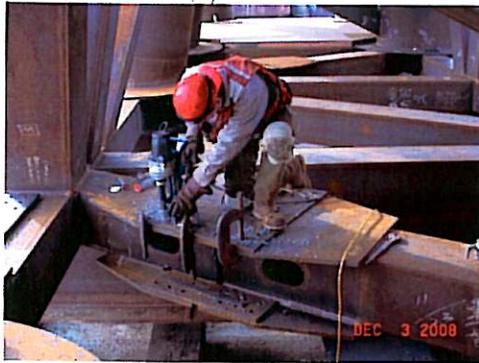

Drilling and bolting TTF North node
