

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 722
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 932
Form HC-10A (Rev. 6/80)	04-0120F4	Date	12/04/2008

Inspectors Hours	Start	0630	Stop	1700
Shift Hours	Start	0630	Stop	1700

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR - ABFJV

EQUIPMENT AND/OR LABOR:		HOURS - ITEM NO.										REMARKS		
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)	Regular	OT								IDLE OR DOWN	Name	Contractor
		Big Digger barge	8											
		DB # 5 Marine barge	0											
		APE 600 Vibration hammer	0											
		Delmag 100 - Diesel hammer	0											
		Superintendent	8	2									Terry Murray	Traylor Dutra
		Pile driver Journeyman	8	2									Gilbert Moya	Traylor Dutra
		Pile driver Journeyman	0	0									Adams Price	Traylor Dutra
		Operator	0	0									Joe Boracci	Traylor Dutra
		Pile driver Journeyman	8	2									Ventura Ochoa	Traylor Dutra
		Operator	0	0									Theo Roth	Traylor Dutra
		Pile driver Journeyman	0	0									Phillip Baker	Traylor Dutra
		Pile driver Journeyman	8	2									Robert Utley	Traylor Dutra
		Pile driver Journeyman	8	2									Bradly Mc Malley	Traylor Dutra
		Pile driver Journeyman	0	0									Lee Tacker	
		Pile driver Journeyman	0	0									Danny Vagas	Traylor Dutra
		Pile driver Journeyman	0	0									Stephen Mc Grew	Traylor Dutra
		Pile driver Journeyman	0	0									Jake Lavash	Traylor Dutra
		Pile driver Journeyman	0	0									Gary Lewis	Traylor Dutra
		Operator	8	2									Bud Germany	Traylor Dutra
		Operator	8	2									Steve Gordon	Traylor Dutra
		Pile driver Journeyman	8	2									Travis Logsdon	Traylor Dutra
		Operator	0	0									Joe Boracci	Traylor Dutra
		Operator	8	2									Ernie Hamilton	Traylor Dutra
		Pile driver Apprentice	8	2									Richard Hiebert J.	Traylor Dutra
		Pile driver Journeyman	0	0									Todd Labarb	Traylor Dutra
		Pile driver Journeyman	0	0									Richard Hiebert	Traylor Dutra
		Pile driver Journeyman	8	2									Randell Lesley	Traylor Dutra

Weather: Partly Cloudy Hi 67 °F, Lo 46 °F.

46.02

**Description of Operation:**

**Temporary Tower F – North Node driving frame assemble**


**Activities:**

1. Office work:
  - Review plans, special provisions, RFI and ABF submittals for TTF and TTG
  - Concrete pour team meeting for E2 cap beam at 1000.
  
2. Field work:
  - Big Digger crew continued drilling and bolting on the top and bottom decks of TTF North node.
  - To correct the issue  $< 50\text{mm}$  edge distance –bolt locations- the crew added eight bolts for South East diagonal beam (four bolts on the top and four bolts at the bottom of the beam connection), the crew added six bolts to the North West outer beam three on the top and three at the bottom of the beam.
  - E2 cap beam site visit for the concrete pour on Friday night.

3. Overtime reason:

Work two hours overtime for construction observation because contractor worked overtime.


Thanh V Le



Trans Engineer (D)/Asst. Struct. Rep



E2 pre pour site visit

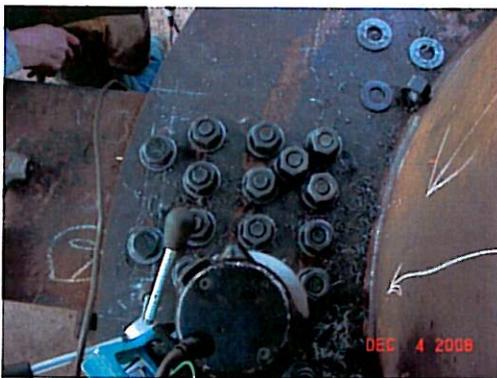

Additional bolts to edge distance  $< 50\text{ mm}$
