

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 723 & 724
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 933 & 934
Form HC-10A (Rev. 6/80)	04-0120F4	Date	12/05/2008 and 12/06/08

Inspectors Hours	Start	0630	Stop	0830
Shift Hours	Start	0630	Stop	0830

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR - ABFJV

EQUIPMENT AND/OR LABOR:		HOURS - ITEM NO.										REMARKS		
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)	Regular	OT								IDLE OR DOWN	Name	Contractor
		Big Digger barge	8											
		DB # 5 Marine barge	0											
		APE 600 Vibration hammer	0											
		Delmag 100 - Diesel hammer	0											
		Superintendant	8	2									Terry Murray	Traylor Dutra
		Pile driver Journeyman	8	2									Gilbert Moya	Traylor Dutra
		Pile driver Journeyman	8	2									Adams Price	Traylor Dutra
		Operator	0	0									Joe Boracci	Traylor Dutra
		Pile driver Journeyman	8	2									Ventura Ochoa	Traylor Dutra
		Operator	8	2									Theo Roth	Traylor Dutra
		Pile driver Journeyman	0	0									Phillip Baker	Traylor Dutra
		Pile driver Journeyman	8	2									Robert Utley	Traylor Dutra
		Pile driver Journeyman	8	2									Bradly Mc Malley	Traylor Dutra
		Pile driver Journeyman	0	0									Lee Tacker	
		Pile driver Journeyman	0	0									Danny Vagas	Traylor Dutra
		Pile driver Journeyman	0	0									Stephen Mc Grew	Traylor Dutra
		Pile driver Journeyman	0	0									Jake Lavash	Traylor Dutra
		Pile driver Journeyman	0	0									Gary Lewis	Traylor Dutra
		Operator	8	2									Bud Germany	Traylor Dutra
		Operator	0	0									Steve Gordon	Traylor Dutra
		Pile driver Journeyman	8	2									Travis Logsdon	Traylor Dutra
		Operator	0	0									Joe Boracci	Traylor Dutra
		Operator	8	2									Ernie Hamilton	Traylor Dutra
		Pile driver Apprentice	8	2									Richard Hiebert J.	Traylor Dutra
		Pile driver Journeyman	0	0									Todd Labarb	Traylor Dutra
		Pile driver Journeyman	8	2									Richard Hiebert	Traylor Dutra
		Pile driver Journeyman	8	2									Randell Lesley	Traylor Dutra

REC'D 09 JAN 05 #008190

Weather: Partly Cloudy Hi 67 °F, Lo 46 °F.

46.02

Description of Operation:

1. Temporary Tower F – North Node driving frame assemble
2. Concrete pour at E2 cap beam.


Activities:

1. Office work:
 - Review plans, special provisions, RFI and ABF submittals for TTF and TTG
2. Field work:
 - A. Temporary Tower F – North: 0630 - 1030**
 - Big Digger crew continued drilling and bolting on the top and bottom decks of TTF North node.
 - Big Digger crew tighten bolts and controlled the torque by Squirters DTI washers, the crew started bolt tighten on the top deck of the driving frame in the morning.
 - B. E2 cap beam**
 - From 8:30 PM Friday to 0830 AM Sat, work at the concrete pour E2 cap beam: monitored concrete quality at South concrete pump, concrete temperatures were from 57°F to 64°F, there was no segregated concrete found.
 - Cement, water, aggregates and admixtures were within limited.
 - The DCI testers performed flow tests for each truck for first 35 trucks, range of the flows were from 27" to 31".

3. Overtime reason:

Worked eight hours overtime for construction observation because contractor worked overtime. (FRIDAY 0630 - 1030; 2000 - 0000)
↳ (SATURDAY 0000 - 0830)

Thanh V Le




Trans Engineer (D)/Asst. Struct. Rep



Four additional bolts on top/ four at bottom



Continued drilling

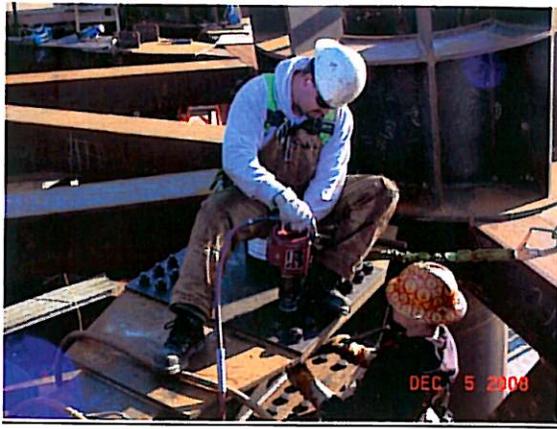

Tightening bolts using DTI washers



SCC concrete flow test.
