

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 726
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 936
Form HC-10A (Rev. 6/60)	04-0120F4	Date	12/08/2008

Inspectors Hours	Start	0630	Stop	1700
Shift Hours	Start	0630	Stop	1700

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR - ABFJV

EQUIPMENT AND/OR LABOR:		HOURS - ITEM NO.										REMARKS		
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)	Regular	OT								IDLE OR DOWN	Name	Contractor
		Big Digger barge	8											
		DB # 5 Marine barge	0											
		APE 600 Vibration hammer	0											
		Delmag 100 - Diesel hammer	0											
		Superintendant	8	2									Terry Murray	Traylor Dutra
		Pile driver Journeyman	8	2									Gilbert Moya	Traylor Dutra
		Pile driver Journeyman	0	0									Adams Price	Traylor Dutra
		Operator	0	0									Joe Boracci	Traylor Dutra
		Pile driver Journeyman	8	2									Ventura Ochoa	Traylor Dutra
		Operator	8	2									Theo Roth	Traylor Dutra
		Pile driver Journeyman	8	2									Phillip Baker	Traylor Dutra
		Pile driver Journeyman	8	2									Robert Utley	Traylor Dutra
		Pile driver Journeyman	0	0									Bradly Mc Malley	Traylor Dutra
		Pile driver Journeyman	0	0									Lee Tacker	
		Pile driver Journeyman	0	0									Danny Vagas	Traylor Dutra
		Pile driver Journeyman	0	0									Stephen Mc Grew	Traylor Dutra
		Pile driver Journeyman	0	0									Jake Lavash	Traylor Dutra
		Pile driver Journeyman	0	0									Gary Lewis	Traylor Dutra
		Operator	8	2									Bud Germany	Traylor Dutra
		Operator	0	0									Steve Gordon	Traylor Dutra
		Pile driver Journeyman	8	2									Travis Logsdon	Traylor Dutra
		Operator	8	2									Ernie Hamilton	Traylor Dutra
		Pile driver Apprentice	0	0									Richard Hiebert J.	Traylor Dutra
		Pile driver Journeyman	0	0									Todd Labarb	Traylor Dutra
		Pile driver Journeyman	0	0									Richard Hiebert	Traylor Dutra
		Pile driver Journeyman	8	2									Randell Lesley	Traylor Dutra

PROJECT-09 JAN 05 #08191

Weather: Partly Cloudy Hi 67 °F, Lo 46 °F.

46-02

Description of Operation:

1. Temporary Tower F – North Node driving frame assemble
2. Concrete pour at E2 cap beam.


Activities:

1. Office work:
 - Review plans, special provisions, RFI and ABF submittals for TTF and TTG
 - Staff meeting 0800
2. Field work:
 - The Big Digger crew continued drilling and bolting top deck South East corner of TTF North node.
 - The crew installed working platform on top deck.
 - Installed safety handrail on top deck.

3. Overtime reason:

Worked two hours overtime for construction observation because contractor worked overtime


Thanh V Le



Trans Engineer (D)/Asst. Struct. Rep



Bolt tightening process

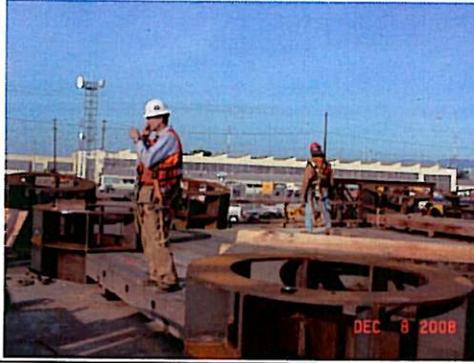

Installed working platform on top deck
