

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 727
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 937
Form HC-10A (Rev. 6/80)	04-0120F4	Date	12/09/2008

Inspectors Hours	Start	0630	Stop	1700
Shift Hours	Start	0630	Stop	1700

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR - ABFJV

EQUIPMENT AND/OR LABOR:		HOURS - ITEM NO.										REMARKS		
Equip. #	N O M E N	DESCRIPTION (Of Equipment or Labor)	Regular	OT								IDLE OR DOWN	Name	Contractor
		Big Digger barge	0											
		DB # 5 Marine barge	8											
		APE 600 Vibration hammer	0											
		Delmag 100 - Diesel hammer	0											
		Superintendant	8	2									Terry Murray	Traylor Dutra
		Pile driver Journeyman	8	2									Gilbert Moya	Traylor Dutra
		Pile driver Journeyman	8	2									Adams Price	Traylor Dutra
		Operator	8	2									Joe Boracci	Traylor Dutra
		Pile driver Journeyman	8	2									Ventura Ochoa	Traylor Dutra
		Operator	8	2									Theo Roth	Traylor Dutra
		Pile driver Journeyman	0	0									Phillip Baker	Traylor Dutra
		Pile driver Journeyman	8	2									Robert Utley	Traylor Dutra
		Pile driver Journeyman	8	2									Bradly Mc Malley	Traylor Dutra
		Pile driver Journeyman	0	0									Lee Tacker	
		Pile driver Journeyman	0	0									Danny Vagas	Traylor Dutra
		Pile driver Journeyman	0	0									Stephen Mc Grew	Traylor Dutra
		Pile driver Journeyman	0	0									Jake Lavash	Traylor Dutra
		Pile driver Journeyman	0	0									Gary Lewis	Traylor Dutra
		Operator	0	0									Bud Germany	Traylor Dutra
		Operator	0	0									Steve Gordon	Traylor Dutra
		Pile driver Journeyman	8	2									Travis Logsdon	Traylor Dutra
		Operator	0	0									Ernie Hamilton	Traylor Dutra
		Pile driver Apprentice	8	2									Richard Hiebert J.	Traylor Dutra
		Pile driver Journeyman	8	2									Todd Labarb	Traylor Dutra
		Pile driver Journeyman	8	2									Richard Hiebert	Traylor Dutra
		Pile driver Journeyman	8	2									Randell Lesley	Traylor Dutra

REC'D 09 JAN 05 #008192

Weather: Partly Cloudy Hi 67 °F, Lo 46 °F.


46-02


**Description of Operation:**

**1. Temporary Tower F – North driving frame piling (24hrs operation)**

**Activities:**

1. Office work:
  - Review plans, special provisions, RFI and ABF submittals for TTF and TTG
2. Field work:
  - BD5 crew stabbed and vibrated four vertical piles after positioning the North driving frame.
  - Phil Thorson and his team (SRS consultant) were present for mammal monitoring.
  - BD5 crew continued tightening bolts for bottom frame.
3. Overtime reason:  
Worked two hours overtime for construction observation because contractor worked overtime

Thanh V Le  Trans Engineer (D)/Asst. Struct. Rep

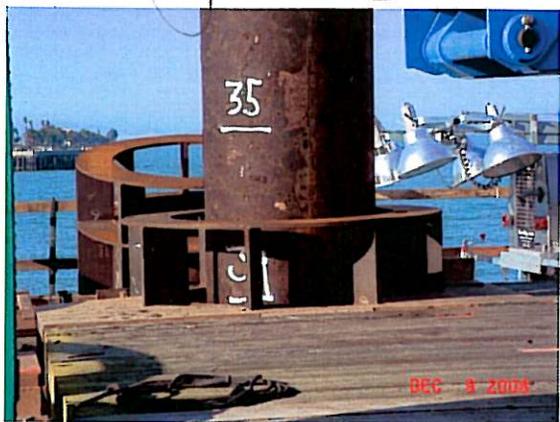

Pile after stabbed



Pile length bottom section



Vibration hammer APE 600
