

TOLL PROGRAM/DIST. 4 CONSTR.

Job Stamp:
04-SF-80-13.2/13.9 04-0120F4
SFOBB SAS
San Francisco Co. in San Francisco
Fm 0.6 km to 1.3 km East of Yerba Buena
Tunnel East Portal

Report No. **46.B**
Date the Shift Began: **11/7/08**
 NIGHTWORK **FRIDAY**
Shift Hrs Start **6:30** Stop **17:00**
Engineer's Hrs Start **7:30** Stop **18:00**

ASSISTANT RESIDENT ENGINEER'S DAILY BRIDGE REPORT

Location: Pier E2	7-day const. cal.: 695	Weather: Sunny & Cold
Remark:	Project work day: 905	

Description of Operation: Placement of Reinforcing Steel, Cooling Pipes, Panel Forms...

			HOURS - ITEM NO.									
EQUIPMENT AND/OR LABOR:			Structural Concrete, Bridge	Structural Concrete, Bridge	RT	OT				Prime	Classification	Prime / Sub
EQPT. NO.	NO. MEN	DESCRIPTION (Of Equipment or Labor)										
Pier E2												
		Pile Driver	8.00	2.00						Terry Cronk	General Foreman	p
		Pile Driver	8.00	2.00						Ed Mendoza	Journeyman	p
		Pile Driver	8.00	2.00						Jason Matlock	Journeyman	p
		Pile Driver	8.00	2.00						Alan Briney	Journeyman	p
		Pile Driver	8.00	2.00						Luke Paulk	Journeyman	p
		Pile Driver	8.00	2.00						Ben Neal	Foreman	p
		Laborer								Jon Van Brusslen	Foreman	S
		Iron worker								Regis Garcia	Journeyman	S
		Iron worker								Jose Cervantes	Journeyman	S
		Iron worker								Jose Juarque	Journeyman	S
		Iron worker								Jorge Lopez	Journeyman	S
		Iron worker								Roberto Berber	Journeyman	S
		Iron worker								Juan Serano	Journeyman	S
		Iron worker								Daniel Gomez	Journeyman	S
		Iron worker								Jose Torres	Journeyman	S
		Iron worker								Eduardo Sanchez	Journeyman	S
		Iron worker								Byron Contreras	Laborer	S
		Pile Driver	8.00	2.00						Leo Vega	Foreman	p
		Pile Driver	8.00	2.00						Karl Nisley	Journeyman	p
		Pile Driver	8.00	2.00						Harry Wheat	Journeyman	p
		Pile Driver	8.00	2.00						Kim June	Journeyman	p
		Pile Driver	8.00	2.00						Richard Yambao	Apprentice	p
		Deck Engineer	8.00	2.00						Ryan Oku	Journeyman	p
		Operator	8.00	2.00						Kevin Fitzgerald	Journeyman	p
		Oiler	8.00	2.00						Doug Greene	Apprentice	p
		Operator	8.00	2.00						Mark Mom	Journeyman	p
		Oiler	8.00	2.00						Kevin Alger	Journeyman	p
		Ringer Barge #1	8.00	2.00						Manitowac Crane		
		Ringer Barge #2	8.00	2.00						Manitowac Crane		
002062		Lincoln Electric								Vantage 500	6008088	
002083		Lincoln Electric								Vantage 500	6008091	
002068		MQ Power Generator								Whisperwatt 25	6007939	
002069		MQ Power Generator								Whisperwatt 25		


JAN 06 10:08:17

Job Stamp:
04-SF-80-13.2/13.9 04-0120F4
SFOBB SAS
San Francisco Co. in San Francisco
Fm 0.6 km to 1.3 km East of Yerba Buena
Tunnel East Portal

Report No. **46.B**
Date the Shift Began: **11/7/08**
 NIGHTWORK **FRIDAY**
Shift Hrs Start 6:30 Stop 17:00
Engineer's Hrs Start 7:30 Stop 18:00

ASSISTANT RESIDENT ENGINEER'S DAILY BRIDGE REPORT

Location: Pier E2		7-day const. cal.: 695	Weather: Sunny & Cold
	Honda 115 Horse Skiff		
002075	Ingersoll Rand P185R		
	Lincoln Electric	8	Vantage 500 768-50-4005
	Lincoln Electric	8	Vantage 500 468-50-4009
2381	MQ Power Generator	8	Whisperwatt

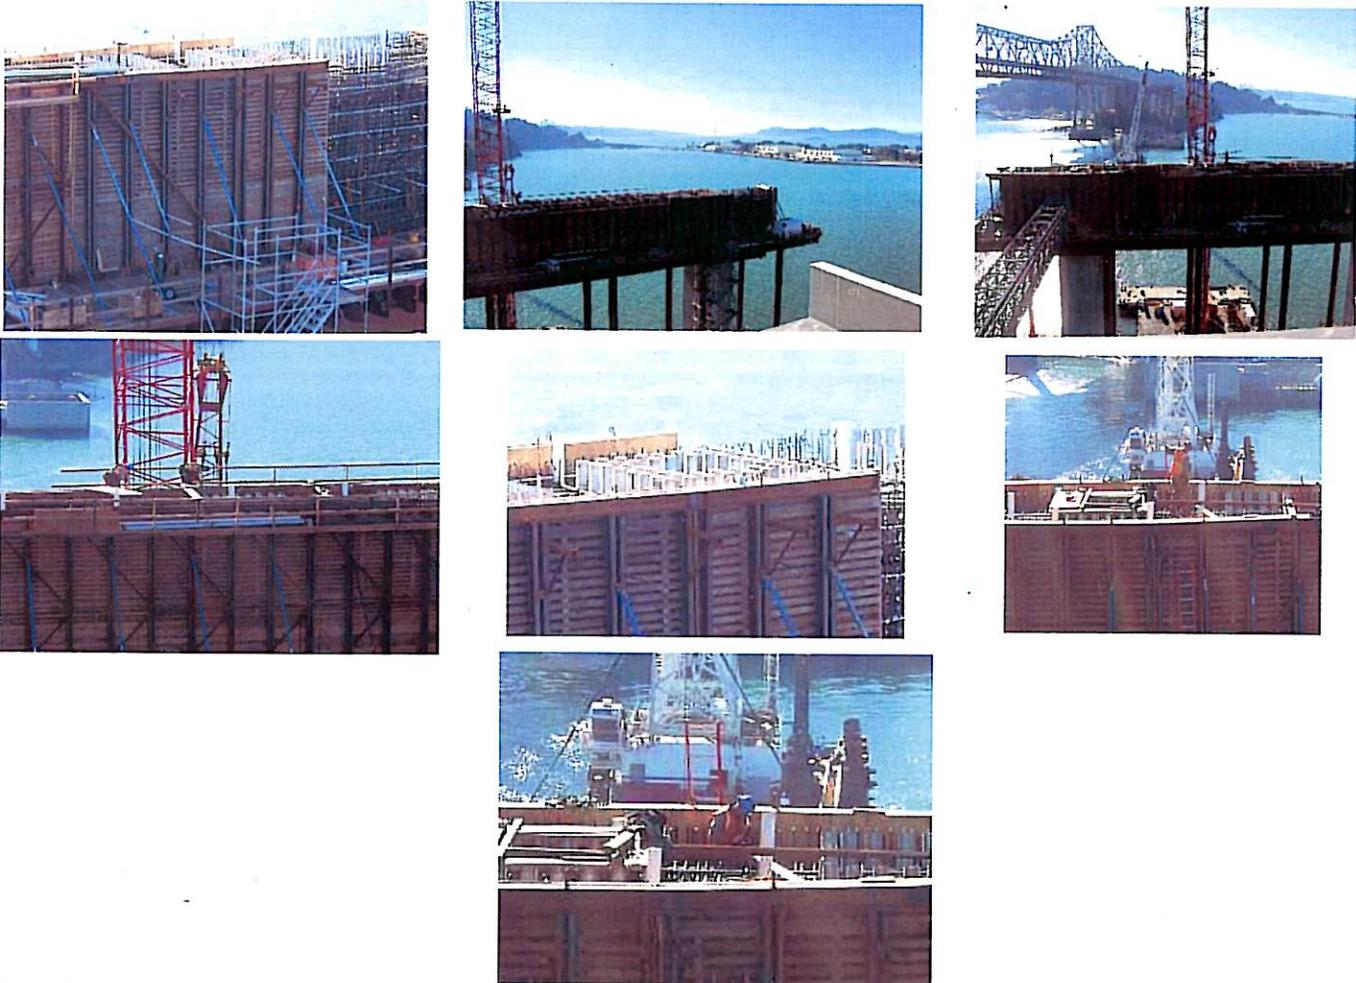

The workload was quite light at this location today as the ABF safety officer imposed an access restriction to the cross-beam for the iron workers until a walkway with handrail is installed and other safety features as discussed two days ago in the Team Concrete Meeting were in place.

The ABF employees were in the throes of completing the cooling pipes and placing the 1" bolts for the panel forms for which they need to drill holes in the panel forms as this task had not been done prior to the installation of the panel forms.

The PT Ducts installation has to wait until the RPS crew comes back. This could happen on Monday, as M. McDonald told me that over the weekend the walkway will be complete and that the completion of the walkway is the main reason for the ABF crew working OT on Saturday. Some of the photos show the railing construction is underway on the West side of the cross-beam as the walkway and the railings on the East side is only partially complete.

Materials:

Insp. Hrs.	
REG: 8.0	INTERMITTENT
OT: [yellow box]	INSPECTION

Saman Soheili
Saman Soheili

ASR/CT
Title
