

Job Stamp

04-0120F4  
SFOBB SAS

Construction Calendar no. 705

Project working days no. 915

Date 11/17/2008

Inspectors Start 07:00 Stop 18:30

Hours

Shift Hours Start 07:00 Stop 23:00

### Assistant Structure Rep.'s Daily Report

Location & Description of Operation	SAS-Temporary towers, Tower C erection (07:00~15:00), Foundation C (15:00~18:30)
Weather	HI: 67 F Low: 51 F Partly cloudy

Equipment and/or labor			Hours - ITEM no.							Remarks
Equip no.	# personnel	Description (of equipment or labor)	Regular	OT	DT	Rental			IDLE	
	C	Liebherr LR 1300	8							ABF
006-18-4293	C	Ingresoll Compressor	8							ABF
481-93-6013	R	Gnie Boom lift	8							ABF
544D-10	R	Gradall Forklift	8							ABF
	1	Ed Meyer	8							ABF Foreman (erection)
	1	Carlos Valverde								ABF Foreman (bolt)
	1	Matt Chamberlain								ABF Iron worker
	1	James Sturgeon								ABF Iron worker
	1	Serina Lafleur								ABF Iron worker
	1	David Lucero	8							ABF Iron worker
	1	Mike Naday								ABF Iron worker
	1	Jerry Kubala, Jr.	8							ABF Iron worker
	1	Alex Bartlett								ABF Iron worker
	1	Ernesto Fresquez	8							ABF Iron worker
CB KELSO	C	Derick Barge	4							TD
12-262	C	DB Crane	4							TD
Morty	C	Material Barge	4							TD
NM27633	C	325 DL Cat Excavator	4							TD
L-624	C	Light Tower	4							TD
L-627	C	Light Tower	4							TD
		Bud Germany	4							DB5 operator
		Kurt Dilard	4							Pile Driver
		Bonisue Coburn	4							Excavator operator
		Alejandro A Perez	4							Pile Driver
		Kevin Ingles	4							Pile Driver
		Dan Clark	4							Captain
		Dan Lopez	4							Deckhand

#### Description of Operation:

- > Daily activity of contractors
  - ABF pretensioned bolts at the south panel of E3-E4 (see Figs 1 and 2).
  - ABF covered hand holes (see Figs 3 and 4)
  - ABF carried out crane maintenance (see Fig 5).
  - T.D. set up turbidity curtains and removed rock (see Fig 6).
  - See Mark Vilcheck and Art Pannu's diaries for contractors' activities and comments.

46.02

REC'D 09 JAN 06 10:00:00

➤ Note

- At 15:40, during the operation of turning around the barge, Tug boat at the south side hit the far north panel of Tower D. I saw cracks and reported this accident to Mark Vilcheck and Art Pannu.
- Attend a staff meeting from 08:00
- 3 hours O.T.



Fig 1



Fig 2

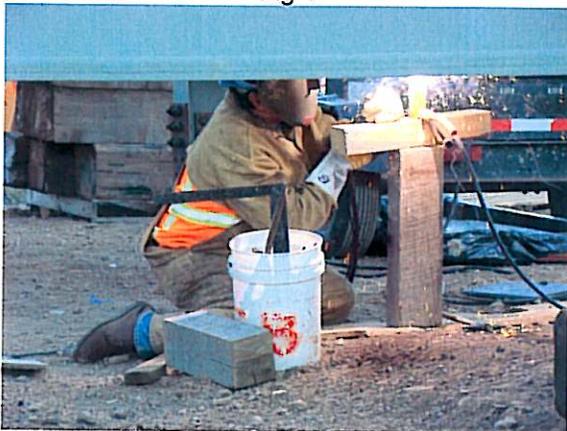


Fig 3

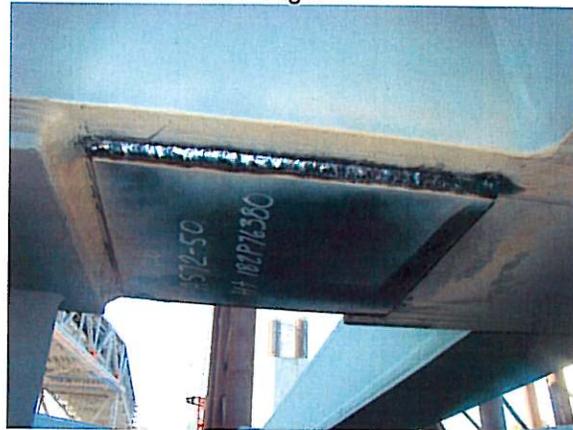


Fig 4



Fig 5



Fig 6

Inspector:  
SeongHyeok Song

Trans Engineer (Civil) / Asst. Struct. Rep
