

Job Stamp
04-0120F4
SFOBB SAS

Construction Calendar no.	707
Project working days no.	917
Date	11/19/2008
Inspectors	Start 12:00 Stop 23:00
Hours	
Shift Hours	Start 07:00 Stop 23:00

### Assistant Structure Rep.'s Daily Report

Location & Description of Operation	SAS-Temporary towers, Tower C erection, Foundation C rock removal
Weather	HI: 67 F Low: 51 F Partly cloudy

Equipment and/or labor			Hours – ITEM no.							Remarks
Equip no.	# personnel	Description (of equipment or labor)	Regular	OT	DT	Rental			IDLE	
CB KELSO	C	Derick Barge	8	3						TD
12-262	C	DB Crane	8	3						TD
Morty	C	Material Barge	8	3						TD
NM27633	C	325 DL Cat Excavator	8	3						TD
L-624	C	Light Tower	4							TD
L-627	C	Light Tower	4							TD
		Bud Germany	8							DB5 operator (Night Shift)
		Kurt Dilard	8							Pile Driver (Night Shift)
		Bonisue Coburn	8							Excavator operator (Night Shift)
		Alejandro A Perez	8							Pile Driver (Night Shift)
		Kevin Ingles	8							Pile Driver (Night Shift)
		Dan Clark	8							Captain (Night Shift)
		Dan Lopez	8							Deckhand (Night Shift)
		Bill White	3							Crane operator (Day Shift)
		Derick Edwards	3							Pile Driver (Day Shift)
		Joe Barato	3							Excavator operator (Day Shift)
		Matt Morton	3							Pile Driver (Day Shift)

**Description of Operation:**

- Daily activity of contractors
  - T.D. continues to remove rocks around Tower C (see Fig 1).
  - ABF removed the pedestals, which were already placed.
  - See Mark Vilcheck and Art Pannu's diaries for contractors' activities and comments.
- Note
  - Notice that ABF writes down words "ABF OK" showing that ABF completed pretensioning, as Scott, Chuck and I agreed (see Fig 2).
  - Dan Dunn informed that ABF completed pretensioning bolts at the lower portion of Tower C east line. Then, I inspected the bolts and marked the bolts, which need to be turned more. Let James Sturgeon know about them (see Fig 3).
  - 2 ½ hours O.T.

46-02



Fig 1



Fig 2

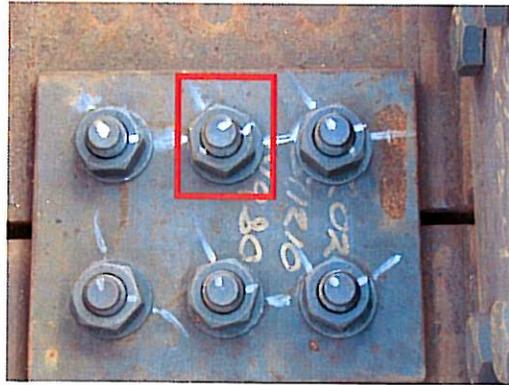


Fig 3

Inspector:  
SeongHyeok Song

Trans Engineer (Civil) / Asst. Struct. Rep
