

Job Stamp
04-0120F4
SFOBB SAS

Construction Calendar no.	709		
Project working days no.	919		
Date	11/21/2008		
Inspectors	Start	07:00	Stop 17:30
Hours			
Shift Hours	Start	06:30	Stop 15:00

Assistant Structure Rep.'s Daily Report

Location & Description of Operation	SAS-Temporary towers, Tower C erection, Foundation C rock removal
Weather	HI: 67 F Low: 51 F Partly cloudy

Equipment and/or labor			Hours – ITEM no.						Remarks
Equip no.	# personnel	Description (of equipment or labor)	Regular	OT	DT	Rental		IDLE	
	C	Liebherr LR 1300	8						ABF
006-18-4293	C	Ingresoll Compressor	8						ABF
481-93-6013	R	Gnie Boom lift	8						ABF
544D-10	R	Gradall Forklift	8						ABF
	1	Ed Meyer	8						ABF Foreman (erection)
	1	Carlos Valverde	8						ABF Foreman (bolt)
	1	Matt Chamberlain							ABF Iron worker
	1	James Sturgeon							ABF Iron worker
	1	Serina Lafleur							ABF Iron worker
	1	David Lucero	8						ABF Iron worker
	1	Mike Naday	8						ABF Iron worker
	1	Jerry Kubala, Jr.							ABF Iron worker
	1	Alex Bartlett	8						ABF Iron worker
	1	Ernesto Fresquez	8						ABF Iron worker
	1	Casey Lux							ABF Iron worker
CB KELSO	C	Derick Barge	8						TD
12-262	C	DB Crane	8						TD
Morty	C	Material Barge	8						TD
NM27633	C	325 DL Cat Excavator	8						TD
L-624	C	Light Tower	4						TD
L-627	C	Light Tower	4						TD
		Bill White	3						Crane operator (Day Shift)
		Derick Edwards	3						Pile Driver (Day Shift)
		Joe Barato	3						Excavator operator (Day Shift)
		Matt Morton	3						Pile Driver (Day Shift)

Description of Operation:

- Daily activity of contractors
 - ABF continues to pretension bolts at E3 to E4 (see Fig 1).
 - T.D. continues to remove rocks and restore shoreline at foundation C (see Figs 2 and 3).
 - See Mark Vilcheck and Art Pannu's diaries for contractors' activities and comments.
- Note
 - Notice that salt water in baker tank is used for dust control. Reported it to Art Pannu and Robert Wang. See Art and Robert's diaries for detailed follow-ups (see Fig 4).
 - Meeting between CT (Mark Vilcheck, Francis, Laura and Art), ABF (Bill O'Sullivan) and T.D. on restoring shoreline at foundation C. See their diaries for the decision made and comments. See the attachment #1 for original shoreline before construction starts.
 - 2 hours O.T.

RECT*09 JAN-06 #008328

4602

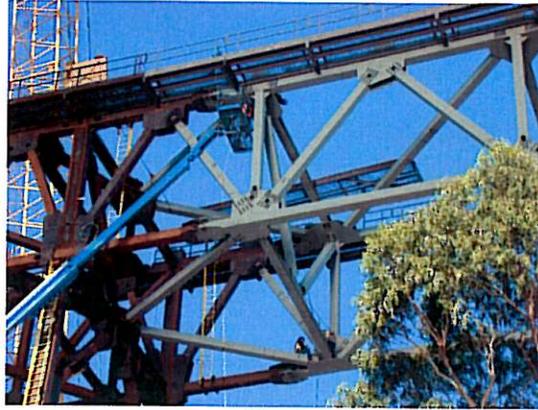


Fig 1

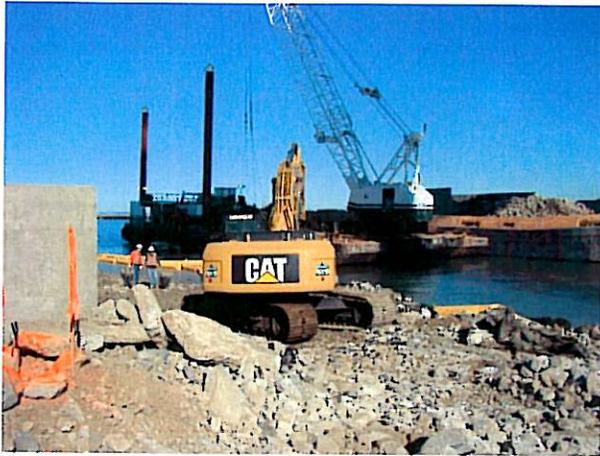


Fig 2



Fig 3




Fig 4



Inspector:


SeongHyeok Song

Trans Engineer (Civil) / Asst. Struct. Rep

Attachment #1

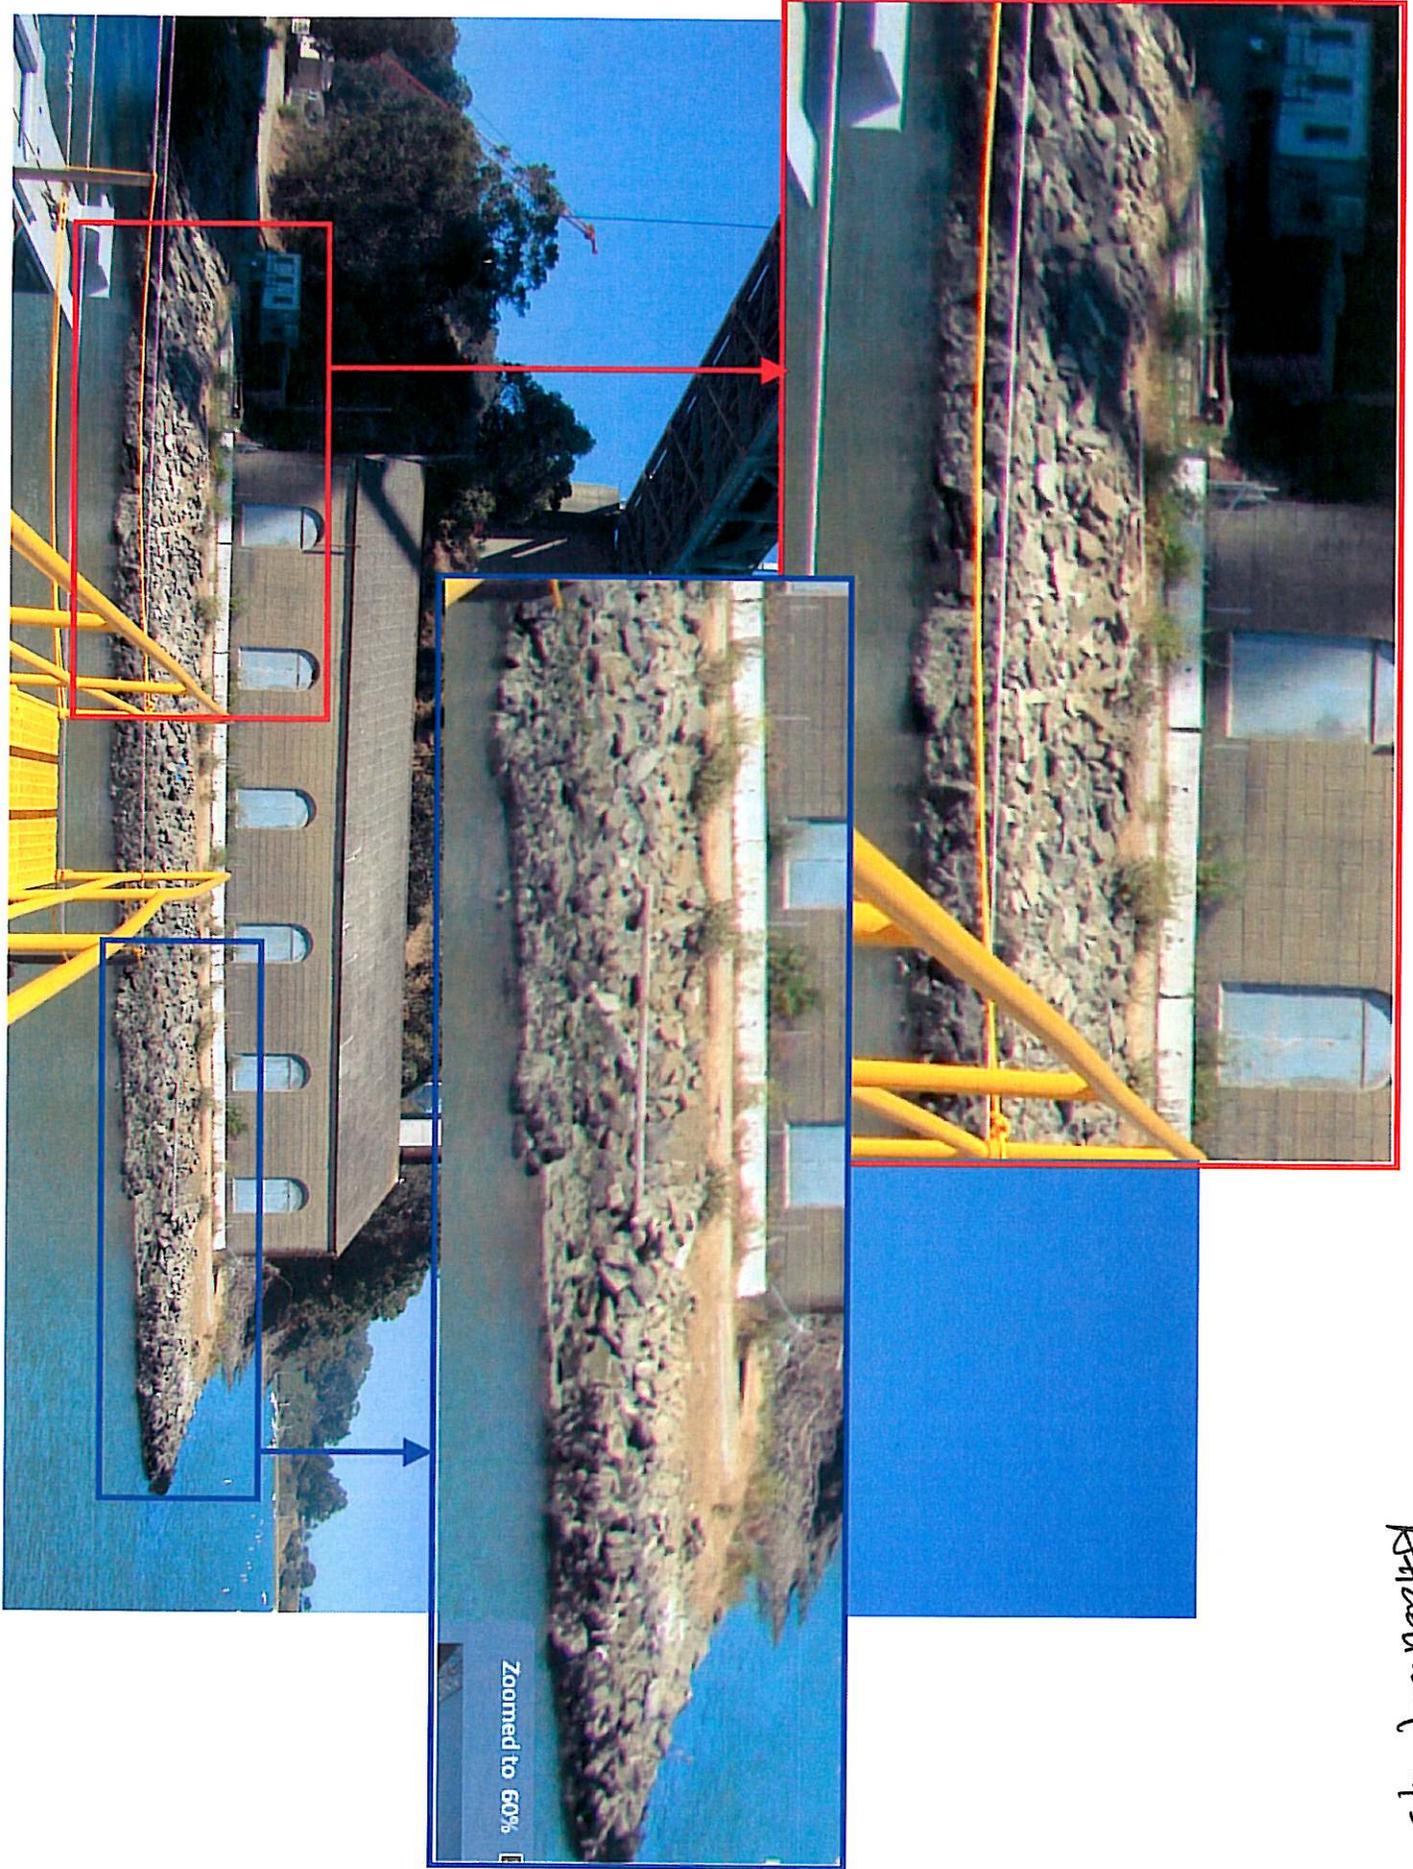

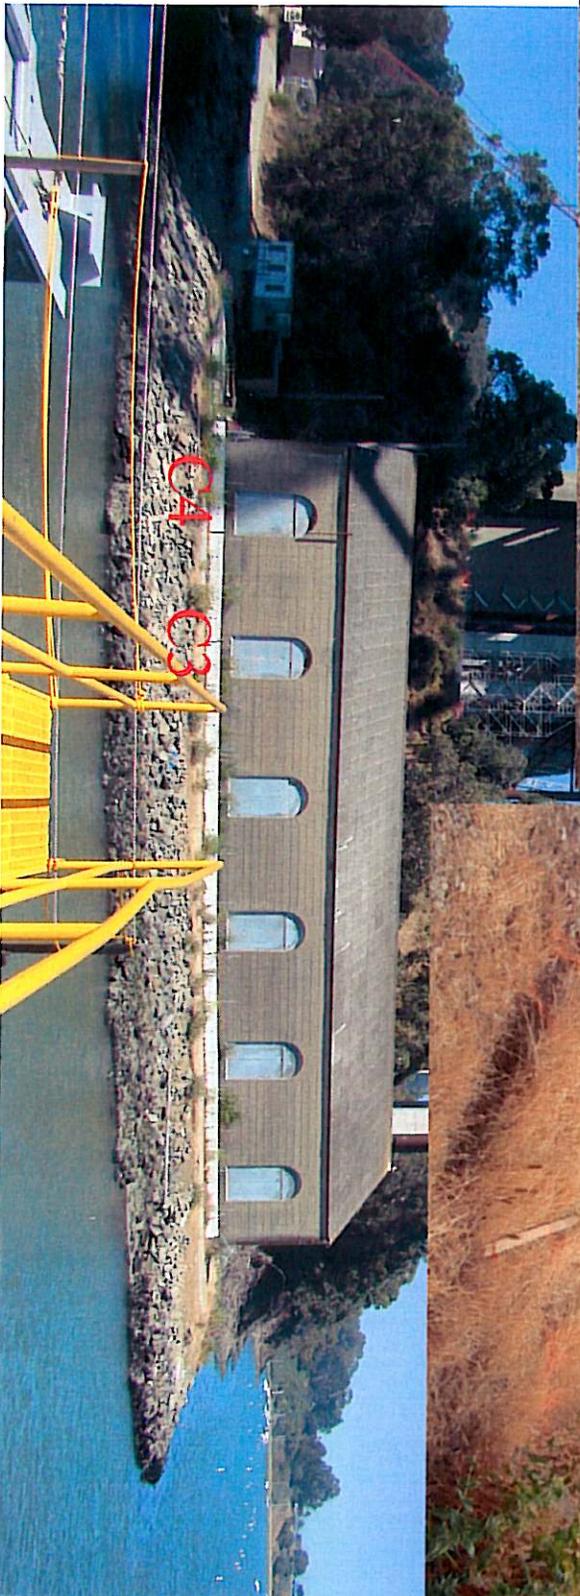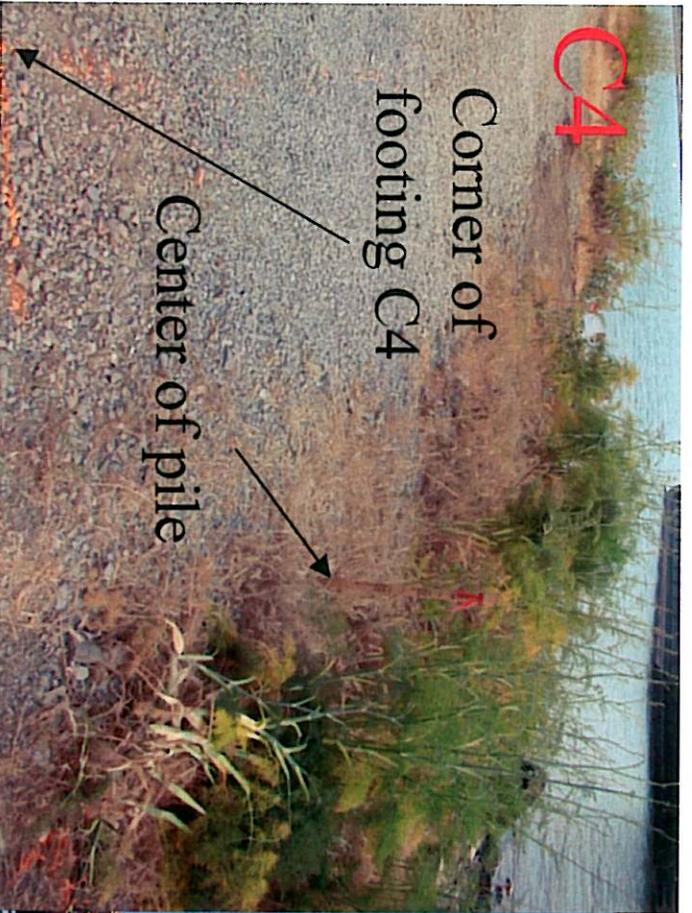

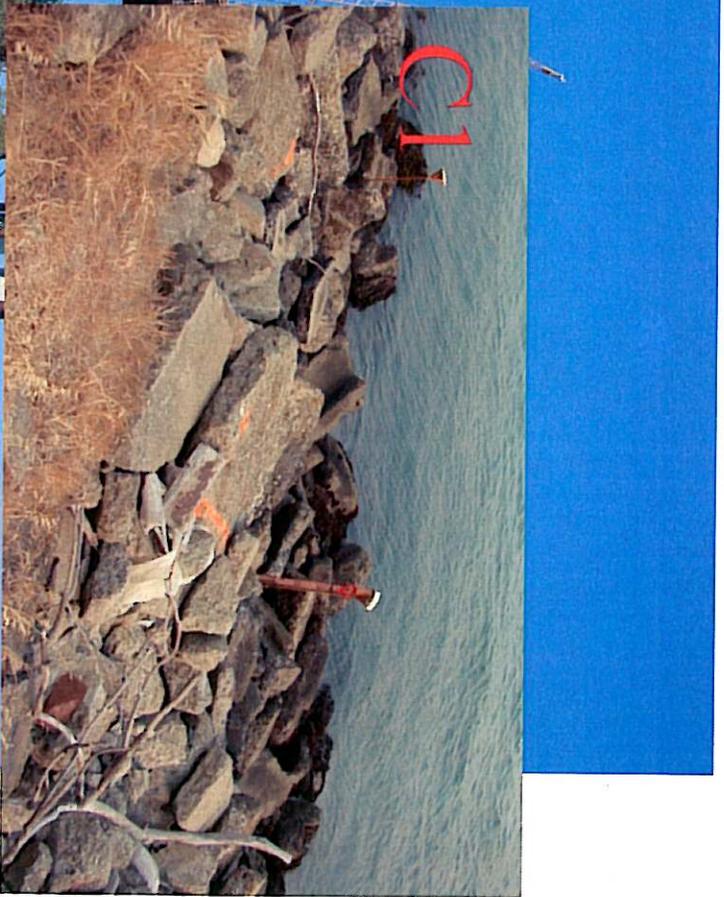

C2

C1
