

Job Stamp

04-0120F4  
SFOBB SAS

Construction Calendar no. 722

Project working days no. 932

Date 12/04/2008

Inspectors Start 06:00 Stop 16:30

Hours

Shift Hours Start 06:30 Stop 15:00

**Assistant Structure Rep.'s Daily Report**

Location & Description of Operation	SAS-Temporary towers, Pier 7
Weather	HI: 64 F Low: 49 F Partly cloudy/ foggy

Equipment and/or labor			Hours - ITEM no.						Remarks
Equip no.	# personnel	Description (of equipment or labor)	Regular	OT	DT	Rental		IDLE	
	C	4100W crane	8						ABF
006-18-4293	C	Ingresoll Compressor	8						ABF
481-93-6013	R	Gnie Boom lift							ABF
	1	Jeff Scott	8						ABF crane operator
	1	Ed Meyer	8						ABF Foreman (erection)
	1	Carlos Valverde	8						ABF Foreman (bolt)
	1	Matt Chamberlain	8						ABF Iron worker
	1	James Sturgeon	8						ABF Foreman (erection)
	1	Serina Lafleur							ABF Iron worker
	1	David Lucero	8						ABF Iron worker
	1	Mike Naday	8						ABF Iron worker
	1	Jerry Kubala, Jr.	8						ABF Iron worker
	1	Alex Bartlett	8						ABF Iron worker
	1	Casey Lux	8						ABF Iron worker
	1	Ernesto Fresquez	8						ABF Iron worker
	1	Jason Kent	8						ABF Iron worker
NM27633	C	325 DL Cat Excavator						8	TD

**Description of Operation:**

- Daily activity of contractors
  - ABF got the irons (E4-E6).
  - See Damon's diary for T.D. subcontractor activities.
  - See Mark Vilcheck and Art Pannu's diaries for contractors' activities and comments.
- Note
  - Spoke to Danny Dunn regarding the bolt inspection. He told me that the work on the island is done. So talk to John. I spoke to Mark regarding the conversation. He communicated with John to set up a schedule on the inspection. .
  - Spoke to Danny Dunn on the crane certificate. He referred to Jerry Kent, who referred to David. Finally, I met David and take a photo of the certificate.
  - Attend a T.T. design meeting from 15:00.
  - I talked to John that CT needs a safe access to inspect bolts. John told me that it is not necessary to provide man-basket to us because crane is not on-site and ironworkers works without man-basket. He thinks that CT should work under same environment with iron-workers, e.g. walk on irons wearing harness and lanyard. Gil told me that CT employee are not supposed to work under the same environment that Ironworkers do.

46.02



Fig 1

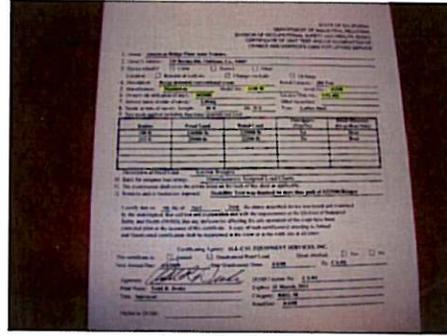


Fig 2

Inspector:  
SeongHyeok Song

Trans Engineer (Civil) / Asst. Struct. Rep
