

STATE OF CALIFORNIA  
DEPARTMENT OF TRANSPORTATION  
Contract 0120F – SFOBB – SAS Superstructure  
Week Ending 2008-11-21

Tuesday November 18, 2008 – Observation via Engineer’s Boat between 0930 and 1200:  
Clear, Cool, Breeze

- E2 – West elevation from water level – Bulkhead form panels in place



**Tightening through bolt nuts on Bulkhead forms (West Elevation)**




REC'D '09 JAN 12 #008351

46 02


**E2 West Elevation Bulkhead forms – note access walkway at top**



**E2 – South end form – note cooling system piping**

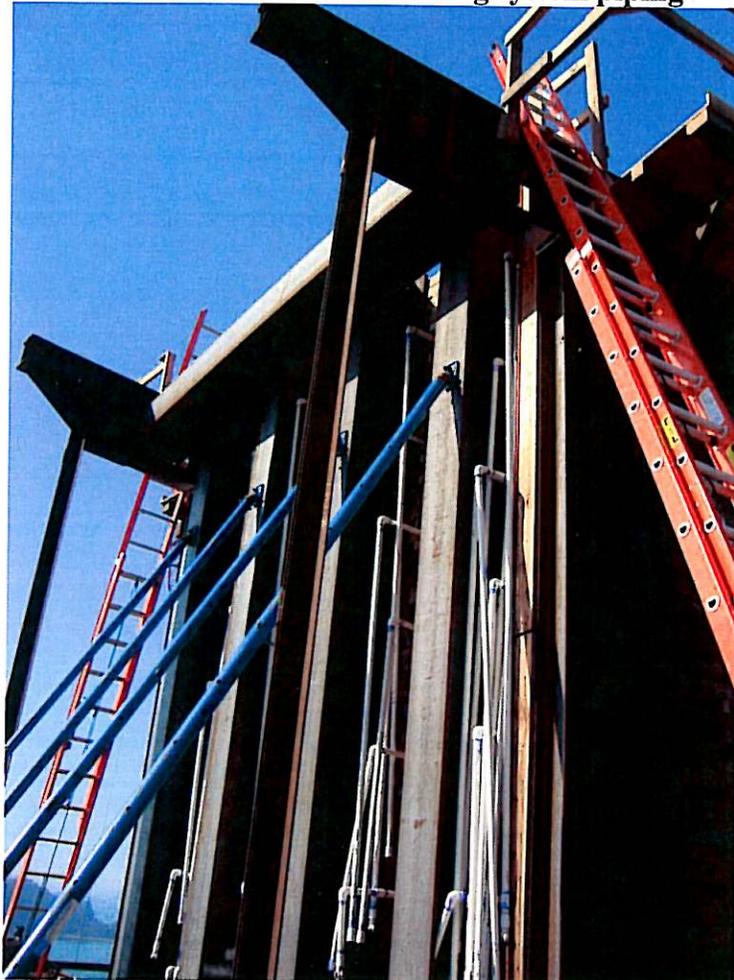

**E2 East Elevation – forms in place**

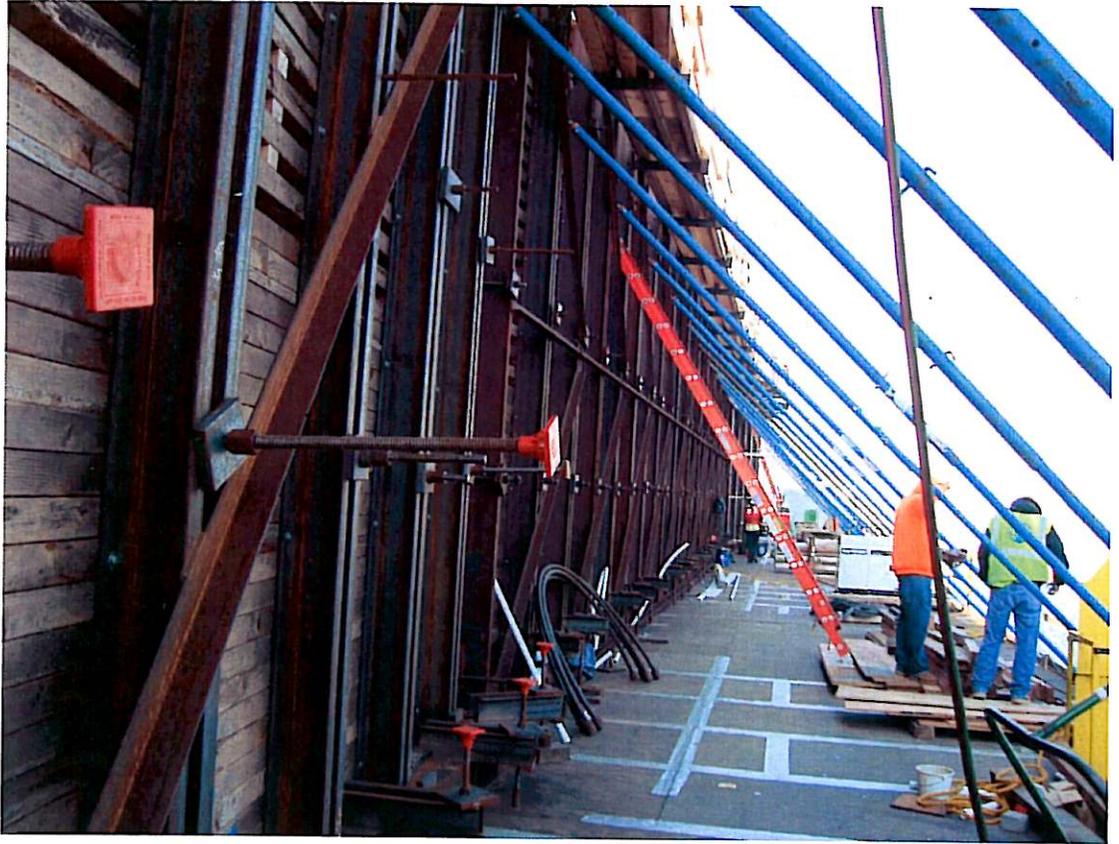

**E2 View from Skyway – Northerly portion**



**E2 View from Skyway – Southerly portion – Target for pour date Night of 5-Dec-2008**



• **TT “F” East Bound Driving Frame – View from East**



**TT "F" Pile-frame Plate welding**



**Close up of weld**



- TT “D” – No observed activity



- TT “C” Area – removing rock fill



**Back hoe Loading into bin**



**Crane flying rock bin**



**Crane dumping rock bin on to barge**



- **Temporary Tower "C" E Line – being assembling at Pier 7**



**More Temporary Tower "C" E line assembly @ Pier 7**



**Temporary Tower "C" E Line – view from Engineer's Boat**



- **View of W2 and Temporary Trusses W Line & E Line (with E3+ extension recently in place)**



**Friday November 21, 2008 Observation from Yerba Buena Island between 1000 and 1230:  
Clear, Cool, Calm**

- **E2 View of top of W2**



- **TT “D” – ( Between Area C rock removal Crane & Barge and TT “F” E Line Driving Frame) – No observed activity**




- **View of TT “F” E Line Driving Frame from top of W2**



**TT "F" W Line Driving Frame @ Pier 7 being assembled (Arrived Job-site 11-19-08)**



**Another view of TT "F" W Line Driving Frame being assembled**

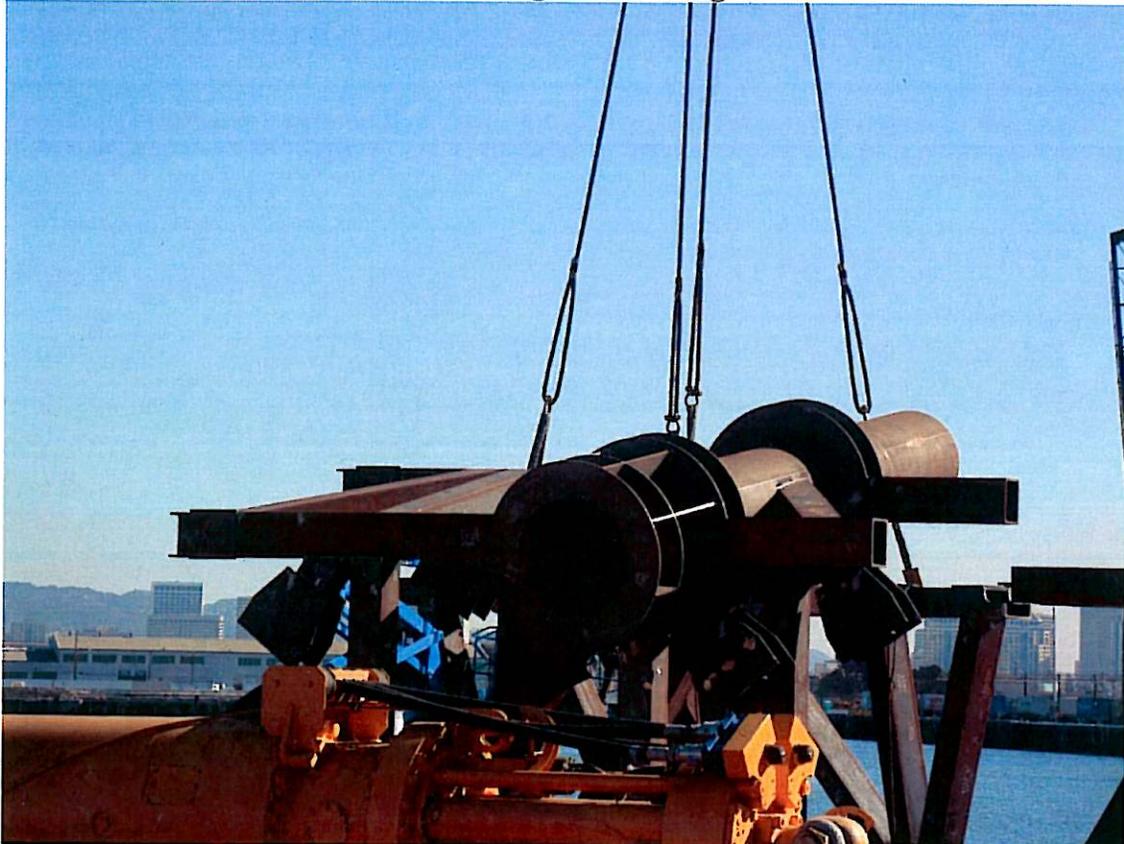

- Area "C" Rock removal continues



Area "C" showing status of rock removal




**Back Hoe loading Rock Bin**



**Crane loading rock on to barge**



**TT "C" E Line first lift in place**

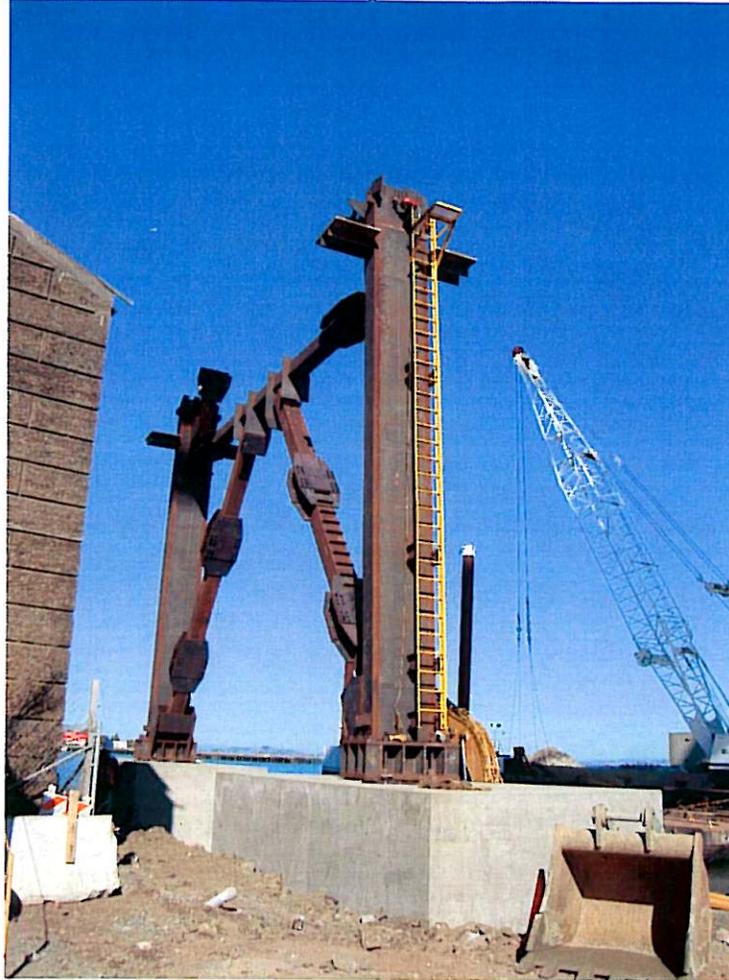

- **E Line Truss B 3+ installation continues**




**E Line Truss elevation view**



- **W2 – Pour 4 area – Curing cover removed**



**W2 – note concrete spillage in pour # 4 area**

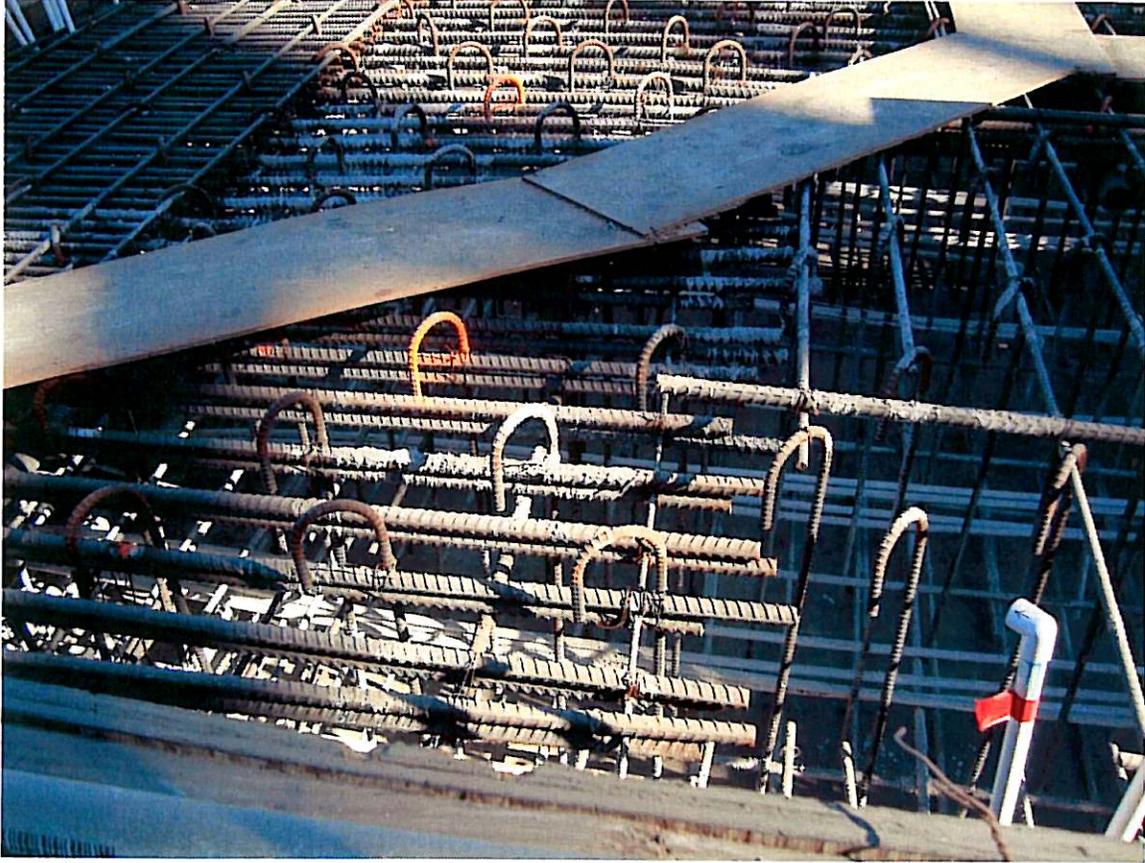

**W2 Sand blasting of pour #4 area in progress**



**Placing rebar in Pour #5 Area – West Bound Northerly portion of W2**



**Pour # 5 Rebar staging on @ W2 deck**

