



STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION
Contract 0120F – SFOBB – SAS Superstructure
Week Ending 2008-11-28

Tuesday November 15, 2008 – Observation via Engineer's Boat between 1000 and 1230;
Overcast, Cool, Calm

- E2 – West Elevation from water level

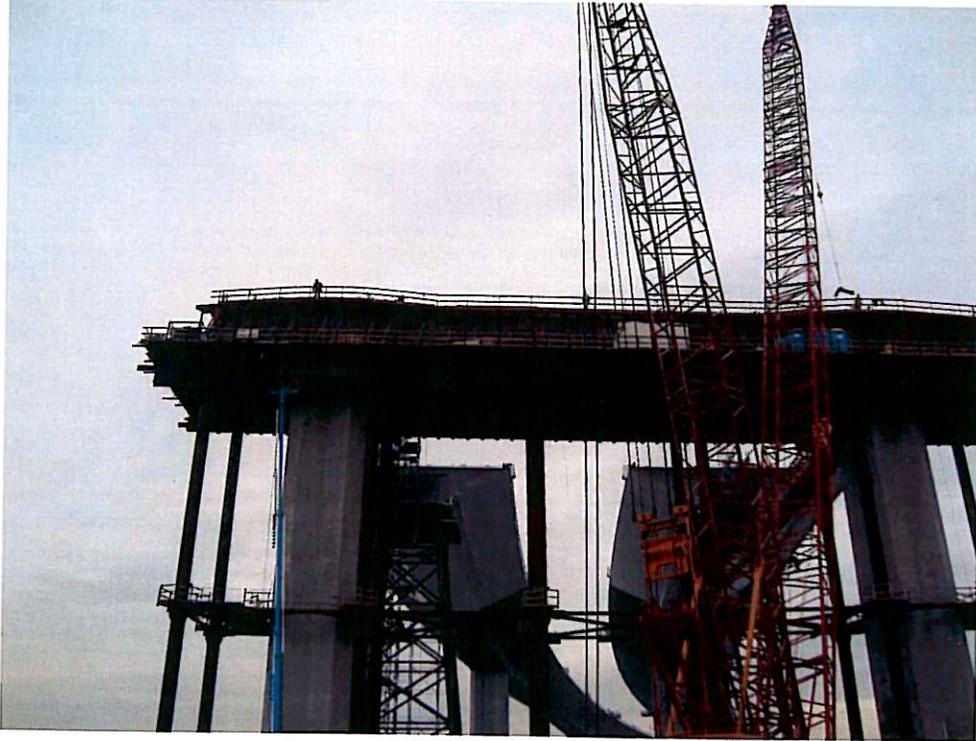


E2 – View of East Elevation from Pedestrian Bridge – Note Concrete Pumping Towers

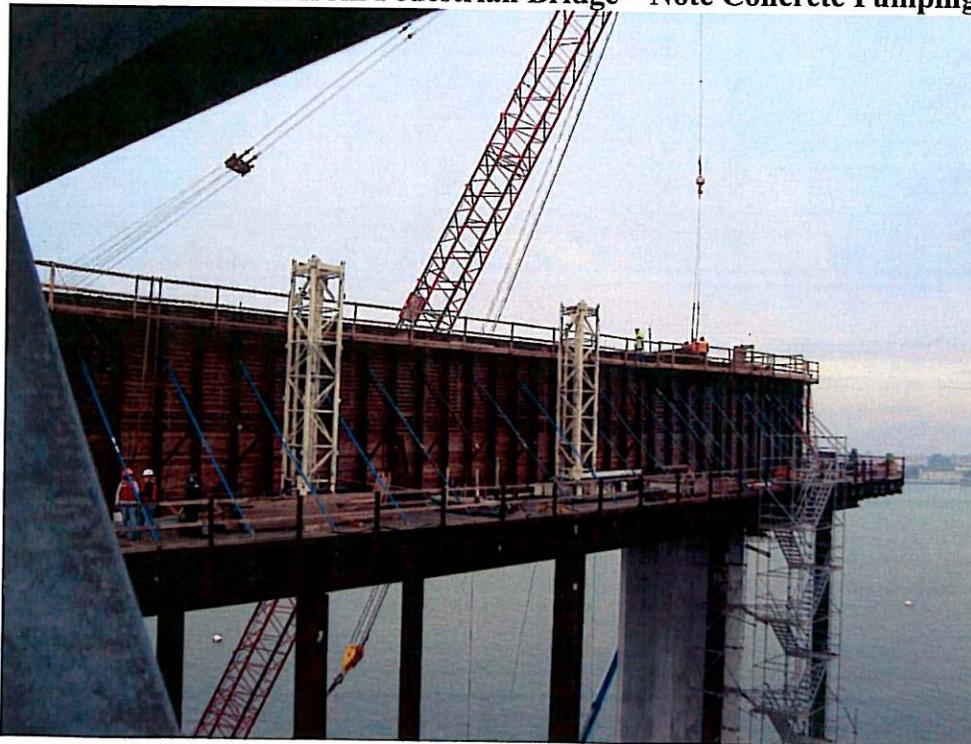

REC'D 09 JAN 12 1008352

46.02


E2 – View from Skyway – southerly portion – cooling system installation in progress

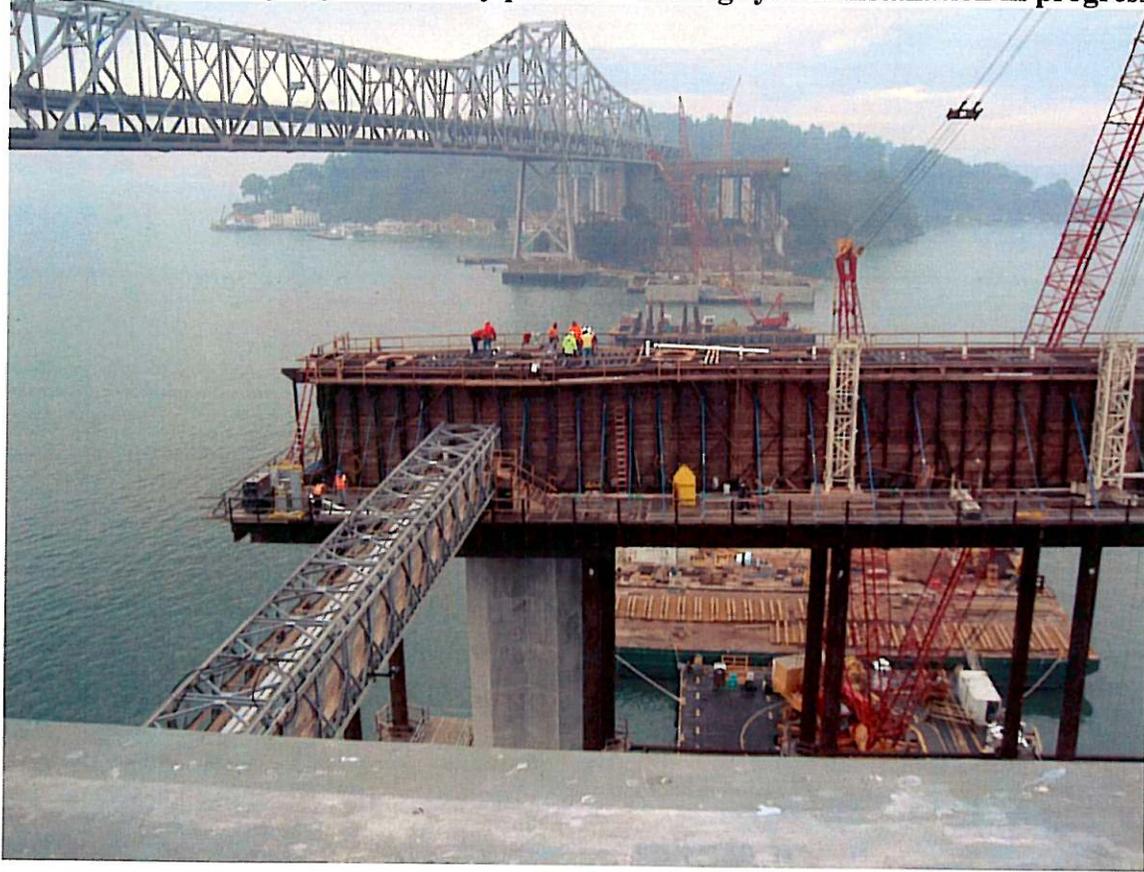


E2- View from Skyway – Northerly portion – cooling system in progress



E2 – West Elevation – Bulkhead forms complete

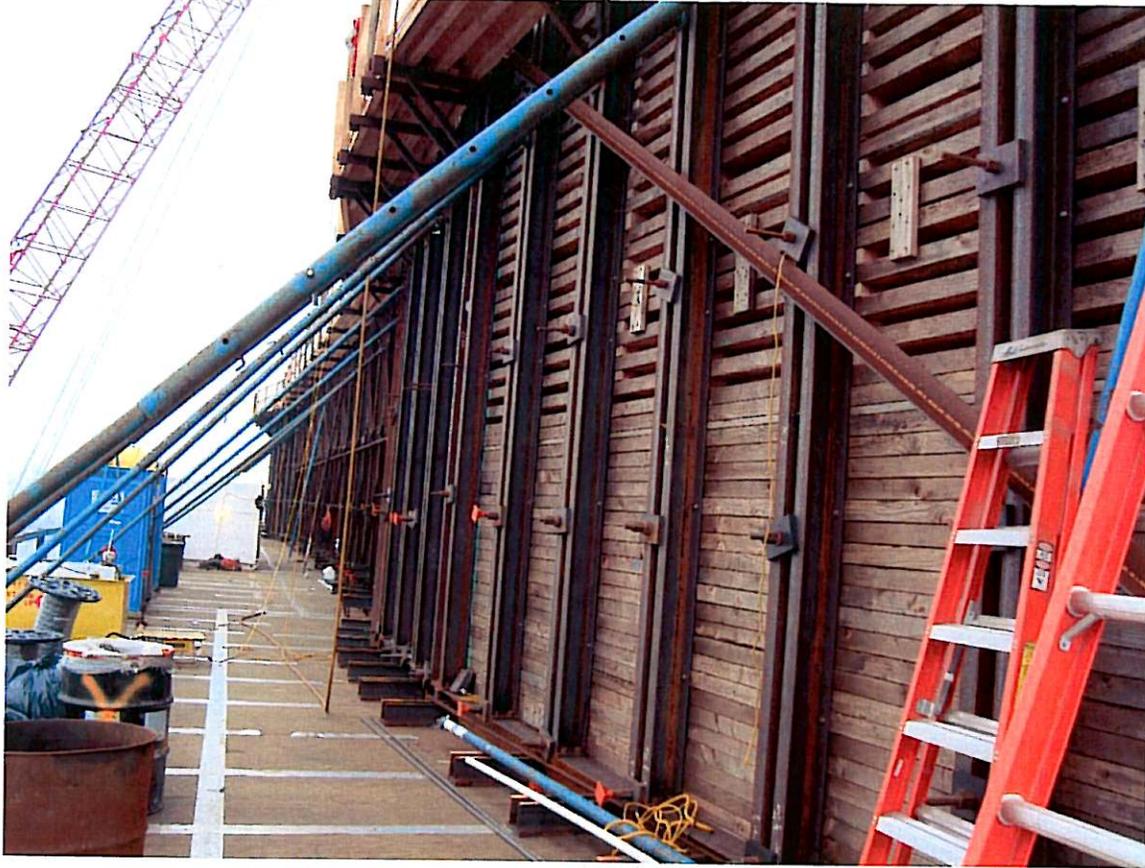

E2 – Cooling & Concrete slick pipes from Skyway down to Pedestrian Bridge

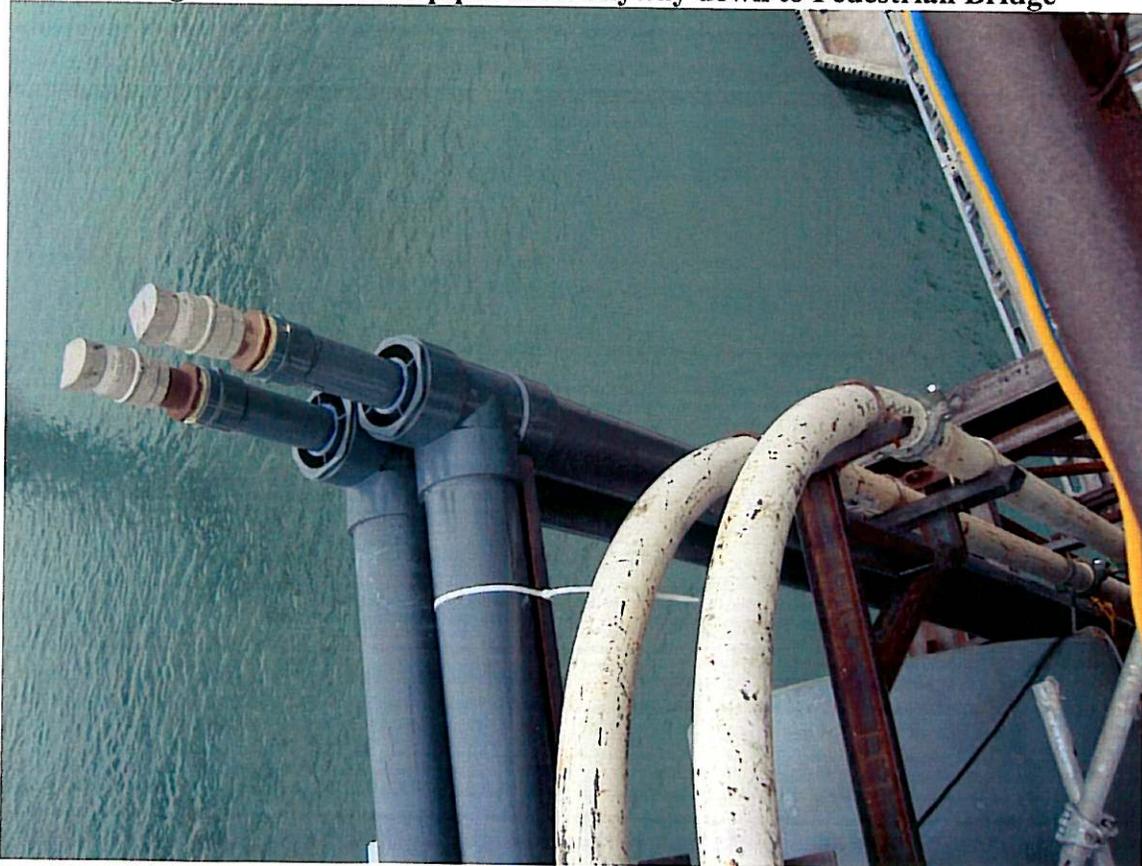

E2 – Installing cooling supply piping on Skyway



E2 – Cooling supply pipe from Pedestrian Bridge to E2 Deck



- TT “F” – West Line Driving frame being assembled at Pier 7



TT “F” West Line Driving Frame staging area at Pier 7



TT "F" East Line Driving Frame – re-tap waiting period




- **TT "D" – No observed activity**




- TT "C" East Line Tower "C" being erected



Another view of TT "C" East Line being erected

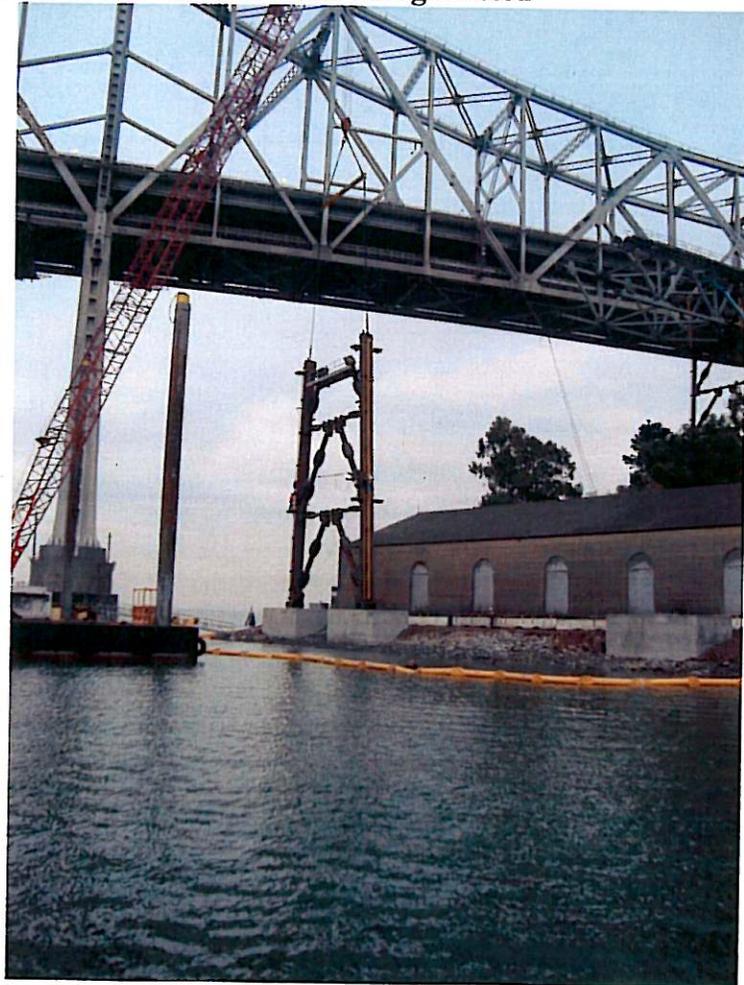

Status of TT "C" Area – Rock fill has been removed

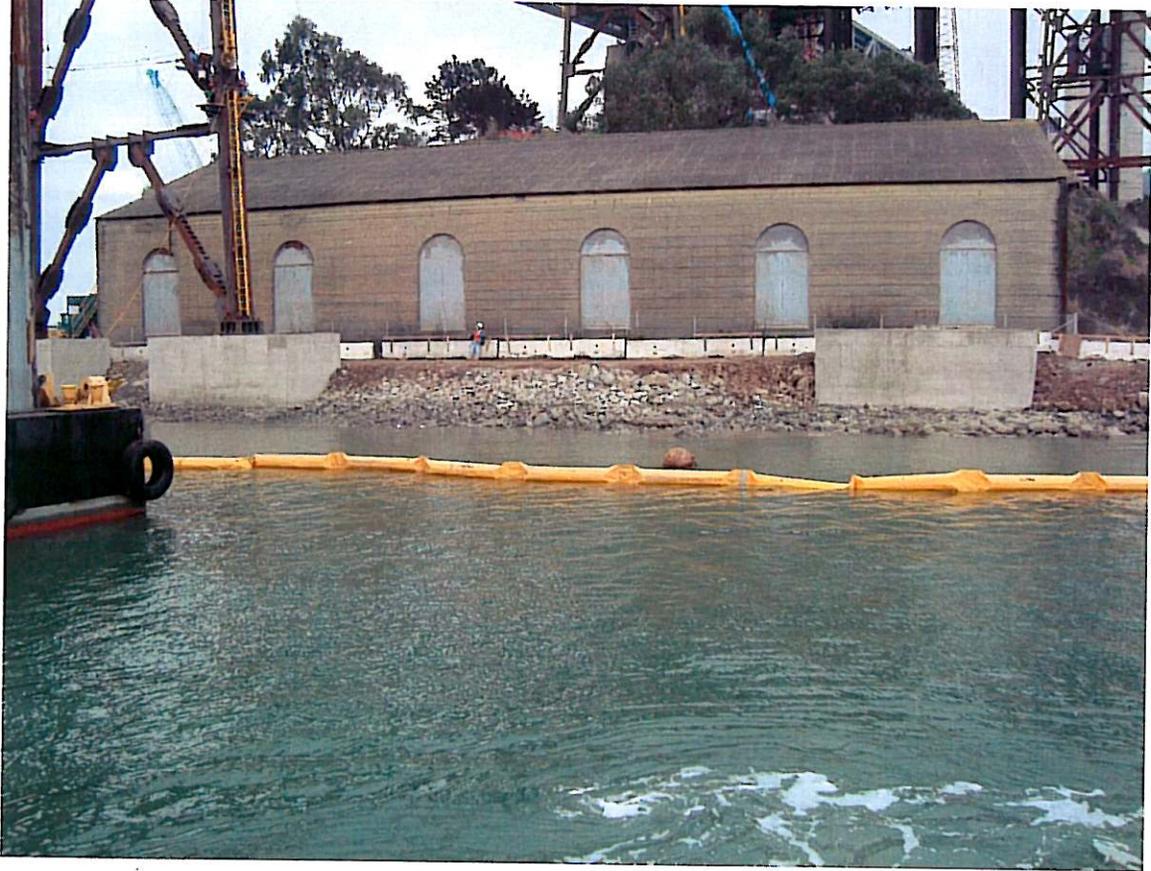

- **E Line Truss from TT "B" toward TT "C"**

