

STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION
Contract 0120F – SFOBB – Superstructure
Week Ending 2008-12-05

Tuesday December 2, 2008 – Observation via Engineer’s Boat between 1000 and 1230:
Clear, Cool, & Calm

- E2 – Southwesterly View showing pedestrian bridge to Skyway



E2 – View of East Elevation – Note Concrete Pumping Towers with booms in place – Pour scheduled for Friday Night / Saturday Morning



RECT*09 JAN-12 #008353

E2 – Cooling Water manifold at North End



E2 – Water Cooling system mains on Northern portion of E2 Deck



Top of E2 – Southerly portion - (TT “D” in background – no observed activity)



Top of E2 – Northerly portion




E2 – Cooling system on Skyway - @ down turn to pedestrian bridge




E2 – Cooling Water from Baker tank on Skyway



E2- Cooling Water mains on South Deck of E2

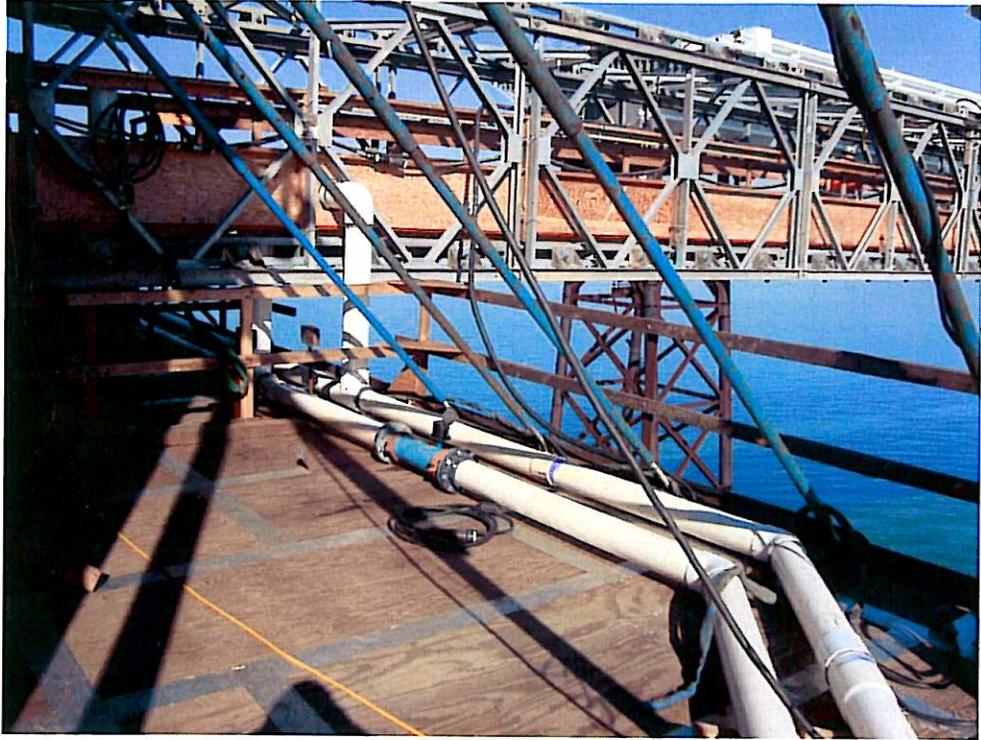

E2 – South Elevation – showing cooling system piping system

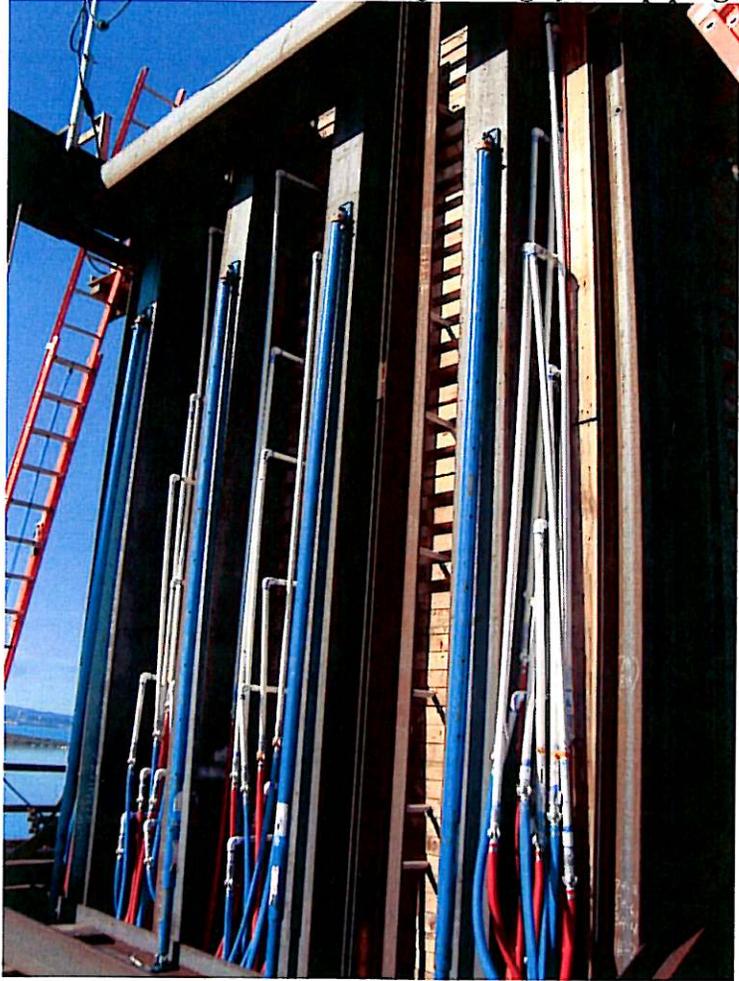

• **TT "F" W-Line – Driving Frame @ Pier 7**



TT "F" E-Line Driving Frame – Re-tap of piles completed this morning



- **TT “C” E-Line Temporary Tower on water side of Torpedo Building**



Snoopy “flying high” on this Blue Sky Day



Thursday December 4, 2008 – Observation from Yerba Buena Island between 1200 and 1330: Clear, Cool, Slight Breeze

- **E2 View from W2 – Prepping for Concrete Placement on Friday night 12-05-2008 and Saturday morning .**



- **TT "D" (Between Temp Tower "C" E-line & TT "F" E-Line driving frame) – No observed activity**



- **View of TT “F” E-Line Driving Frame – Pile Frame welding in process**




- **Area “C” – Temporary Tower “C” E-Line**



Temporary Truss E-Line from TT "B" toward TT "C"



Restored C Area shoreline – looking toward Northerly (W-Line) foundations

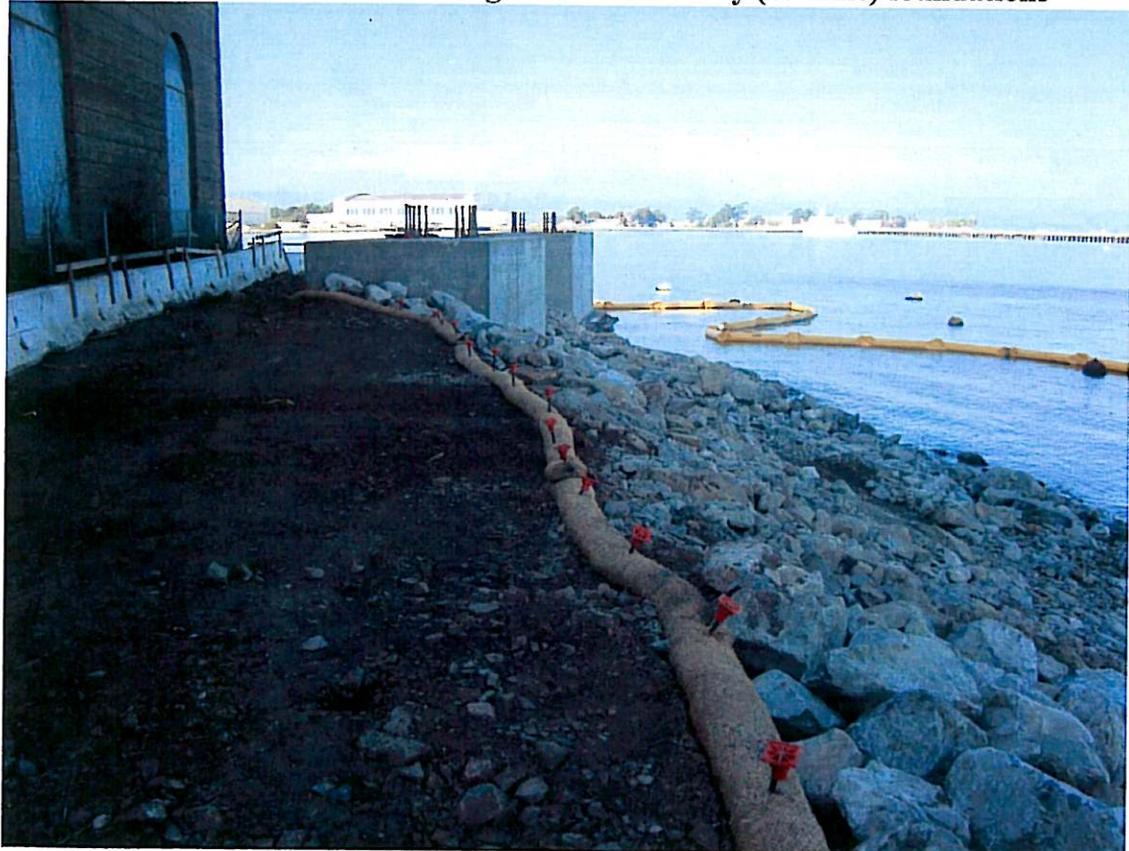

- **W2 – installing rebar for Pour 5 (Northerly portion – West Bound)**



W2 – Pour 5 rebar continued



W2 – More Pour 5 area rebar



W2 – Pour 5 Area close-up



W2 – Pour 4 Area subsequent to sandblasting



Today's "High Flyer" – the zeppelin "Airship Ventures"



